

Prilog - drugi slučaj

Butorac, Lovro

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:429499>

Rights / Prava: [In copyright](#)/[Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-07-11**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)




ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23				Aug '23				Sep '23			Oct '23						
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	
1	OPREMANJE 2. PLATFORME STROJARNICE	62 days	Thu 6.7.23	Fri 29.9.23		\$296.896,00	4.588 hrs		OPREMANJE 2. PLATFORME STROJARNICE																	
2	Montaža temelja	13,88 days	Thu 6.7.23	Tue 25.7.23		\$17.760,00	444 hrs		Montaža temelja																	
3	Montaža temelja 445-003	0,38 days	Thu 6.7.23	Thu 6.7.23		\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 445-003	B																
4	Montaža temelja 445-004	0,38 days	Thu 6.7.23	Thu 6.7.23	3	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 445-004	F B																
5	Montaža temelja 452-001	0,38 days	Thu 6.7.23	Fri 7.7.23	4	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 452-001	G B																
6	Montaža temelja 452-005	0,38 days	Fri 7.7.23	Fri 7.7.23	5	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 452-005	F B																
7	Montaža temelja 581-001	0,38 days	Fri 7.7.23	Fri 7.7.23	6	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-001	F B																
8	Montaža temelja 581-002	0,38 days	Fri 7.7.23	Mon 10.7.23	7	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-002	F B																
9	Montaža temelja 581-003	0,38 days	Mon 10.7.23	Mon 10.7.23	8	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-003	F B																
10	Montaža temelja 582-001	0,38 days	Mon 10.7.23	Mon 10.7.23	9	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-001	F B																
11	Montaža temelja 582-003/01	0,38 days	Tue 11.7.23	Tue 11.7.23	10	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-003/01	F B																
12	Montaža temelja 582-003/02	0,38 days	Tue 11.7.23	Tue 11.7.23	11	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-003/02	F B																
13	Montaža temelja 644-008/01	0,38 days	Tue 11.7.23	Wed 12.7.23	12	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 644-008/01	F B																
14	Montaža temelja 644-008/02	0,38 days	Wed 12.7.23	Wed 12.7.23	13	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 644-008/02	F B																
15	Montaža temelja 651-001	0,38 days	Wed 12.7.23	Wed 12.7.23	14	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-001	F B																
16	Montaža temelja 651-002	0,38 days	Wed 12.7.23	Thu 13.7.23	15	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-002	G B																
17	Montaža temelja 651-003	0,38 days	Thu 13.7.23	Thu 13.7.23	16	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-003	F B																
18	Montaža temelja 702-001	0,38 days	Thu 13.7.23	Thu 13.7.23	17	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-001	F B																
19	Montaža temelja 702-004	0,38 days	Fri 14.7.23	Fri 14.7.23	18	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-004	F B																
20	Montaža temelja 702-005	0,38 days	Fri 14.7.23	Fri 14.7.23	19	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-005	F B																
21	Montaža temelja 703-001	0,38 days	Fri 14.7.23	Mon 17.7.23	20	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 703-001	F B																
22	Montaža temelja 703-002	0,38 days	Mon 17.7.23	Mon 17.7.23	21	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 703-002	F B																
23	Montaža temelja 712-001	0,38 days	Mon 17.7.23	Mon 17.7.23	22	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 712-001	F B																
24	Montaža temelja 713-007	0,38 days	Mon 17.7.23	Tue 18.7.23	23	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 713-007	G B																
25	Montaža temelja 714-001	0,38 days	Tue 18.7.23	Tue 18.7.23	24	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 714-001	F B																
26	Montaža temelja 756-001/02	0,38 days	Tue 18.7.23	Tue 18.7.23	25	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 756-001/02	F B																
27	Montaža temelja 722-011	0,38 days	Wed 19.7.23	Wed 19.7.23	26	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 722-011	F B																
28	Montaža temelja 731-001/01	0,38 days	Wed 19.7.23	Wed 19.7.23	27	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-001/01	F B																
29	Montaža temelja 731-001/02	0,38 days	Wed 19.7.23	Thu 20.7.23	28	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-001/02	G B																
30	Montaža temelja 731-002	0,38 days	Thu 20.7.23	Thu 20.7.23	29	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-002	F B																
31	Montaža temelja 731-003/01	0,38 days	Thu 20.7.23	Thu 20.7.23	30	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-003/01	F B																

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23					Aug '23					Sep '23			Oct '23				
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	
32	Montaža temelja 731-003/01	0,38 days	Thu 20.7.23	Fri 21.7.23	31	\$480,00	12 hrs	Bravari (4)[400%]																		
33	Montaža temelja 733-001	0,38 days	Fri 21.7.23	Fri 21.7.23	32	\$480,00	12 hrs	Bravari (4)[400%]																		
34	Montaža temelja 733-012	0,38 days	Fri 21.7.23	Fri 21.7.23	33	\$480,00	12 hrs	Bravari (4)[400%]																		
35	Montaža temelja 734-001	0,38 days	Mon 24.7.23	Mon 24.7.23	34	\$480,00	12 hrs	Bravari (4)[400%]																		
36	Montaža temelja 743-002	0,38 days	Mon 24.7.23	Mon 24.7.23	35	\$480,00	12 hrs	Bravari (4)[400%]																		
37	Montaža temelja 743-003	0,38 days	Mon 24.7.23	Tue 25.7.23	36	\$480,00	12 hrs	Bravari (4)[400%]																		
38	Montaža temelja 751-001	0,38 days	Tue 25.7.23	Tue 25.7.23	37	\$480,00	12 hrs	Bravari (4)[400%]																		
39	Montaža temelja 756-004	0,38 days	Tue 25.7.23	Tue 25.7.23	38	\$480,00	12 hrs	Bravari (4)[400%]																		
40	Montaža strojeva I uređaja	9,25 days	Wed 12.7.23	Wed 26.7.23	2FS-9 days	\$14.208,00	296 hrs																			
41	Montaža 445-003	0,25 days	Wed 12.7.23	Thu 13.7.23		\$384,00	8 hrs	Mehaničari (4)[400%]																		
42	Montaža 445-004	0,25 days	Thu 13.7.23	Thu 13.7.23	41	\$384,00	8 hrs	Mehaničari (4)[400%]																		
43	Montaža 452-001	0,25 days	Thu 13.7.23	Thu 13.7.23	42	\$384,00	8 hrs	Mehaničari (4)[400%]																		
44	Montaža 452-005	0,25 days	Thu 13.7.23	Thu 13.7.23	43	\$384,00	8 hrs	Mehaničari (4)[400%]																		
45	Montaža 581-001	0,25 days	Thu 13.7.23	Fri 14.7.23	44	\$384,00	8 hrs	Mehaničari (4)[400%]																		
46	Montaža 581-002	0,25 days	Fri 14.7.23	Fri 14.7.23	45	\$384,00	8 hrs	Mehaničari (4)[400%]																		
47	Montaža 581-003	0,25 days	Fri 14.7.23	Fri 14.7.23	46	\$384,00	8 hrs	Mehaničari (4)[400%]																		
48	Montaža 582-001	0,25 days	Fri 14.7.23	Fri 14.7.23	47	\$384,00	8 hrs	Mehaničari (4)[400%]																		
49	Montaža 582-003/01	0,25 days	Fri 14.7.23	Mon 17.7.23	48	\$384,00	8 hrs	Mehaničari (4)[400%]																		
50	Montaža 582-003/02	0,25 days	Mon 17.7.23	Mon 17.7.23	49	\$384,00	8 hrs	Mehaničari (4)[400%]																		
51	Montaža 644-008/01	0,25 days	Mon 17.7.23	Mon 17.7.23	50	\$384,00	8 hrs	Mehaničari (4)[400%]																		
52	Montaža 644-008/02	0,25 days	Mon 17.7.23	Mon 17.7.23	51	\$384,00	8 hrs	Mehaničari (4)[400%]																		
53	Montaža 651-001	0,25 days	Mon 17.7.23	Tue 18.7.23	52	\$384,00	8 hrs	Mehaničari (4)[400%]																		
54	Montaža 651-002	0,25 days	Tue 18.7.23	Tue 18.7.23	53	\$384,00	8 hrs	Mehaničari (4)[400%]																		
55	Montaža 651-003	0,25 days	Tue 18.7.23	Tue 18.7.23	54	\$384,00	8 hrs	Mehaničari (4)[400%]																		
56	Montaža 702-001	0,25 days	Tue 18.7.23	Tue 18.7.23	55	\$384,00	8 hrs	Mehaničari (4)[400%]																		
57	Montaža 702-004	0,25 days	Tue 18.7.23	Wed 19.7.23	56	\$384,00	8 hrs	Mehaničari (4)[400%]																		
58	Montaža 702-005	0,25 days	Wed 19.7.23	Wed 19.7.23	57	\$384,00	8 hrs	Mehaničari (4)[400%]																		
59	Montaža 703-001	0,25 days	Wed 19.7.23	Wed 19.7.23	58	\$384,00	8 hrs	Mehaničari (4)[400%]																		
60	Montaža 703-002	0,25 days	Wed 19.7.23	Wed 19.7.23	59	\$384,00	8 hrs	Mehaničari (4)[400%]																		
61	Montaža 712-001	0,25 days	Wed 19.7.23	Thu 20.7.23	60	\$384,00	8 hrs	Mehaničari (4)[400%]																		
62	Montaža 713-007	0,25 days	Thu 20.7.23	Thu 20.7.23	61	\$384,00	8 hrs	Mehaničari (4)[400%]																		

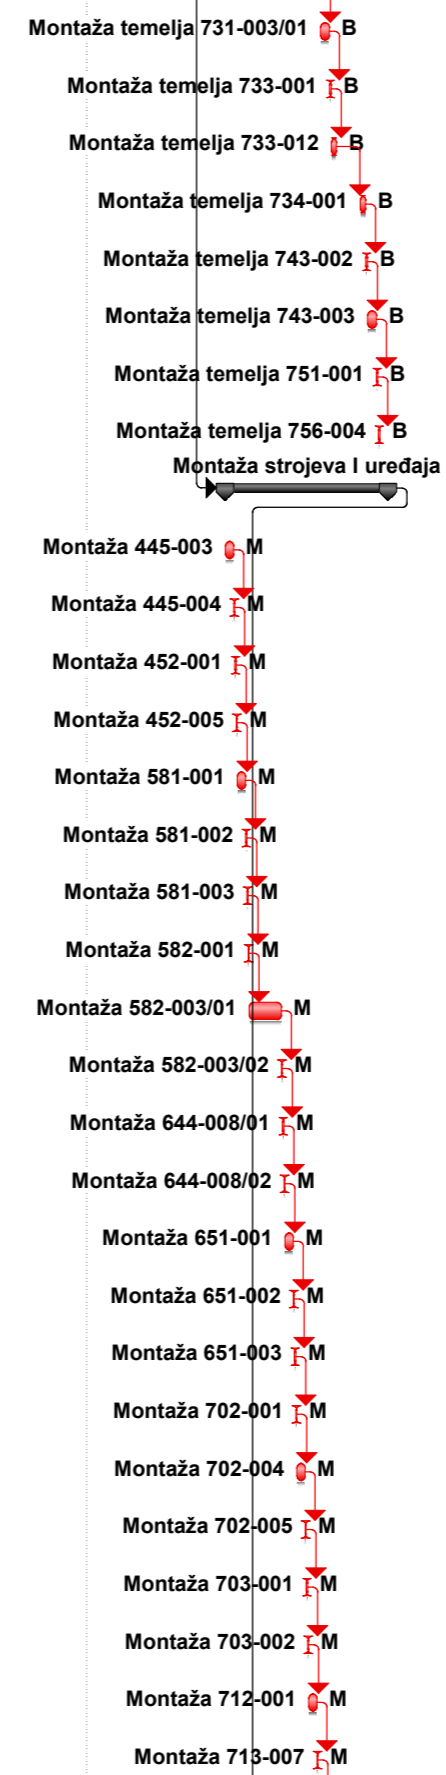


Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical **Split** **Slack** **Project Summary** **External Tasks**

Critical Split **Progress** **Slippage** **Rolled Up Critical** **External Milestone**

Task **Milestone** **Summary** **Rolled Up Critical** **Deadline**


ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23				Aug '23				Sep '23				Oct '23		
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17
63	Montaža 714-001	0,25 days	Thu 20.7.23	Thu 20.7.23	62	\$384,00	8 hrs	Mehaničari (4)[400%]															
64	Montaža 756-001/02	0,25 days	Thu 20.7.23	Thu 20.7.23	63	\$384,00	8 hrs	Mehaničari (4)[400%]															
65	Montaža 722-011	0,25 days	Thu 20.7.23	Fri 21.7.23	64	\$384,00	8 hrs	Mehaničari (4)[400%]															
66	Montaža 731-001/01	0,25 days	Fri 21.7.23	Fri 21.7.23	65	\$384,00	8 hrs	Mehaničari (4)[400%]															
67	Montaža 731-001/02	0,25 days	Fri 21.7.23	Fri 21.7.23	66	\$384,00	8 hrs	Mehaničari (4)[400%]															
68	Montaža 731-002	0,25 days	Fri 21.7.23	Fri 21.7.23	67	\$384,00	8 hrs	Mehaničari (4)[400%]															
69	Montaža 731-003/01	0,25 days	Fri 21.7.23	Mon 24.7.23	68	\$384,00	8 hrs	Mehaničari (4)[400%]															
70	Montaža 731-003/01	0,25 days	Mon 24.7.23	Mon 24.7.23	69	\$384,00	8 hrs	Mehaničari (4)[400%]															
71	Montaža 733-001	0,25 days	Mon 24.7.23	Mon 24.7.23	70	\$384,00	8 hrs	Mehaničari (4)[400%]															
72	Montaža 733-012	0,25 days	Mon 24.7.23	Mon 24.7.23	71	\$384,00	8 hrs	Mehaničari (4)[400%]															
73	Montaža 734-001	0,25 days	Mon 24.7.23	Tue 25.7.23	72	\$384,00	8 hrs	Mehaničari (4)[400%]															
74	Montaža 743-002	0,25 days	Tue 25.7.23	Tue 25.7.23	73	\$384,00	8 hrs	Mehaničari (4)[400%]															
75	Montaža 743-003	0,25 days	Tue 25.7.23	Tue 25.7.23	74	\$384,00	8 hrs	Mehaničari (4)[400%]															
76	Montaža 751-001	0,25 days	Tue 25.7.23	Tue 25.7.23	75	\$384,00	8 hrs	Mehaničari (4)[400%]															
77	Montaža 756-004	0,25 days	Tue 25.7.23	Wed 26.7.23	76	\$384,00	8 hrs	Mehaničari (4)[400%]															
78	Cjevarski radovi	13,88 days	Mon 17.7.23	Thu 3.8.23	40FS-7 days	\$78.144,00	888 hrs																
79	Montaža prolaza	2,63 days	Mon 17.7.23	Wed 19.7.23		\$14.784,00	168 hrs	Cjevvari (8)[800%]															
80	Montaža nosača	3,75 days	Wed 19.7.23	Tue 25.7.23	79	\$21.120,00	240 hrs	Cjevvari (8)[800%]															
81	Montaža cijevi	7,5 days	Tue 25.7.23	Thu 3.8.23	80	\$42.240,00	480 hrs	Cjevvari (8)[800%]															
82	Bravarski radovi	13,25 days	Wed 26.7.23	Mon 14.8.23	78FS-7 days	\$16.960,00	424 hrs																
83	Montaža podnica	5,25 days	Wed 26.7.23	Wed 2.8.23		\$6.720,00	168 hrs	Bravari (4)[400%]															
84	Montaža ljestvi	4,5 days	Wed 2.8.23	Tue 8.8.23	83	\$5.760,00	144 hrs	Bravari (4)[400%]															
85	Montaža skala	3,5 days	Tue 8.8.23	Mon 14.8.23	84	\$4.480,00	112 hrs	Bravari (4)[400%]															
86	Električarski radovi	17,63 days	Fri 21.7.23	Wed 16.8.23	80FS-2 days	\$108.288,00	1.128 hrs																
87	Montaža kablskih prolaza	2,63 days	Fri 21.7.23	Wed 26.7.23		\$16.128,00	168 hrs	Električari (8)[800%]															
88	Montaža kablskih staza	5,63 days	Wed 26.7.23	Wed 2.8.23	87	\$34.560,00	360 hrs	Električari (8)[800%]															
89	Provlačenje kabela	9,38 days	Wed 2.8.23	Wed 16.8.23	88	\$57.600,00	600 hrs	Električari (8)[800%]															
90	Limarski radovi	16,25 days	Fri 1.9.23	Mon 25.9.23	78FS+20 days	\$16.320,00	408 hrs																
91	Montaža ventilacijskih prolaza	3,5 days	Fri 1.9.23	Wed 6.9.23		\$4.480,00	112 hrs	Limari (4)[400%]															
92	Montaža ventilacijskih kanala	7,5 days	Tue 12.9.23	Thu 21.9.23	91SS+7 days	\$9.600,00	240 hrs	Limari (4)[400%]															
93	Montaža zaštite strojeva I uređaja	1,75 days	Thu 21.9.23	Mon 25.9.23	92	\$2.240,00	56 hrs	Limari (4)[400%]															

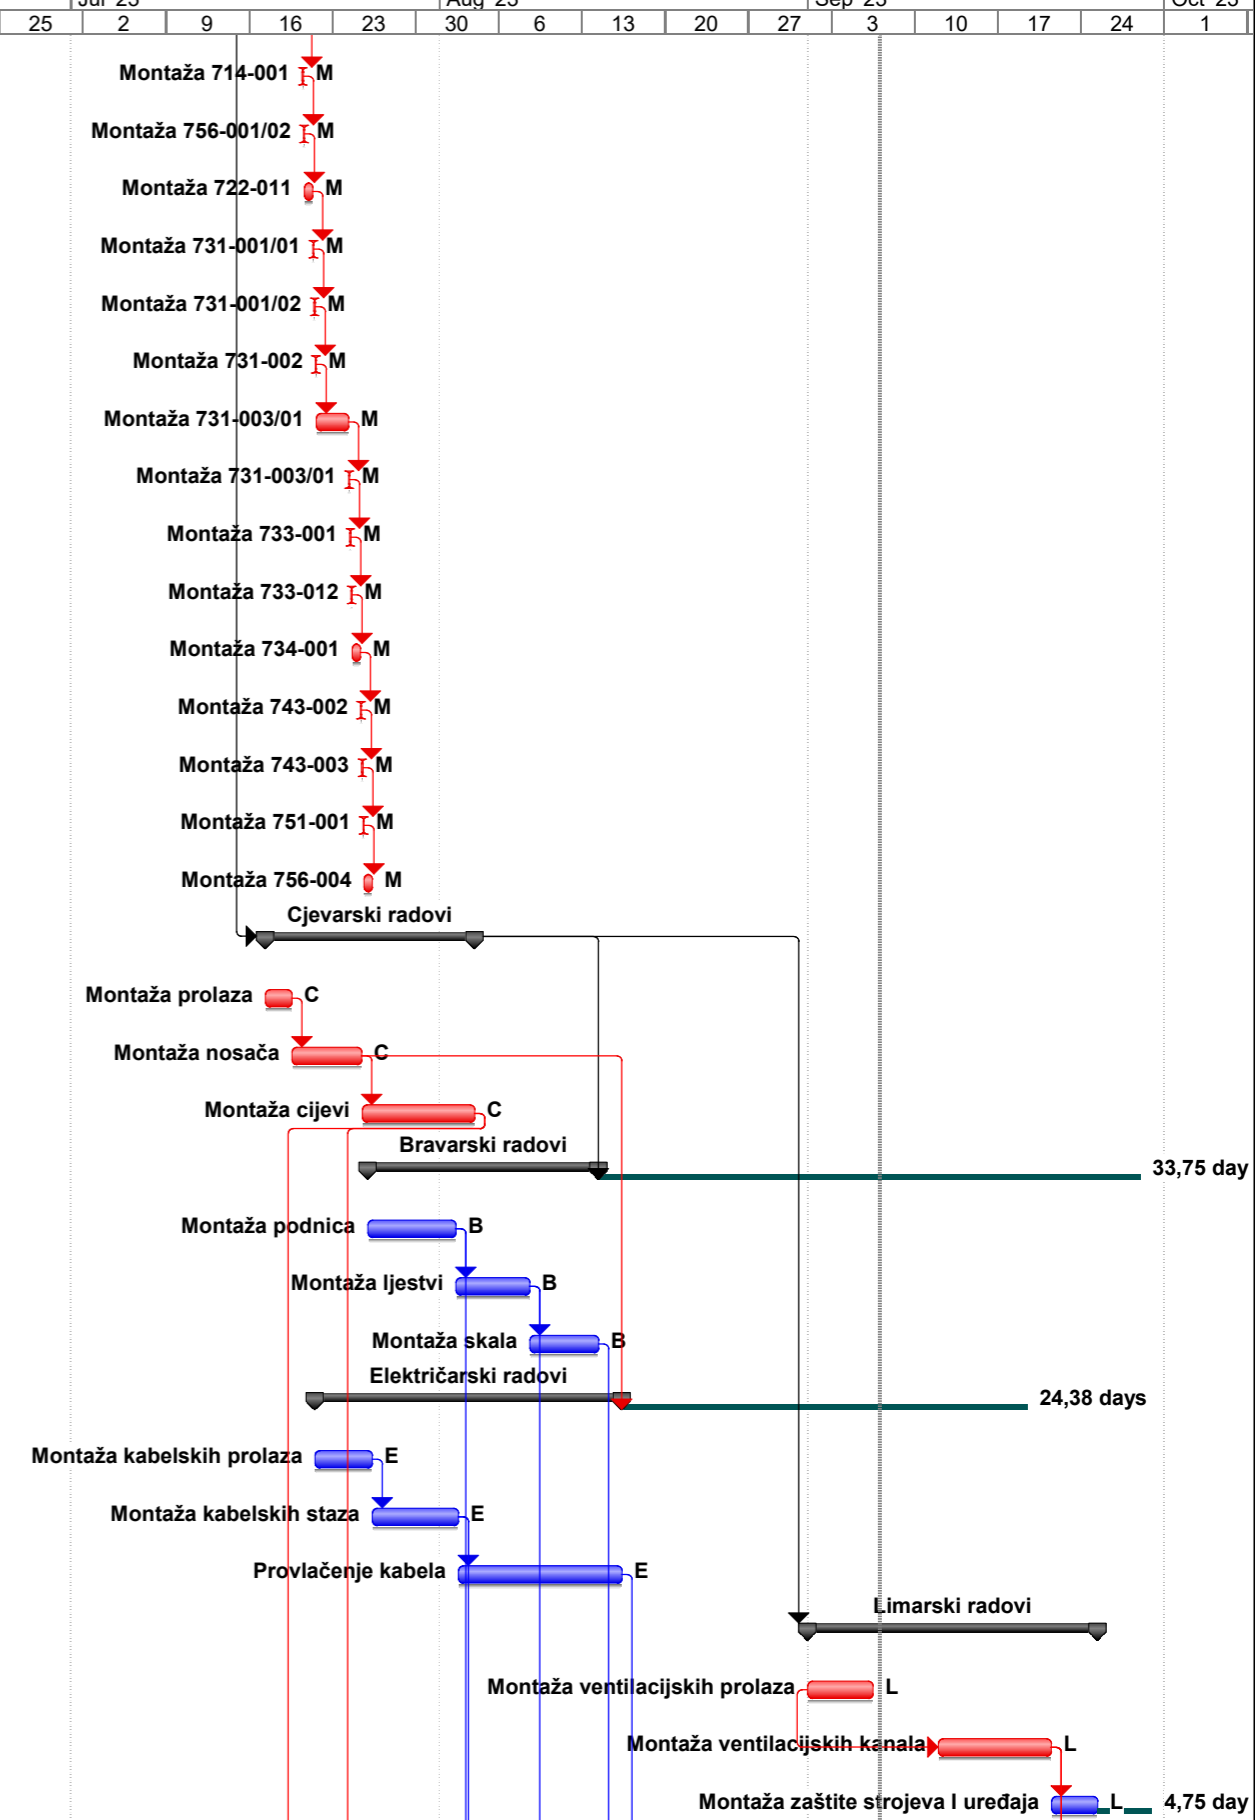

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical (Red bar) **Split** (Dashed line) **Slack** (Blue bar) **Project Summary** (Grey arrow) **External Tasks** (Grey bar)
Critical Split (Red dashed bar) **Progress** (Black bar) **Slippage** (Black bar) **Rolled Up Critical** (Green bar) **External Milestone** (Diamond)
Task (Blue bar) **Milestone** (Diamond) **Summary** (Grey arrow) **Rolled Up Critical** (Red bar) **Deadline** (Green arrow)

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23			Aug '23			Sep '23			Oct '23		
									11	18	25	2	9	16	23	30	6	13	20	27
94	Izolaterski radovi	5 days	Thu 21.9.23	Thu 28.9.23	92	\$14.400,00	240 hrs													
95	Montaža izolacije	5 days	Thu 21.9.23	Thu 28.9.23		\$14.400,00	240 hrs	Izolateri (6)[600%]												
96	Ispitivanje	51 days	Fri 21.7.23	Fri 29.9.23		\$30.816,00	760 hrs													
97	Ispitivanje rada strojeva I uređaja	1,5 days	Wed 26.7.23	Thu 27.7.23	81FS-7 days	\$576,00	24 hrs	Ispitivači/Mehaničari (2)[200%]												
98	Ispitivanje cjevovoda	8,25 days	Fri 21.7.23	Wed 2.8.23		\$11.616,00	264 hrs													
99	Pregled strukture cjevovoda	3,5 days	Fri 21.7.23	Wed 26.7.23	81FS-10 days	\$4.928,00	112 hrs	Ispitivači/cjevvari (4)[400%]												
100	Tlačenje cjevovoda	3 days	Wed 26.7.23	Mon 31.7.23	99	\$4.224,00	96 hrs	Ispitivači/cjevvari (4)[400%]												
101	Pregled funkcionalnosti cjevovoda	1,75 days	Mon 31.7.23	Wed 2.8.23	100	\$2.464,00	56 hrs	Ispitivači/cjevvari (4)[400%]												
102	Pregled bravarskih radova	9 days	Wed 2.8.23	Tue 15.8.23		\$1.280,00	64 hrs													
103	Pregled strukture podnica	2 days	Wed 2.8.23	Fri 4.8.23	83	\$640,00	32 hrs	Kontrolori/Bravari (2)[200%]												
104	Pregled strukture ljestvi	1 day	Tue 8.8.23	Wed 9.8.23	84	\$320,00	16 hrs	Kontrolori/Bravari (2)[200%]												
105	Pregled strukture skala	1 day	Mon 14.8.23	Tue 15.8.23	85	\$320,00	16 hrs	Kontrolori/Bravari (2)[200%]												
106	Ispitivanje električarskih radova	17,88 days	Wed 2.8.23	Mon 28.8.23		\$15.744,00	328 hrs													
107	Pregled strukture kablskih staza	1,75 days	Wed 2.8.23	Fri 4.8.23	88	\$2.688,00	56 hrs	Ispitivači/Električari (4)[400%]												
108	Pregled montaže kabela	2,5 days	Wed 16.8.23	Fri 18.8.23	89	\$3.840,00	80 hrs	Ispitivači/Električari (4)[400%]												
109	Ispitivanje ožičenja kabela	3,5 days	Fri 18.8.23	Thu 24.8.23	108	\$5.376,00	112 hrs	Ispitivači/Električari (4)[400%]												
110	Test ispitivanja pod naponom	2,5 days	Thu 24.8.23	Mon 28.8.23	109	\$3.840,00	80 hrs	Ispitivači/Električari (4)[400%]												
111	Ispitivanje limarskih radova	3,5 days	Thu 21.9.23	Tue 26.9.23		\$1.120,00	56 hrs													
112	Pregled strukture ventilacije	1 day	Thu 21.9.23	Fri 22.9.23	92	\$320,00	16 hrs	Kontrolori/Limari (2)[200%]												
113	Pregled funkcionalnosti ventilacije	2 days	Fri 22.9.23	Tue 26.9.23	112	\$640,00	32 hrs	Kontrolori/Limari (2)[200%]												
114	Pregled strukture zaštite strojeva	0,5 days	Tue 26.9.23	Tue 26.9.23	113	\$160,00	8 hrs	Kontrolori/Limari (2)[200%]												
115	Ispitivanje izolaterskih radova	1,5 days	Thu 28.9.23	Fri 29.9.23		\$480,00	24 hrs													
116	Pregled montaže izolacije	1,5 days	Thu 28.9.23	Fri 29.9.23	95	\$480,00	24 hrs	Kontrolori/Izolateri (2)[200%]												

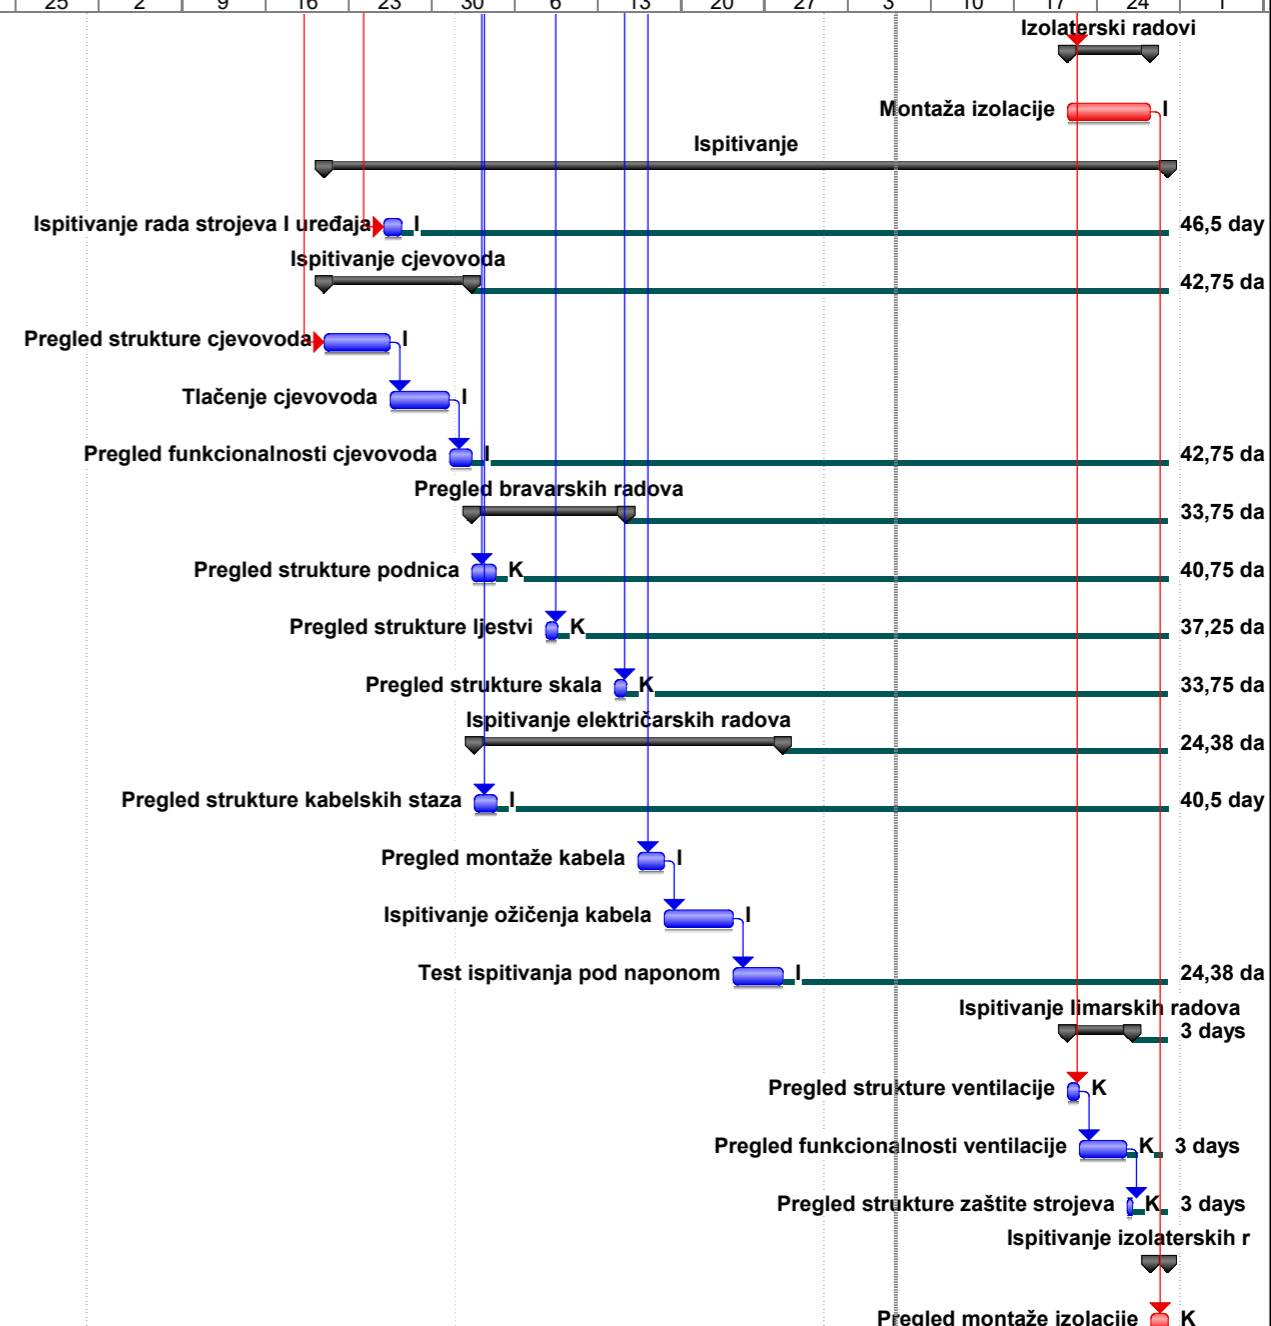

Project: OPREMANJE 2 PLATFORME Date: Thu 7.9.23	Critical		Split		Slack		Project Summary		External Tasks	
	Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
	Task		Milestone		Summary		Rolled Up Critical		Deadline	
