

# Prilog - četvrti slučaj

---

**Butorac, Lovro**

**Supplement / Prilog**

*Publication year / Godina izdavanja:* **2023**

*Permanent link / Trajna poveznica:* <https://urn.nsk.hr/urn:nbn:hr:190:922545>

*Rights / Prava:* [In copyright](#)/[Zaštićeno autorskim pravom.](#)

*Download date / Datum preuzimanja:* **2024-11-30**



*Repository / Repozitorij:*

[Repository of the University of Rijeka, Faculty of Engineering](#)




ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23				Aug '23				Sep '23				Oct '23							
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22
1	<b>OPREMANJE 2. PLATFORME STROJARNICE</b>	<b>71 days</b>	<b>Thu 6.7.23</b>	<b>Thu 12.10.23</b>		<b>\$148.448,00</b>	<b>4.588 hrs</b>		<b>OPREMANJE 2. PLATFORME STROJARNICE</b>																			
2	<b>Montaža temelja</b>	<b>14,25 days</b>	<b>Thu 6.7.23</b>	<b>Wed 26.7.23</b>		<b>\$8.880,00</b>	<b>444 hrs</b>		<b>Montaža temelja</b>																			
3	Montaža temelja 445-003	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 445-003 B1																			
4	Montaža temelja 445-004	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 445-004 B2																			
5	Montaža temelja 452-001	0,75 days	Thu 6.7.23	Fri 7.7.23	3	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 452-001 B1																			
6	Montaža temelja 452-005	0,75 days	Thu 6.7.23	Fri 7.7.23	4	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 452-005 B2																			
7	Montaža temelja 581-001	0,75 days	Fri 7.7.23	Mon 10.7.23	5	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 581-001 B1																			
8	Montaža temelja 581-002	0,75 days	Fri 7.7.23	Mon 10.7.23	6	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 581-002 B2																			
9	Montaža temelja 581-003	0,75 days	Mon 10.7.23	Mon 10.7.23	7	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 581-003 B1																			
10	Montaža temelja 582-001	0,75 days	Mon 10.7.23	Mon 10.7.23	8	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 582-001 B2																			
11	Montaža temelja 582-003/01	0,75 days	Tue 11.7.23	Tue 11.7.23	9	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 582-003/01 B1																			
12	Montaža temelja 582-003/02	0,75 days	Tue 11.7.23	Tue 11.7.23	10	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 582-003/02 B2																			
13	Montaža temelja 644-008/01	0,75 days	Tue 11.7.23	Wed 12.7.23	11	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 644-008/01 B1																			
14	Montaža temelja 644-008/02	0,75 days	Tue 11.7.23	Wed 12.7.23	12	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 644-008/02 B2																			
15	Montaža temelja 651-001	0,75 days	Wed 12.7.23	Thu 13.7.23	13	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 651-001 B1																			
16	Montaža temelja 651-002	0,75 days	Wed 12.7.23	Thu 13.7.23	14	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 651-002 B2																			
17	Montaža temelja 651-003	0,75 days	Thu 13.7.23	Thu 13.7.23	15	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 651-003 B1																			
18	Montaža temelja 702-001	0,75 days	Thu 13.7.23	Thu 13.7.23	16	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 702-001 B2																			
19	Montaža temelja 702-004	0,75 days	Fri 14.7.23	Fri 14.7.23	17	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 702-004 B1																			
20	Montaža temelja 702-005	0,75 days	Fri 14.7.23	Fri 14.7.23	18	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 702-005 B2																			
21	Montaža temelja 703-001	0,75 days	Fri 14.7.23	Mon 17.7.23	19	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 703-001 B1																			
22	Montaža temelja 703-002	0,75 days	Fri 14.7.23	Mon 17.7.23	20	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 703-002 B2																			
23	Montaža temelja 712-001	0,75 days	Mon 17.7.23	Tue 18.7.23	21	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 712-001 B1																			
24	Montaža temelja 713-007	0,75 days	Mon 17.7.23	Tue 18.7.23	22	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 713-007 B2																			
25	Montaža temelja 714-001	0,75 days	Tue 18.7.23	Tue 18.7.23	23	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 714-001 B1																			
26	Montaža temelja 756-001/02	0,75 days	Tue 18.7.23	Tue 18.7.23	24	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 756-001/02 B2																			
27	Montaža temelja 722-011	0,75 days	Wed 19.7.23	Wed 19.7.23	25	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 722-011 B1																			
28	Montaža temelja 731-001/01	0,75 days	Wed 19.7.23	Wed 19.7.23	26	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 731-001/01 B2																			
29	Montaža temelja 731-001/02	0,75 days	Wed 19.7.23	Thu 20.7.23	27	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 731-001/02 B1																			
30	Montaža temelja 731-002	0,75 days	Wed 19.7.23	Thu 20.7.23	28	\$240,00	12 hrs	Bravari2 (2)[200%]	Montaža temelja 731-002 B2																			
31	Montaža temelja 731-003/01	0,75 days	Thu 20.7.23	Fri 21.7.23	29	\$240,00	12 hrs	Bravari1 (2)[200%]	Montaža temelja 731-003/01 B1																			

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	



ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23			Aug '23				Sep '23			Oct '23					
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24
63	Montaža 714-001	0,5 days	Mon 24.7.23	Tue 25.7.23	61	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
64	Montaža 756-001/02	0,5 days	Mon 24.7.23	Tue 25.7.23	62	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
65	Montaža 722-011	0,5 days	Tue 25.7.23	Tue 25.7.23	63	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
66	Montaža 731-001/01	0,5 days	Tue 25.7.23	Tue 25.7.23	64	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
67	Montaža 731-001/02	0,5 days	Tue 25.7.23	Wed 26.7.23	65	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
68	Montaža 731-002	0,5 days	Tue 25.7.23	Wed 26.7.23	66	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
69	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	67	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
70	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	68	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
71	Montaža 733-001	0,5 days	Wed 26.7.23	Thu 27.7.23	69	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
72	Montaža 733-012	0,5 days	Wed 26.7.23	Thu 27.7.23	70	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
73	Montaža 734-001	0,5 days	Thu 27.7.23	Thu 27.7.23	71	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
74	Montaža 743-002	0,5 days	Thu 27.7.23	Thu 27.7.23	72	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
75	Montaža 743-003	0,5 days	Thu 27.7.23	Fri 28.7.23	73	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
76	Montaža 751-001	0,5 days	Thu 27.7.23	Fri 28.7.23	74	\$192,00	8 hrs	Mehaničari2 (2)[200%]																
77	Montaža 756-004	0,5 days	Fri 28.7.23	Fri 28.7.23	75	\$192,00	8 hrs	Mehaničari1 (2)[200%]																
78	<b>Cjevarski radovi</b>	<b>20,25 days</b>	<b>Wed 19.7.23</b>	<b>Wed 16.8.23</b>	<b>40FS-7 days</b>	<b>\$39.072,00</b>	<b>888 hrs</b>																	
79	Montaža prolaza	5,25 days	Wed 19.7.23	Wed 26.7.23		\$7.392,00	168 hrs	Cjevari1 (4)[400%]																
80	Montaža nosača	7,5 days	Thu 20.7.23	Mon 31.7.23	79FS-5 days	\$10.560,00	240 hrs	Cjevari2 (4)[400%]																
81	Montaža cijevi	15 days	Thu 27.7.23	Wed 16.8.23	79	\$21.120,00	480 hrs	Cjevari1 (4)[400%]																
82	<b>Bravarski radovi</b>	<b>17,5 days</b>	<b>Thu 10.8.23</b>	<b>Mon 4.9.23</b>	<b>78FS-5 days</b>	<b>\$8.480,00</b>	<b>424 hrs</b>																	
83	Montaža podnica	10,5 days	Thu 10.8.23	Thu 24.8.23		\$3.360,00	168 hrs	Bravari2 (2)[200%]																
84	Montaža ljestvi	9 days	Fri 11.8.23	Wed 23.8.23	83SS+1 day	\$2.880,00	144 hrs	Bravari1 (2)[200%]																
85	Montaža skala	7 days	Thu 24.8.23	Mon 4.9.23	83	\$2.240,00	112 hrs	Bravari2 (2)[200%]																
86	<b>Električarski radovi</b>	<b>35,25 days</b>	<b>Mon 31.7.23</b>	<b>Mon 18.9.23</b>	<b>80</b>	<b>\$54.144,00</b>	<b>1.128 hrs</b>																	
87	Montaža kablskih prolaza	5,25 days	Mon 31.7.23	Mon 7.8.23		\$8.064,00	168 hrs	Električari1 (4)[400%]																
88	Montaža kablskih staza	11,25 days	Mon 7.8.23	Tue 22.8.23	87	\$17.280,00	360 hrs	Električari1 (4)[400%]																
89	Provlačenje kabela	18,75 days	Wed 23.8.23	Mon 18.9.23	88	\$28.800,00	600 hrs	Električari1 (4)[400%]																
90	<b>Limarski radovi</b>	<b>15 days</b>	<b>Thu 14.9.23</b>	<b>Wed 4.10.23</b>	<b>78FS+20 days</b>	<b>\$8.160,00</b>	<b>408 hrs</b>																	
91	Montaža ventilacijskih prolaza	7 days	Thu 14.9.23	Fri 22.9.23		\$2.240,00	112 hrs	Limari1 (2)[200%]																
92	Montaža ventilacijskih kanala	15 days	Thu 14.9.23	Wed 4.10.23		\$4.800,00	240 hrs	Limari2 (2)[200%]																
93	Montaža zaštite strojeva I uređaja	3,5 days	Mon 25.9.23	Thu 28.9.23	91	\$1.120,00	56 hrs	Limari1 (2)[200%]																

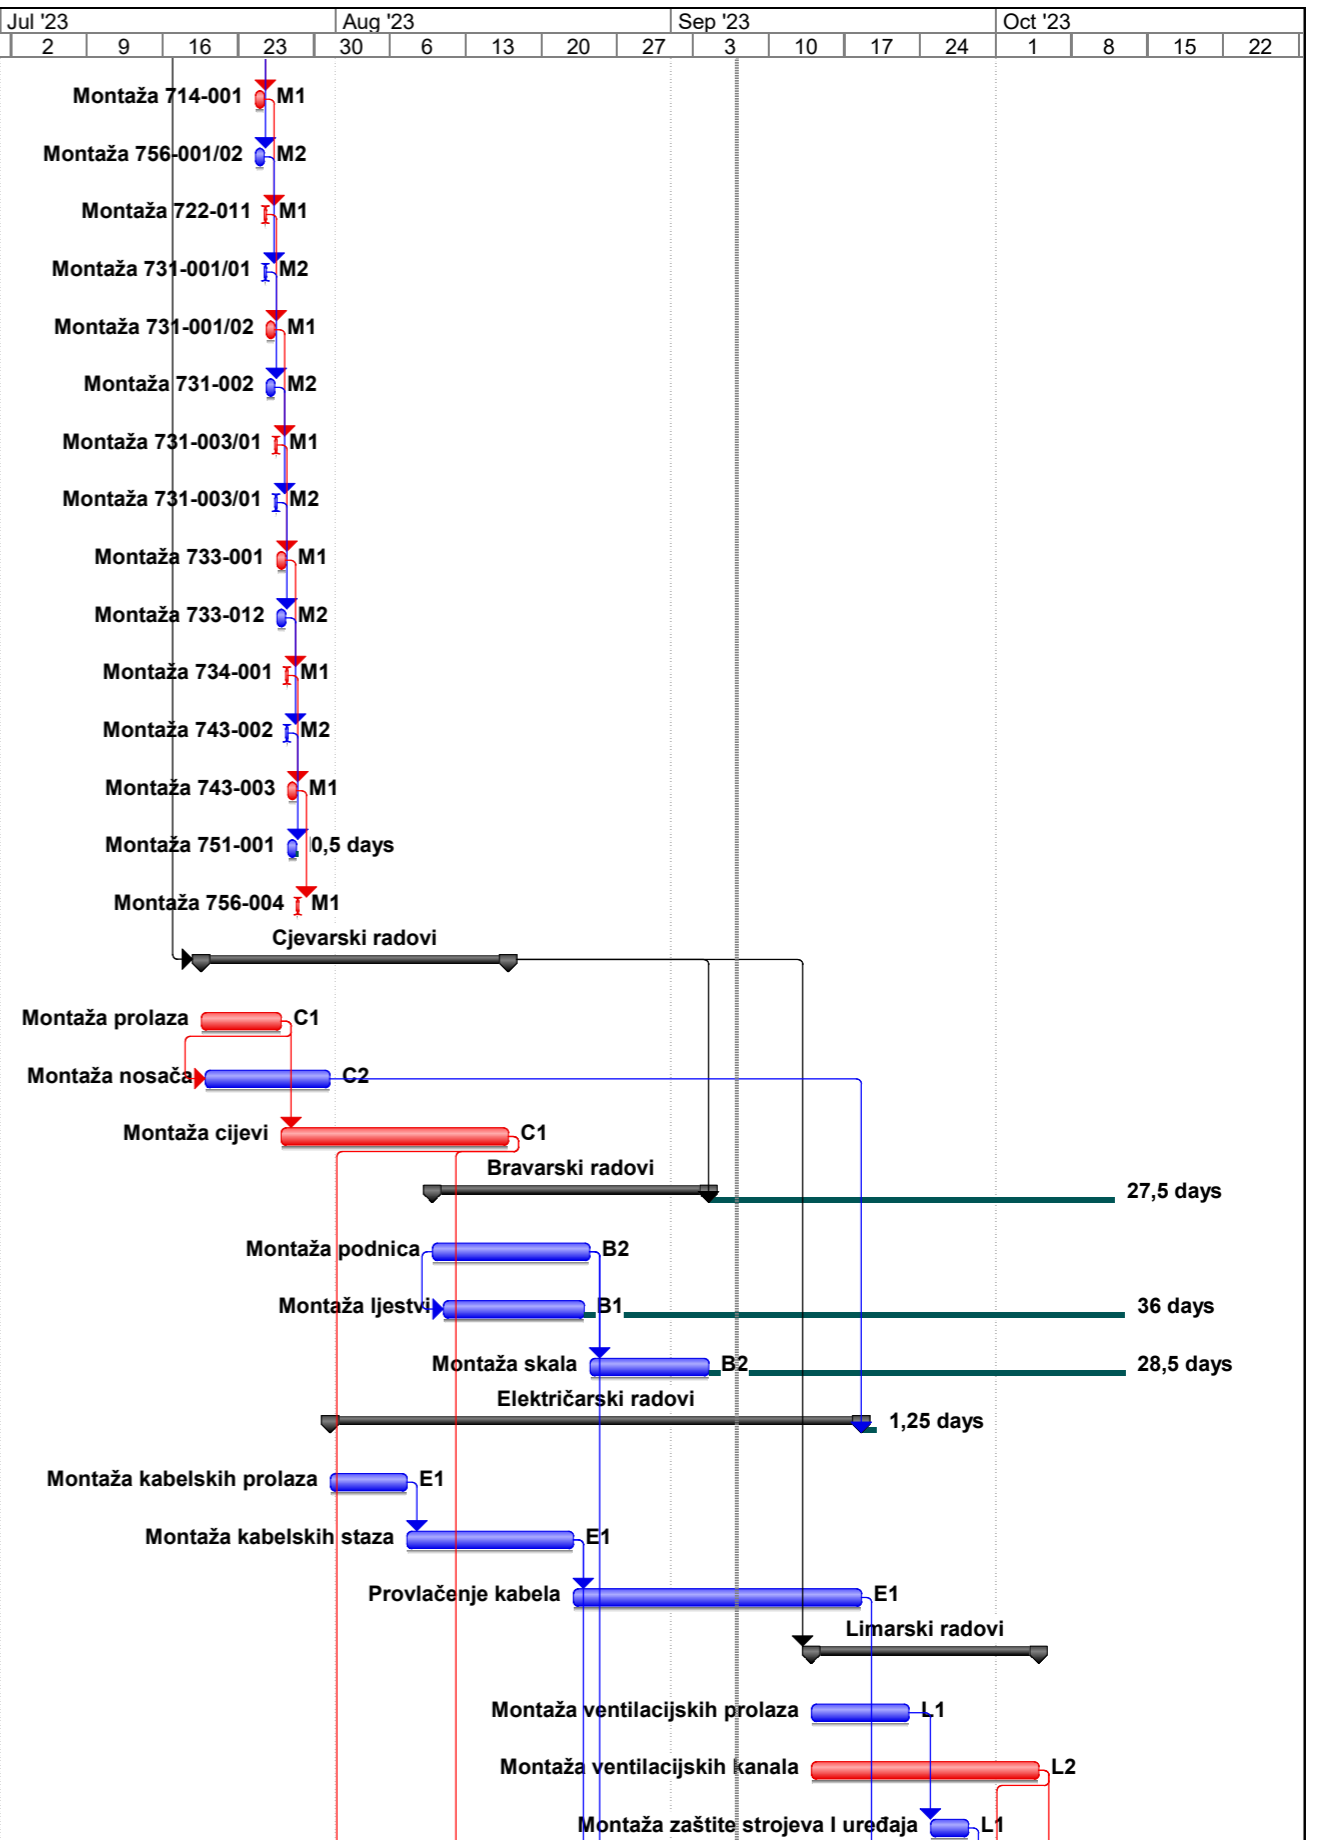

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23			Aug '23				Sep '23			Oct '23									
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22
94	<b>Izolaterski radovi</b>	<b>10 days</b>	<b>Tue 19.9.23</b>	<b>Mon 2.10.23</b>	<b>92FS-12 days</b>	<b>\$7.200,00</b>	<b>240 hrs</b>																					
95	Montaža izolacije	10 days	Tue 19.9.23	Mon 2.10.23		\$7.200,00	240 hrs	Izolateri (3)[300%]																				
96	<b>Ispitivanje</b>	<b>51 days</b>	<b>Thu 3.8.23</b>	<b>Thu 12.10.23</b>		<b>\$15.408,00</b>	<b>760 hrs</b>																					
97	Ispitivanje rada strojeva I uređaja	3 days	Mon 14.8.23	Wed 16.8.23	81FS-3 days	\$288,00	24 hrs	Ispitivači/Mehaničari (1)																				
98	<b>Ispitivanje cjevovoda</b>	<b>16,5 days</b>	<b>Thu 3.8.23</b>	<b>Fri 25.8.23</b>		<b>\$5.808,00</b>	<b>264 hrs</b>																					
99	Pregled strukture cjevovoda	7 days	Thu 3.8.23	Fri 11.8.23	81FS-10 days	\$2.464,00	112 hrs	Ispitivači/cjevar (2)[200%]																				
100	Tlačenje cjevovoda	6 days	Mon 14.8.23	Mon 21.8.23	99	\$2.112,00	96 hrs	Ispitivači/cjevar (2)[200%]																				
101	Pregled funkcionalnosti cjevovoda	3,5 days	Tue 22.8.23	Fri 25.8.23	100	\$1.232,00	56 hrs	Ispitivači/cjevar (2)[200%]																				
102	<b>Pregled bravarskih radova</b>	<b>8 days</b>	<b>Thu 24.8.23</b>	<b>Tue 5.9.23</b>		<b>\$640,00</b>	<b>64 hrs</b>																					
103	Pregled strukture podnica	4 days	Thu 24.8.23	Wed 30.8.23	83	\$320,00	32 hrs	Kontrolori/Bravari (1)																				
104	Pregled strukture ljestvi	2 days	Wed 30.8.23	Fri 1.9.23	103	\$160,00	16 hrs	Kontrolori/Bravari (1)																				
105	Pregled strukture skala	2 days	Fri 1.9.23	Tue 5.9.23	104	\$160,00	16 hrs	Kontrolori/Bravari (1)																				
106	<b>Ispitivanje električarskih radova</b>	<b>35,75 days</b>	<b>Wed 23.8.23</b>	<b>Wed 11.10.23</b>		<b>\$7.872,00</b>	<b>328 hrs</b>																					
107	Pregled strukture kablinskih staza	3,5 days	Wed 23.8.23	Mon 28.8.23	88	\$1.344,00	56 hrs	Ispitivači/Električari (2)[200%]																				
108	Pregled montaže kabela	5 days	Mon 18.9.23	Mon 25.9.23	89	\$1.920,00	80 hrs	Ispitivači/Električari (2)[200%]																				
109	Ispitivanje ožičenja kabela	7 days	Mon 25.9.23	Wed 4.10.23	108	\$2.688,00	112 hrs	Ispitivači/Električari (2)[200%]																				
110	Test ispitivanja pod naponom	5 days	Wed 4.10.23	Wed 11.10.23	109	\$1.920,00	80 hrs	Ispitivači/Električari (2)[200%]																				
111	<b>Ispitivanje limarskih radova</b>	<b>10,5 days</b>	<b>Thu 28.9.23</b>	<b>Thu 12.10.23</b>		<b>\$560,00</b>	<b>56 hrs</b>																					
112	Pregled strukture ventilacije	2 days	Thu 5.10.23	Fri 6.10.23	92	\$160,00	16 hrs	Kontrolori/Limari1 (1)																				
113	Pregled funkcionalnosti ventilacije	4 days	Mon 9.10.23	Thu 12.10.23	112	\$320,00	32 hrs	Kontrolori/Limari1 (1)																				
114	Pregled strukture zaštite strojeva	1 day	Thu 28.9.23	Fri 29.9.23	93	\$80,00	8 hrs	Kontrolori/Limari2 (1)																				
115	<b>Ispitivanje izolaterskih radova</b>	<b>3 days</b>	<b>Tue 3.10.23</b>	<b>Thu 5.10.23</b>		<b>\$240,00</b>	<b>24 hrs</b>																					

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	
