

## Prilog 4

---

Ćosić, Matej

### Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:693992>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-09-29**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023		Qtr 2, 2023		Qtr 3, 2023		
							Nov	Dec	Jan	Feb	Mar	Apr	May
1	<b>OPREMANJE KROVA DVODNA STROJARNICE</b>	142,8 days	Mon 12.12.22	105.563,20 €	3.164,8 hrs	Wed 28.6.23	<b>OPREMANJE KROVA DVODNA STROJARNICE</b>						
2	<b>Montaža temelja Brigada 1</b>	8,5 days	Mon 12.12.22	1.360,00 €	68 hrs	Thu 22.12.22	<b>Montaža temelja Brigada 1</b>						
3	Montaža temelja 382-002/01	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	Bravari (2) B1						
4	Montaža temelja 382-002/02	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	Bravari (2) B1						
5	Montaža temelja 601-001	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	Bravari (2) B1						
6	Montaža temelja 601-019	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	Bravari (2) B1						
7	Montaža temelja 631-014	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	Bravari (2) B1						
8	Montaža temelja 631-015	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	Bravari (2) B1						
9	Montaža temelja 631-016	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	Bravari (2) B1						
10	Montaža temelja 631-022	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	Bravari (2) B1						
11	Montaža temelja 701-001/01	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	Bravari (2) B1						
12	Montaža temelja 701-001/02	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	Bravari (2) B1						
13	Montaža temelja 701-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	Bravari (2) B1						
14	Montaža temelja 702-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	Bravari (2) B1						
15	Montaža temelja 702-003	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	Bravari (2) B1						
16	Montaža temelja 711-001	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	Bravari (2) B1						
17	Montaža temelja 712-002/01	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	Bravari (2) B1						
18	Montaža temelja 712-002/02	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	Bravari (2) B1						
19	Montaža temelja 713-001/01	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22	Bravari (2) B1						
20	<b>Montaža temelja Brigada 2</b>	8,5 days	Mon 12.12.22	1.360,00 €	68 hrs	Thu 22.12.22	<b>Montaža temelja Brigada 2</b>						
21	Montaža temelja 713-001/02	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	Bravari (2) B2						
22	Montaža temelja 713-009	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	Bravari (2) B2						
23	Montaža temelja 721-001/01	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	Bravari (2) B2						
24	Montaža temelja 721-001/02	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	Bravari (2) B2						
25	Montaža temelja 721-001/03	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	Bravari (2) B2						
26	Montaža temelja 756-001/01	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	Bravari (2) B2						
27	Montaža temelja 756-001/02	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	Bravari (2) B2						
28	Montaža temelja 756-002/01	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	Bravari (2) B2						
29	Montaža temelja 756-002/02	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	Bravari (2) B2						
30	Montaža temelja 756-003	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	Bravari (2) B2						
31	Montaža temelja 761-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	Bravari (2) B2						

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
32	Montaža temelja 803-001	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22		Bravari (2) B2						
33	Montaža temelja 803-002	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22		Bravari (2) B2						
34	Montaža temelja 803-003	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22		Bravari (2) B2						
35	Montaža temelja 803-004	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22		Bravari (2) B2						
36	Montaža temelja 813-001/01	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22		Bravari (2) B2						
37	Montaža temelja 813-001/02	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22		Bravari (2) B2						
38	<b>Montaža strojeva I uređaja Brigada 1</b>	<b>6,8 days</b>	<b>Tue 13.12.22</b>	<b>1.305,60 €</b>	<b>54,4 hrs</b>	<b>Thu 22.12.22</b>		<b>Montaža strojeva I uređaja Brigada 1</b>						
39	Montaža 382-002/01	0,4 days	Tue 13.12.22	76,80 €	3,2 hrs	Tue 13.12.22		Mehaničari (2) M1						
40	Montaža 382-002/02	0,4 days	Tue 13.12.22	76,80 €	3,2 hrs	Wed 14.12.22		Mehaničari (2) M1						
41	Montaža 601-001	0,4 days	Wed 14.12.22	76,80 €	3,2 hrs	Wed 14.12.22		Mehaničari (2) M1						
42	Montaža 601-019	0,4 days	Wed 14.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M1						
43	Montaža 631-014	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M1						
44	Montaža 631-015	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M1						
45	Montaža 631-016	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Fri 16.12.22		Mehaničari (2) M1						
46	Montaža 631-022	0,4 days	Fri 16.12.22	76,80 €	3,2 hrs	Fri 16.12.22		Mehaničari (2) M1						
47	Montaža 701-001/01	0,4 days	Fri 16.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M1						
48	Montaža 701-001/02	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M1						
49	Montaža 701-002	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M1						
50	Montaža 702-002	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Tue 20.12.22		Mehaničari (2) M1						
51	Montaža 702-003	0,4 days	Tue 20.12.22	76,80 €	3,2 hrs	Tue 20.12.22		Mehaničari (2) M1						
52	Montaža 711-001	0,4 days	Tue 20.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M1						
53	Montaža 712-002/01	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M1						
54	Montaža 712-002/02	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M1						
55	Montaža 713-001/01	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Thu 22.12.22		Mehaničari (2) M1						
56	<b>Montaža strojeva I uređaja Brigada 2</b>	<b>6,8 days</b>	<b>Tue 13.12.22</b>	<b>1.305,60 €</b>	<b>54,4 hrs</b>	<b>Thu 22.12.22</b>		<b>Montaža strojeva I uređaja Brigada 2</b>						
57	Montaža 713-001/02	0,4 days	Tue 13.12.22	76,80 €	3,2 hrs	Tue 13.12.22		Mehaničari (2) M2						
58	Montaža 713-009	0,4 days	Tue 13.12.22	76,80 €	3,2 hrs	Wed 14.12.22		Mehaničari (2) M2						
59	Montaža 721-001/01	0,4 days	Wed 14.12.22	76,80 €	3,2 hrs	Wed 14.12.22		Mehaničari (2) M2						
60	Montaža 721-001/02	0,4 days	Wed 14.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M2						
61	Montaža 721-001/03	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M2						
62	Montaža 756-001/01	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Thu 15.12.22		Mehaničari (2) M2						

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23


Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
63	Montaža 756-001/02	0,4 days	Thu 15.12.22	76,80 €	3,2 hrs	Fri 16.12.22		Mehaničari (2) M2						
64	Montaža 756-002/01	0,4 days	Fri 16.12.22	76,80 €	3,2 hrs	Fri 16.12.22		Mehaničari (2) M2						
65	Montaža 756-002/02	0,4 days	Fri 16.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M2						
66	Montaža 756-003	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M2						
67	Montaža 761-002	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Mon 19.12.22		Mehaničari (2) M2						
68	Montaža 803-001	0,4 days	Mon 19.12.22	76,80 €	3,2 hrs	Tue 20.12.22		Mehaničari (2) M2						
69	Montaža 803-002	0,4 days	Tue 20.12.22	76,80 €	3,2 hrs	Tue 20.12.22		Mehaničari (2) M2						
70	Montaža 803-003	0,4 days	Tue 20.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M2						
71	Montaža 803-004	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M2						
72	Montaža 813-001/01	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Wed 21.12.22		Mehaničari (2) M2						
73	Montaža 813-001/02	0,4 days	Wed 21.12.22	76,80 €	3,2 hrs	Thu 22.12.22		Mehaničari (2) M2						
74	<b>Cjevarski radovi</b>	<b>47,5 days</b>	<b>Tue 13.12.22</b>	<b>29.920,00 €</b>	<b>680 hrs</b>	<b>Thu 16.2.23</b>								
75	Montaža prolaza	15 days	Tue 13.12.22	5.280,00 €	120 hrs	Tue 3.1.23		Cjevari (4) C1						
76	Montaža nosača	25 days	Tue 13.12.22	8.800,00 €	200 hrs	Tue 17.1.23		Cjevari (4) C2						
77	Montaža cijevi brigada 1	22,5 days	Tue 3.1.23	7.920,00 €	180 hrs	Thu 2.2.23		Cjevari (4) C1						
78	Montaža cijevi brigada 2	22,5 days	Tue 17.1.23	7.920,00 €	180 hrs	Thu 16.2.23		Cjevari (4) C2						
79	<b>Bravarski radovi</b>	<b>16,5 days</b>	<b>Thu 5.1.23</b>	<b>5.120,00 €</b>	<b>256 hrs</b>	<b>Mon 30.1.23</b>								
80	Montaža podnica	13 days	Thu 5.1.23	2.080,00 €	104 hrs	Tue 24.1.23		Bravari (2) B1						
81	Montaža ljestvi	12 days	Thu 5.1.23	1.920,00 €	96 hrs	Mon 23.1.23		Bravari (2) B2						
82	Montaža skala brigada 1	3,5 days	Tue 24.1.23	560,00 €	28 hrs	Mon 30.1.23		Bravari (2) B1						
83	Montaža skala brigada 2	3,5 days	Mon 23.1.23	560,00 €	28 hrs	Fri 27.1.23		Bravari (2) B2						
84	<b>Električarski radovi</b>	<b>60 days</b>	<b>Thu 16.2.23</b>	<b>38.400,00 €</b>	<b>800 hrs</b>	<b>Thu 11.5.23</b>								
85	Montaža kablskih prolaza - brigada 1	10 days	Thu 16.2.23	3.840,00 €	80 hrs	Thu 2.3.23		Električari (4) E1						
86	Montaža kablskih staza - brigada 2	30 days	Thu 16.2.23	11.520,00 €	240 hrs	Thu 30.3.23		Električari (4) E2						
87	Provlačenje kabela brigada 1	30 days	Thu 2.3.23	11.520,00 €	240 hrs	Thu 13.4.23		Električari (4) E1						
88	Provlačenje kabela brigada 2	30 days	Thu 30.3.23	11.520,00 €	240 hrs	Thu 11.5.23		Električari (4) E2						
89	<b>Limarski radovi</b>	<b>21 days</b>	<b>Thu 16.3.23</b>	<b>6.080,00 €</b>	<b>304 hrs</b>	<b>Fri 14.4.23</b>								
90	Montaža ventilacijskih prolaza - brigada 1	10 days	Thu 16.3.23	1.600,00 €	80 hrs	Thu 30.3.23		Limari (2) L1						
91	Montaža ventilacijskih kanala - brigada 2	21 days	Thu 16.3.23	3.360,00 €	168 hrs	Fri 14.4.23		Limari (2) L2						
92	Montaža zaštita strojeva I uređaja - brigada 1	3,5 days	Thu 30.3.23	560,00 €	28 hrs	Wed 5.4.23		Limari (2) L1						
93	Montaža zaštita strojeva I uređaja - brigada 1	3,5 days	Wed 5.4.23	560,00 €	28 hrs	Mon 10.4.23		Limari (2) L1						

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Nov		Dec		Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023	
											Jan	Feb	Mar	Apr	May	Jun	Jul	
94	<b>Izolaterski radovi</b>	7,5 days	Fri 14.4.23	2.400,00 €	120 hrs	Wed 26.4.23												
95	Montaža izolacije - brigada 1	7,5 days	Fri 14.4.23	1.200,00 €	60 hrs	Wed 26.4.23												
96	Montaža izolacije - brigada 2	7,5 days	Fri 14.4.23	1.200,00 €	60 hrs	Wed 26.4.23												
97	<b>Ispitivanje</b>	111 days	Tue 24.1.23	18.312,00 €	760 hrs	Wed 28.6.23												
98	Ispitivanje rada strojeva I uređaja	1,5 days	Tue 7.2.23	144,00 €	12 hrs	Thu 9.2.23												
99	Ispitivanje rada strojeva I uređaja	1,5 days	Tue 7.2.23	144,00 €	12 hrs	Thu 9.2.23												
100	<b>Ispitivanje cjevovoda</b>	24,5 days	Thu 2.2.23	8.712,00 €	264 hrs	Thu 9.3.23												
101	Pregled strukture cjevovoda	14 days	Thu 2.2.23	3.696,00 €	112 hrs	Wed 22.2.23												
102	Tlačenje cjevovoda	12 days	Wed 15.2.23	3.168,00 €	96 hrs	Fri 3.3.23												
103	Pregled funkcionalnosti cjevovoda - brigada 1	3,5 days	Fri 3.3.23	924,00 €	28 hrs	Thu 9.3.23												
104	Pregled funkcionalnosti cjevovoda - brigada 2	3,5 days	Fri 3.3.23	924,00 €	28 hrs	Thu 9.3.23												
105	<b>Pregled bravarskih radova</b>	4,5 days	Tue 24.1.23	640,00 €	64 hrs	Tue 31.1.23												
106	Pregled strukture podnica - brigada 1	2 days	Tue 24.1.23	160,00 €	16 hrs	Thu 26.1.23												
107	Pregled strukture podnica - brigada 2	2 days	Tue 24.1.23	160,00 €	16 hrs	Thu 26.1.23												
108	Pregled strukture ljestvi	2 days	Thu 26.1.23	160,00 €	16 hrs	Fri 27.1.23												
109	Pregled strukture skala	2 days	Fri 27.1.23	160,00 €	16 hrs	Tue 31.1.23												
110	<b>Ispitivanje električarskih radova</b>	64 days	Thu 30.3.23	7.872,00 €	328 hrs	Wed 28.6.23												
111	Pregled strukture kablskih staza	7 days	Thu 30.3.23	1.344,00 €	56 hrs	Mon 10.4.23												
112	Pregled montaže kabela	10 days	Thu 11.5.23	1.920,00 €	80 hrs	Thu 25.5.23												
113	Ispitivanje ožičenja kabela	14 days	Thu 25.5.23	2.688,00 €	112 hrs	Wed 14.6.23												
114	Test ispitivanja pod naponom	10 days	Wed 14.6.23	1.920,00 €	80 hrs	Wed 28.6.23												
115	<b>Ispitivanje limarskih radova</b>	14,2 days	Fri 14.4.23	560,00 €	56 hrs	Thu 4.5.23												
116	Pregled strukture ventilacije	2 days	Fri 14.4.23	160,00 €	16 hrs	Tue 18.4.23												
117	Pregled funkcionalnosti ventilacije brigada 1	2 days	Tue 18.4.23	160,00 €	16 hrs	Thu 20.4.23												
118	Pregled funkcionalnosti ventilacije brigada 2	2 days	Tue 18.4.23	160,00 €	16 hrs	Thu 20.4.23												
119	Pregled strukture zaštite strojeva	1 day	Thu 4.5.23	80,00 €	8 hrs	Thu 4.5.23												
120	<b>Ispitivanje izolaterskih radova</b>	1,5 days	Wed 26.4.23	240,00 €	24 hrs	Thu 27.4.23												
121	Pregled montaže izolacije brigada 1	1,5 days	Wed 26.4.23	120,00 €	12 hrs	Thu 27.4.23												
122	Pregled montaže izolacije brigada 2	1,5 days	Wed 26.4.23	120,00 €	12 hrs	Thu 27.4.23												

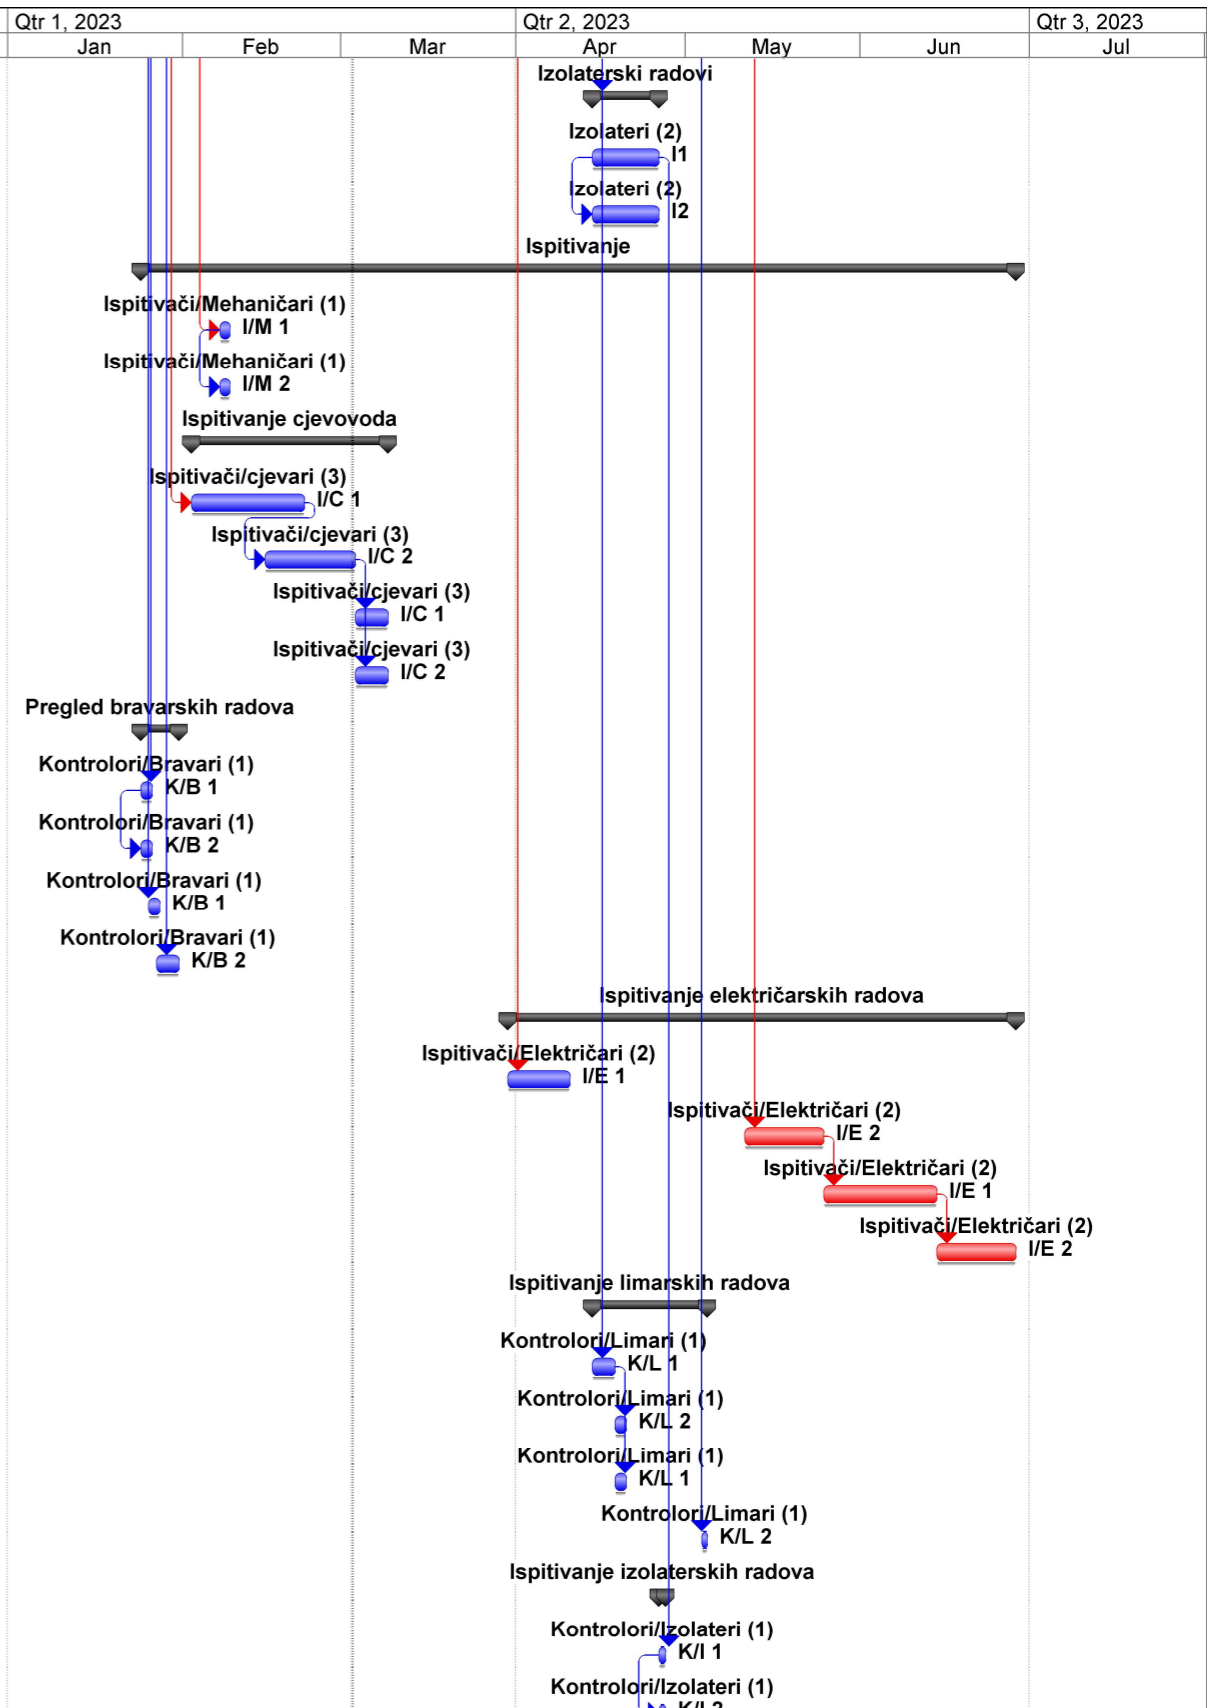

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			
