

Prilog - peti slučaj

Butorac, Lovro

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:889398>

Rights / Prava: [In copyright](#)/[Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-11-30**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23							Aug '23				Sep '23			Oct '23				
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1		
1	OPREMANJE 2. PLATFORME STROJARNICE	59 days	Thu 6.7.23	Tue 26.9.23		\$148.928,00	4.588 hrs		OPREMANJE 2. PLATFORME STROJARNICE																		
2	Montaža temelja	14,25 days	Thu 6.7.23	Wed 26.7.23		\$8.880,00	444 hrs		Montaža temelja																		
3	Montaža temelja 445-003	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari1 (2)[200%]																			
4	Montaža temelja 445-004	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari2 (2)[200%]																			
5	Montaža temelja 452-001	0,75 days	Thu 6.7.23	Fri 7.7.23	3	\$240,00	12 hrs	Bravari1 (2)[200%]																			
6	Montaža temelja 452-005	0,75 days	Thu 6.7.23	Fri 7.7.23	4	\$240,00	12 hrs	Bravari2 (2)[200%]																			
7	Montaža temelja 581-001	0,75 days	Fri 7.7.23	Mon 10.7.23	5	\$240,00	12 hrs	Bravari1 (2)[200%]																			
8	Montaža temelja 581-002	0,75 days	Fri 7.7.23	Mon 10.7.23	6	\$240,00	12 hrs	Bravari2 (2)[200%]																			
9	Montaža temelja 581-003	0,75 days	Mon 10.7.23	Mon 10.7.23	7	\$240,00	12 hrs	Bravari1 (2)[200%]																			
10	Montaža temelja 582-001	0,75 days	Mon 10.7.23	Mon 10.7.23	8	\$240,00	12 hrs	Bravari2 (2)[200%]																			
11	Montaža temelja 582-003/01	0,75 days	Tue 11.7.23	Tue 11.7.23	9	\$240,00	12 hrs	Bravari1 (2)[200%]																			
12	Montaža temelja 582-003/02	0,75 days	Tue 11.7.23	Tue 11.7.23	10	\$240,00	12 hrs	Bravari2 (2)[200%]																			
13	Montaža temelja 644-008/01	0,75 days	Tue 11.7.23	Wed 12.7.23	11	\$240,00	12 hrs	Bravari1 (2)[200%]																			
14	Montaža temelja 644-008/02	0,75 days	Tue 11.7.23	Wed 12.7.23	12	\$240,00	12 hrs	Bravari2 (2)[200%]																			
15	Montaža temelja 651-001	0,75 days	Wed 12.7.23	Thu 13.7.23	13	\$240,00	12 hrs	Bravari1 (2)[200%]																			
16	Montaža temelja 651-002	0,75 days	Wed 12.7.23	Thu 13.7.23	14	\$240,00	12 hrs	Bravari2 (2)[200%]																			
17	Montaža temelja 651-003	0,75 days	Thu 13.7.23	Thu 13.7.23	15	\$240,00	12 hrs	Bravari1 (2)[200%]																			
18	Montaža temelja 702-001	0,75 days	Thu 13.7.23	Thu 13.7.23	16	\$240,00	12 hrs	Bravari2 (2)[200%]																			
19	Montaža temelja 702-004	0,75 days	Fri 14.7.23	Fri 14.7.23	17	\$240,00	12 hrs	Bravari1 (2)[200%]																			
20	Montaža temelja 702-005	0,75 days	Fri 14.7.23	Fri 14.7.23	18	\$240,00	12 hrs	Bravari2 (2)[200%]																			
21	Montaža temelja 703-001	0,75 days	Fri 14.7.23	Mon 17.7.23	19	\$240,00	12 hrs	Bravari1 (2)[200%]																			
22	Montaža temelja 703-002	0,75 days	Fri 14.7.23	Mon 17.7.23	20	\$240,00	12 hrs	Bravari2 (2)[200%]																			
23	Montaža temelja 712-001	0,75 days	Mon 17.7.23	Tue 18.7.23	21	\$240,00	12 hrs	Bravari1 (2)[200%]																			
24	Montaža temelja 713-007	0,75 days	Mon 17.7.23	Tue 18.7.23	22	\$240,00	12 hrs	Bravari2 (2)[200%]																			
25	Montaža temelja 714-001	0,75 days	Tue 18.7.23	Tue 18.7.23	23	\$240,00	12 hrs	Bravari1 (2)[200%]																			
26	Montaža temelja 756-001/02	0,75 days	Tue 18.7.23	Tue 18.7.23	24	\$240,00	12 hrs	Bravari2 (2)[200%]																			
27	Montaža temelja 722-011	0,75 days	Wed 19.7.23	Wed 19.7.23	25	\$240,00	12 hrs	Bravari1 (2)[200%]																			
28	Montaža temelja 731-001/01	0,75 days	Wed 19.7.23	Wed 19.7.23	26	\$240,00	12 hrs	Bravari2 (2)[200%]																			
29	Montaža temelja 731-001/02	0,75 days	Wed 19.7.23	Thu 20.7.23	27	\$240,00	12 hrs	Bravari1 (2)[200%]																			
30	Montaža temelja 731-002	0,75 days	Wed 19.7.23	Thu 20.7.23	28	\$240,00	12 hrs	Bravari2 (2)[200%]																			
31	Montaža temelja 731-003/01	0,75 days	Thu 20.7.23	Fri 21.7.23	29	\$240,00	12 hrs	Bravari1 (2)[200%]																			

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23


Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23					Aug '23					Sep '23			Oct '23					
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1		
32	Montaža temelja 731-003/01	0,75 days	Thu 20.7.23	Fri 21.7.23	30	\$240,00	12 hrs	Bravari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 731-003/01 B2</p> </div>																		
33	Montaža temelja 733-001	0,75 days	Fri 21.7.23	Fri 21.7.23	31	\$240,00	12 hrs	Bravari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 733-001 B1</p> </div>																		
34	Montaža temelja 733-012	0,75 days	Fri 21.7.23	Fri 21.7.23	32	\$240,00	12 hrs	Bravari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 733-012 B2</p> </div>																		
35	Montaža temelja 734-001	0,75 days	Mon 24.7.23	Mon 24.7.23	33	\$240,00	12 hrs	Bravari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 734-001 B1</p> </div>																		
36	Montaža temelja 743-002	0,75 days	Mon 24.7.23	Mon 24.7.23	34	\$240,00	12 hrs	Bravari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 743-002 B2</p> </div>																		
37	Montaža temelja 743-003	0,75 days	Mon 24.7.23	Tue 25.7.23	35	\$240,00	12 hrs	Bravari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 743-003 B1</p> </div>																		
38	Montaža temelja 751-001	0,75 days	Mon 24.7.23	Tue 25.7.23	36	\$240,00	12 hrs	Bravari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 751-001 B0,75 days</p> </div>																		
39	Montaža temelja 756-004	0,75 days	Tue 25.7.23	Wed 26.7.23	37	\$240,00	12 hrs	Bravari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža temelja 756-004 B1</p> </div>																		
40	Montaža strojeva I uređaja	9,5 days	Mon 17.7.23	Fri 28.7.23	2FS-7 days	\$7.104,00	296 hrs		<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža strojeva I uređaja</p> </div>																		
41	Montaža 445-003	0,5 days	Mon 17.7.23	Mon 17.7.23		\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 445-003 M1</p> </div>																		
42	Montaža 445-004	0,5 days	Mon 17.7.23	Mon 17.7.23		\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 445-004 M2</p> </div>																		
43	Montaža 452-001	0,5 days	Mon 17.7.23	Tue 18.7.23	41	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 452-001 M1</p> </div>																		
44	Montaža 452-005	0,5 days	Mon 17.7.23	Tue 18.7.23	42	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 452-005 M2</p> </div>																		
45	Montaža 581-001	0,5 days	Tue 18.7.23	Tue 18.7.23	43	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 581-001 M1</p> </div>																		
46	Montaža 581-002	0,5 days	Tue 18.7.23	Tue 18.7.23	44	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 581-002 M2</p> </div>																		
47	Montaža 581-003	0,5 days	Tue 18.7.23	Wed 19.7.23	45	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 581-003 M1</p> </div>																		
48	Montaža 582-001	0,5 days	Tue 18.7.23	Wed 19.7.23	46	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 582-001 M2</p> </div>																		
49	Montaža 582-003/01	0,5 days	Wed 19.7.23	Wed 19.7.23	47	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 582-003/01 M1</p> </div>																		
50	Montaža 582-003/02	0,5 days	Wed 19.7.23	Wed 19.7.23	48	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 582-003/02 M2</p> </div>																		
51	Montaža 644-008/01	0,5 days	Wed 19.7.23	Thu 20.7.23	49	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 644-008/01 M1</p> </div>																		
52	Montaža 644-008/02	0,5 days	Wed 19.7.23	Thu 20.7.23	50	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 644-008/02 M2</p> </div>																		
53	Montaža 651-001	0,5 days	Thu 20.7.23	Thu 20.7.23	51	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 651-001 M1</p> </div>																		
54	Montaža 651-002	0,5 days	Thu 20.7.23	Thu 20.7.23	52	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 651-002 M2</p> </div>																		
55	Montaža 651-003	0,5 days	Thu 20.7.23	Fri 21.7.23	53	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 651-003 M1</p> </div>																		
56	Montaža 702-001	0,5 days	Thu 20.7.23	Fri 21.7.23	54	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 702-001 M2</p> </div>																		
57	Montaža 702-004	0,5 days	Fri 21.7.23	Fri 21.7.23	55	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 702-004 M1</p> </div>																		
58	Montaža 702-005	0,5 days	Fri 21.7.23	Fri 21.7.23	56	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 702-005 M2</p> </div>																		
59	Montaža 703-001	0,5 days	Fri 21.7.23	Mon 24.7.23	57	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 703-001 M1</p> </div>																		
60	Montaža 703-002	0,5 days	Fri 21.7.23	Mon 24.7.23	58	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 703-002 M2</p> </div>																		
61	Montaža 712-001	0,5 days	Mon 24.7.23	Mon 24.7.23	59	\$192,00	8 hrs	Mehaničari1 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 712-001 M1</p> </div>																		
62	Montaža 713-007	0,5 days	Mon 24.7.23	Mon 24.7.23	60	\$192,00	8 hrs	Mehaničari2 (2)[200%]	<div style="position: absolute; left: 50%; top: 0; width: 100%; text-align: center;"> <p>Montaža 713-007 M2</p> </div>																		

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical	Split	Slack	Project Summary	External Tasks
Critical Split	Progress	Slippage	Rolled Up Critical	External Milestone
Task	Milestone	Summary	Rolled Up Critical	Deadline

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23				Aug '23				Sep '23				Oct '23	
									11	18	25	2	9	16	23	30	6	13	20	27	3	10
63	Montaža 714-001	0,5 days	Mon 24.7.23	Tue 25.7.23	61	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
64	Montaža 756-001/02	0,5 days	Mon 24.7.23	Tue 25.7.23	62	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
65	Montaža 722-011	0,5 days	Tue 25.7.23	Tue 25.7.23	63	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
66	Montaža 731-001/01	0,5 days	Tue 25.7.23	Tue 25.7.23	64	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
67	Montaža 731-001/02	0,5 days	Tue 25.7.23	Wed 26.7.23	65	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
68	Montaža 731-002	0,5 days	Tue 25.7.23	Wed 26.7.23	66	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
69	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	67	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
70	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	68	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
71	Montaža 733-001	0,5 days	Wed 26.7.23	Thu 27.7.23	69	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
72	Montaža 733-012	0,5 days	Wed 26.7.23	Thu 27.7.23	70	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
73	Montaža 734-001	0,5 days	Thu 27.7.23	Thu 27.7.23	71	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
74	Montaža 743-002	0,5 days	Thu 27.7.23	Thu 27.7.23	72	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
75	Montaža 743-003	0,5 days	Thu 27.7.23	Fri 28.7.23	73	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
76	Montaža 751-001	0,5 days	Thu 27.7.23	Fri 28.7.23	74	\$192,00	8 hrs	Mehaničari2 (2)[200%]														
77	Montaža 756-004	0,5 days	Fri 28.7.23	Fri 28.7.23	75	\$192,00	8 hrs	Mehaničari1 (2)[200%]														
78	Cjevarski radovi	20,25 days	Wed 19.7.23	Wed 16.8.23	40FS-7 days	\$39.072,00	888 hrs															
79	Montaža prolaza	5,25 days	Wed 19.7.23	Wed 26.7.23		\$7.392,00	168 hrs	Cjevari1 (4)[400%]														
80	Montaža nosača	7,5 days	Thu 20.7.23	Mon 31.7.23	79FS-5 days	\$10.560,00	240 hrs	Cjevari2 (4)[400%]														
81	Montaža cijevi	15 days	Thu 27.7.23	Wed 16.8.23	79	\$21.120,00	480 hrs	Cjevari1 (4)[400%]														
82	Bravarski radovi	17,5 days	Wed 26.7.23	Fri 18.8.23	78FS-16 days	\$8.480,00	424 hrs															
83	Montaža podnica	10,5 days	Wed 26.7.23	Wed 9.8.23		\$3.360,00	168 hrs	Bravari2 (2)[200%]														
84	Montaža ljestvi	9 days	Thu 27.7.23	Wed 9.8.23	37FS+2 days	\$2.880,00	144 hrs	Bravari1 (2)[200%]														
85	Montaža skala	7 days	Wed 9.8.23	Fri 18.8.23	83	\$2.240,00	112 hrs	Bravari2 (2)[200%]														
86	Električarski radovi	24 days	Mon 31.7.23	Fri 1.9.23	80	\$54.144,00	1.128 hrs															
87	Montaža kablskih prolaza	5,25 days	Mon 31.7.23	Mon 7.8.23		\$8.064,00	168 hrs	Električari1 (4)[400%]														
88	Montaža kablskih staza	11,25 days	Mon 7.8.23	Tue 22.8.23	87	\$17.280,00	360 hrs	Električari1 (4)[400%]														
89	Provlačenje kabela	18,75 days	Mon 7.8.23	Fri 1.9.23	87	\$28.800,00	600 hrs	Električari2 (4)[400%]														
90	Limarski radovi	15 days	Thu 31.8.23	Wed 20.9.23	78FS+10 days	\$8.160,00	408 hrs															
91	Montaža ventilacijskih prolaza	7 days	Thu 31.8.23	Fri 8.9.23		\$2.240,00	112 hrs	Limari2 (2)[200%]														
92	Montaža ventilacijskih kanala	15 days	Thu 31.8.23	Wed 20.9.23		\$4.800,00	240 hrs	Limari1 (2)[200%]														
93	Montaža zaštite strojeva I uređaja	3,5 days	Mon 11.9.23	Thu 14.9.23	91	\$1.120,00	56 hrs	Limari2 (2)[200%]														

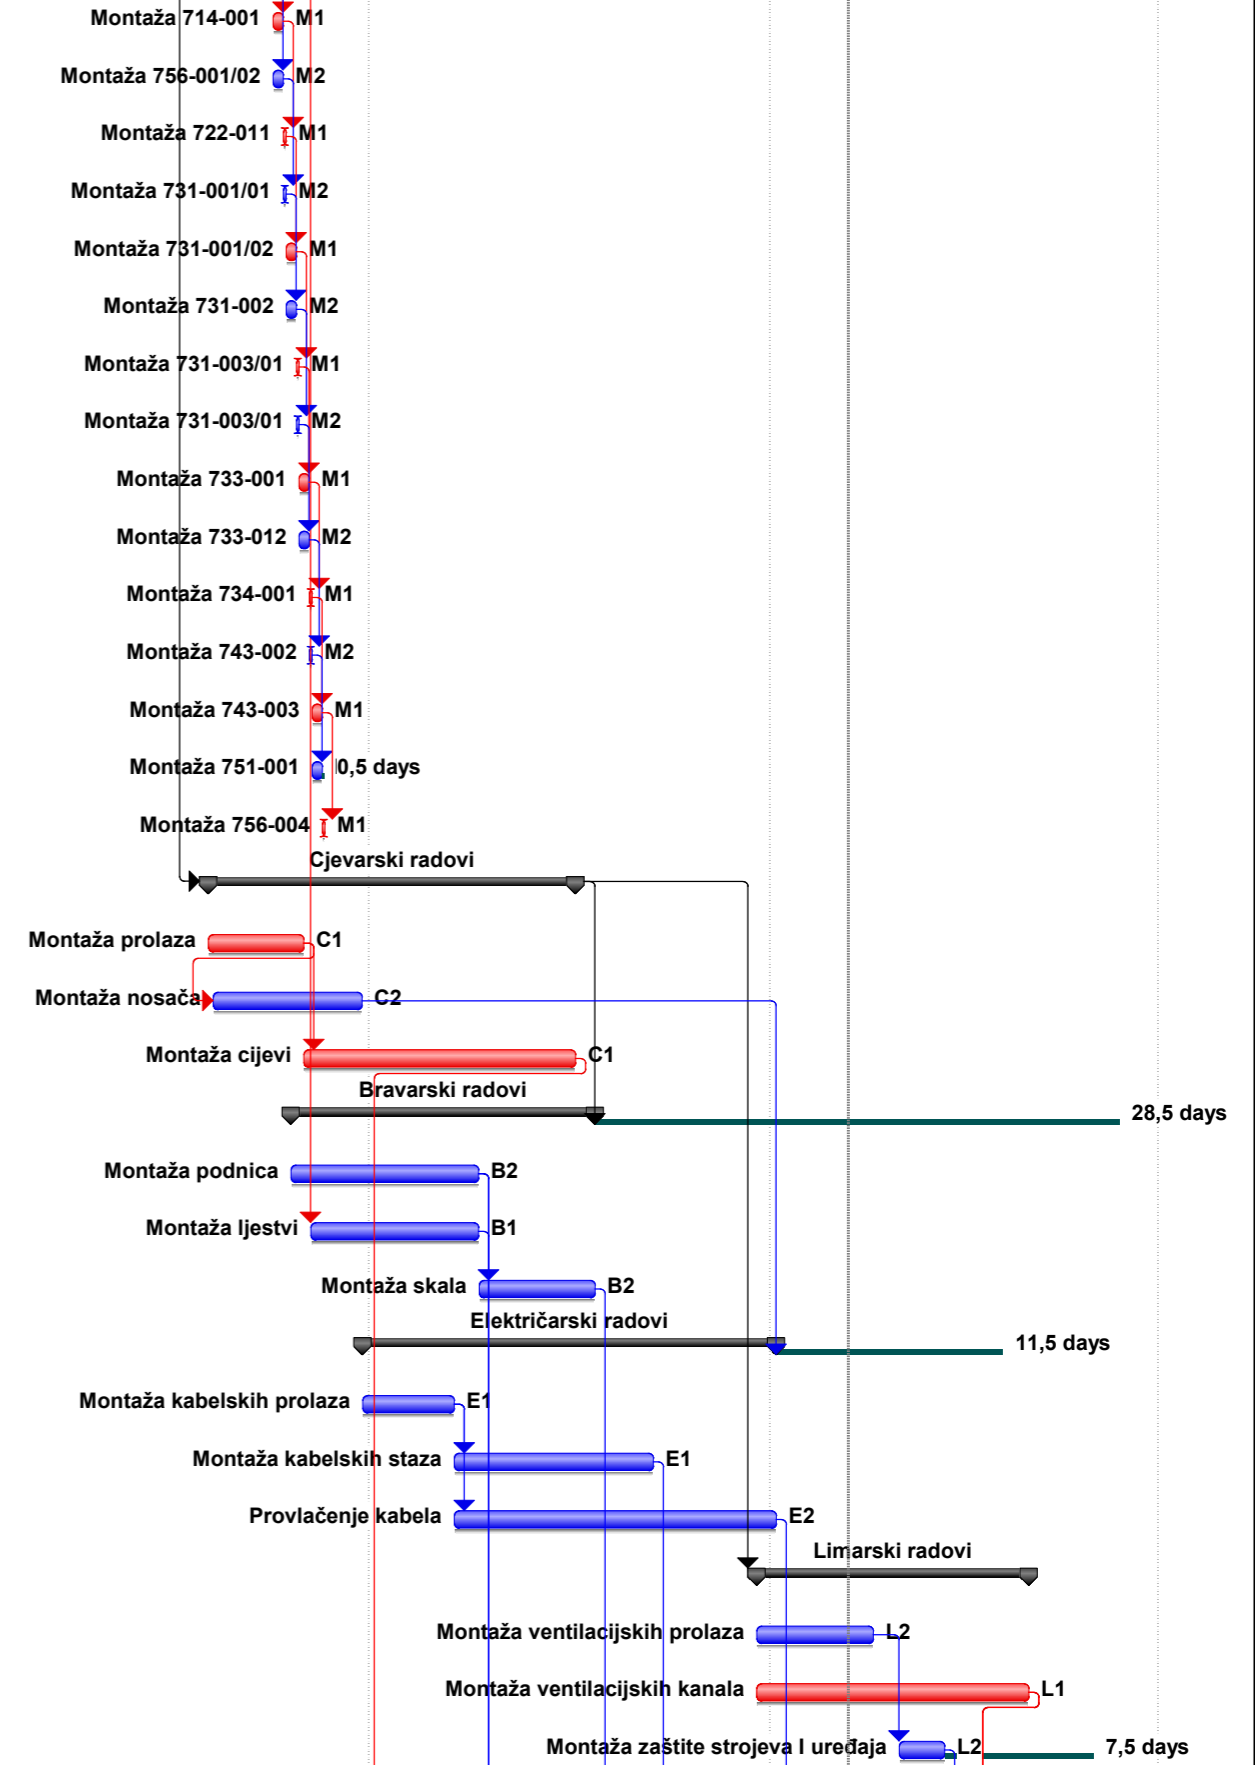

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23							Aug '23							Sep '23				Oct '23
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1		
94	Izolaterski radovi	10 days	Tue 5.9.23	Mon 18.9.23	92FS-12 days	\$7.200,00	240 hrs																				
95	Montaža izolacije	10 days	Tue 5.9.23	Mon 18.9.23		\$7.200,00	240 hrs	Izolateri (3)[300%]																			
96	Ispitivanje	39 days	Thu 3.8.23	Tue 26.9.23		\$15.888,00	760 hrs																				
97	Ispitivanje cjevovoda	13,5 days	Thu 3.8.23	Tue 22.8.23		\$5.808,00	264 hrs																				
98	Pregled strukture cjevovoda	7 days	Thu 3.8.23	Fri 11.8.23	81FS-10 days	\$2.464,00	112 hrs	Ispitivači/cjevari1 (2)[200%]																			
99	Tlačenje cjevovoda	6 days	Mon 14.8.23	Mon 21.8.23	98	\$2.112,00	96 hrs	Ispitivači/cjevari1 (2)[200%]																			
100	Pregled funkcionalnosti cjevovoda	3,5 days	Thu 17.8.23	Tue 22.8.23	99SS+3 days	\$1.232,00	56 hrs	Ispitivači/cjevari2 (2)[200%]																			
101	Ispitivanje rada strojeva I uređaja	1,5 days	Tue 22.8.23	Wed 23.8.23	100	\$288,00	24 hrs	Ispitivači/Mehaničari (1)[200%]																			
102	Pregled bravarskih radova	8 days	Wed 9.8.23	Mon 21.8.23		\$640,00	64 hrs																				
103	Pregled strukture podnica	2 days	Wed 9.8.23	Fri 11.8.23	83	\$320,00	32 hrs	Kontrolori/Bravari2 (1)[200%]																			
104	Pregled strukture ljestvi	1 day	Wed 9.8.23	Thu 10.8.23	84	\$160,00	16 hrs	Kontrolori/Bravari1 (1)[200%]																			
105	Pregled strukture skala	1 day	Fri 18.8.23	Mon 21.8.23	85	\$160,00	16 hrs	Kontrolori/Bravari2 (1)[200%]																			
106	Ispitivanje električarskih radova	15,5 days	Wed 23.8.23	Wed 13.9.23		\$7.872,00	328 hrs																				
107	Pregled strukture kabelskih staza	3,5 days	Wed 23.8.23	Mon 28.8.23	88	\$1.344,00	56 hrs	Ispitivači/Električari1 (2)[200%]																			
108	Pregled montaže kabela	5 days	Fri 1.9.23	Fri 8.9.23	89	\$1.920,00	80 hrs	Ispitivači/Električari1 (2)[200%]																			
109	Ispitivanje ožičenja kabela	7 days	Mon 28.8.23	Wed 6.9.23	107	\$2.688,00	112 hrs	Ispitivači/Električari2 (2)[200%]																			
110	Test ispitivanja pod naponom	5 days	Wed 6.9.23	Wed 13.9.23	109	\$1.920,00	80 hrs	Ispitivači/Električari2 (2)[200%]																			
111	Ispitivanje limarskih radova	8,5 days	Thu 14.9.23	Tue 26.9.23		\$560,00	56 hrs																				
112	Pregled strukture ventilacije	2 days	Tue 19.9.23	Wed 20.9.23	92FS-2 days	\$160,00	16 hrs	Kontrolori/Limari1 (1)																			
113	Pregled funkcionalnosti ventilacije	4 days	Thu 21.9.23	Tue 26.9.23	112	\$320,00	32 hrs	Kontrolori/Limari1 (1)																			
114	Pregled strukture zaštite strojeva	1 day	Thu 14.9.23	Fri 15.9.23	93	\$80,00	8 hrs	Kontrolori/Limari2 (1)																			
115	Ispitivanje izolaterskih radova	3 days	Tue 19.9.23	Thu 21.9.23		\$720,00	24 hrs																				
116	Pregled montaže izolacije	3 days	Tue 19.9.23	Thu 21.9.23	95	\$720,00	24 hrs	Izolateri (3)																			

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	
