

## Prilog 2

---

Ćosić, Matej

### Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:824190>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2025-02-04**



Repository / Repozitorij:


[Repository of the University of Rijeka, Faculty of Engineering](#)





| ID | Task Name                         | Duration         | Start               | Cost              | Work             | Finish              | Qtr 1, 2023 |     | Qtr 2, 2023 |     |     | Qtr 3, 2023 |     |     |     |
|----|-----------------------------------|------------------|---------------------|-------------------|------------------|---------------------|-------------|-----|-------------|-----|-----|-------------|-----|-----|-----|
|    |                                   |                  |                     |                   |                  |                     | Nov         | Dec | Jan         | Feb | Mar | Apr         | May | Jun | Jul |
| 32 | Montaža temelja 803-002           | 0,33 days        | Fri 23.12.22        | 120,00 €          | 4 hrs            | Fri 23.12.22        |             |     |             |     |     |             |     |     |     |
| 33 | Montaža temelja 803-003           | 0,33 days        | Mon 26.12.22        | 120,00 €          | 4 hrs            | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 34 | Montaža temelja 803-004           | 0,33 days        | Mon 26.12.22        | 120,00 €          | 4 hrs            | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 35 | Montaža temelja 813-001/01        | 0,33 days        | Mon 26.12.22        | 120,00 €          | 4 hrs            | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 36 | Montaža temelja 813-001/02        | 0,33 days        | Tue 27.12.22        | 120,00 €          | 4 hrs            | Tue 27.12.22        |             |     |             |     |     |             |     |     |     |
| 37 | <b>Montaža strojeva I uređaja</b> | <b>9,07 days</b> | <b>Fri 16.12.22</b> | <b>3.916,80 €</b> | <b>108,8 hrs</b> | <b>Thu 29.12.22</b> |             |     |             |     |     |             |     |     |     |
| 38 | Montaža 382-002/01                | 0,27 days        | Fri 16.12.22        | 115,20 €          | 3,2 hrs          | Fri 16.12.22        |             |     |             |     |     |             |     |     |     |
| 39 | Montaža 382-002/02                | 0,27 days        | Fri 16.12.22        | 115,20 €          | 3,2 hrs          | Fri 16.12.22        |             |     |             |     |     |             |     |     |     |
| 40 | Montaža 601-001                   | 0,27 days        | Fri 16.12.22        | 115,20 €          | 3,2 hrs          | Mon 19.12.22        |             |     |             |     |     |             |     |     |     |
| 41 | Montaža 601-019                   | 0,27 days        | Mon 19.12.22        | 115,20 €          | 3,2 hrs          | Mon 19.12.22        |             |     |             |     |     |             |     |     |     |
| 42 | Montaža 631-014                   | 0,27 days        | Mon 19.12.22        | 115,20 €          | 3,2 hrs          | Mon 19.12.22        |             |     |             |     |     |             |     |     |     |
| 43 | Montaža 631-015                   | 0,27 days        | Mon 19.12.22        | 115,20 €          | 3,2 hrs          | Mon 19.12.22        |             |     |             |     |     |             |     |     |     |
| 44 | Montaža 631-016                   | 0,27 days        | Mon 19.12.22        | 115,20 €          | 3,2 hrs          | Tue 20.12.22        |             |     |             |     |     |             |     |     |     |
| 45 | Montaža 631-022                   | 0,27 days        | Tue 20.12.22        | 115,20 €          | 3,2 hrs          | Tue 20.12.22        |             |     |             |     |     |             |     |     |     |
| 46 | Montaža 701-001/01                | 0,27 days        | Tue 20.12.22        | 115,20 €          | 3,2 hrs          | Tue 20.12.22        |             |     |             |     |     |             |     |     |     |
| 47 | Montaža 701-001/02                | 0,27 days        | Tue 20.12.22        | 115,20 €          | 3,2 hrs          | Tue 20.12.22        |             |     |             |     |     |             |     |     |     |
| 48 | Montaža 701-002                   | 0,27 days        | Wed 21.12.22        | 115,20 €          | 3,2 hrs          | Wed 21.12.22        |             |     |             |     |     |             |     |     |     |
| 49 | Montaža 702-002                   | 0,27 days        | Wed 21.12.22        | 115,20 €          | 3,2 hrs          | Wed 21.12.22        |             |     |             |     |     |             |     |     |     |
| 50 | Montaža 702-003                   | 0,27 days        | Wed 21.12.22        | 115,20 €          | 3,2 hrs          | Wed 21.12.22        |             |     |             |     |     |             |     |     |     |
| 51 | Montaža 711-001                   | 0,27 days        | Wed 21.12.22        | 115,20 €          | 3,2 hrs          | Thu 22.12.22        |             |     |             |     |     |             |     |     |     |
| 52 | Montaža 712-002/01                | 0,27 days        | Thu 22.12.22        | 115,20 €          | 3,2 hrs          | Thu 22.12.22        |             |     |             |     |     |             |     |     |     |
| 53 | Montaža 712-002/02                | 0,27 days        | Thu 22.12.22        | 115,20 €          | 3,2 hrs          | Thu 22.12.22        |             |     |             |     |     |             |     |     |     |
| 54 | Montaža 713-001/01                | 0,27 days        | Thu 22.12.22        | 115,20 €          | 3,2 hrs          | Thu 22.12.22        |             |     |             |     |     |             |     |     |     |
| 55 | Montaža 713-001/02                | 0,27 days        | Thu 22.12.22        | 115,20 €          | 3,2 hrs          | Fri 23.12.22        |             |     |             |     |     |             |     |     |     |
| 56 | Montaža 713-009                   | 0,27 days        | Fri 23.12.22        | 115,20 €          | 3,2 hrs          | Fri 23.12.22        |             |     |             |     |     |             |     |     |     |
| 57 | Montaža 721-001/01                | 0,27 days        | Fri 23.12.22        | 115,20 €          | 3,2 hrs          | Fri 23.12.22        |             |     |             |     |     |             |     |     |     |
| 58 | Montaža 721-001/02                | 0,27 days        | Fri 23.12.22        | 115,20 €          | 3,2 hrs          | Fri 23.12.22        |             |     |             |     |     |             |     |     |     |
| 59 | Montaža 721-001/03                | 0,27 days        | Fri 23.12.22        | 115,20 €          | 3,2 hrs          | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 60 | Montaža 756-001/01                | 0,27 days        | Mon 26.12.22        | 115,20 €          | 3,2 hrs          | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 61 | Montaža 756-001/02                | 0,27 days        | Mon 26.12.22        | 115,20 €          | 3,2 hrs          | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |
| 62 | Montaža 756-002/01                | 0,27 days        | Mon 26.12.22        | 115,20 €          | 3,2 hrs          | Mon 26.12.22        |             |     |             |     |     |             |     |     |     |


Montaža strojeva I uređaja

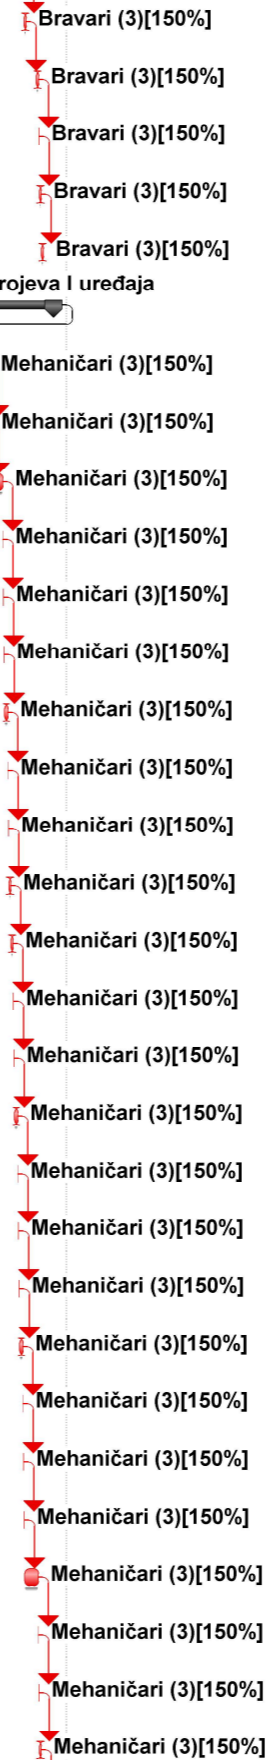

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23

|               |  |                |  |                         |  |                 |  |                  |  |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task          |  | Milestone      |  | Rolled Up Critical Task |  | Split           |  | Group By Summary |  |
| Critical Task |  | Summary        |  | Rolled Up Milestone     |  | External Tasks  |  | Deadline         |  |
| Progress      |  | Rolled Up Task |  | Rolled Up Progress      |  | Project Summary |  |                  |  |


| ID | Task Name                           | Duration           | Start               | Cost               | Work           | Finish             | Qtr 1, 2023 |     |     | Qtr 2, 2023 |     |     | Qtr 3, 2023 |     |     |
|----|-------------------------------------|--------------------|---------------------|--------------------|----------------|--------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|
|    |                                     |                    |                     |                    |                |                    | Nov         | Dec | Jan | Feb         | Mar | Apr | May         | Jun | Jul |
| 63 | Montaža 756-002/02                  | 0,27 days          | Tue 27.12.22        | 115,20 €           | 3,2 hrs        | Tue 27.12.22       |             |     |     |             |     |     |             |     |     |
| 64 | Montaža 756-003                     | 0,27 days          | Tue 27.12.22        | 115,20 €           | 3,2 hrs        | Tue 27.12.22       |             |     |     |             |     |     |             |     |     |
| 65 | Montaža 761-002                     | 0,27 days          | Tue 27.12.22        | 115,20 €           | 3,2 hrs        | Tue 27.12.22       |             |     |     |             |     |     |             |     |     |
| 66 | Montaža 803-001                     | 0,27 days          | Tue 27.12.22        | 115,20 €           | 3,2 hrs        | Wed 28.12.22       |             |     |     |             |     |     |             |     |     |
| 67 | Montaža 803-002                     | 0,27 days          | Wed 28.12.22        | 115,20 €           | 3,2 hrs        | Wed 28.12.22       |             |     |     |             |     |     |             |     |     |
| 68 | Montaža 803-003                     | 0,27 days          | Wed 28.12.22        | 115,20 €           | 3,2 hrs        | Wed 28.12.22       |             |     |     |             |     |     |             |     |     |
| 69 | Montaža 803-004                     | 0,27 days          | Wed 28.12.22        | 115,20 €           | 3,2 hrs        | Wed 28.12.22       |             |     |     |             |     |     |             |     |     |
| 70 | Montaža 813-001/01                  | 0,27 days          | Wed 28.12.22        | 115,20 €           | 3,2 hrs        | Thu 29.12.22       |             |     |     |             |     |     |             |     |     |
| 71 | Montaža 813-001/02                  | 0,27 days          | Thu 29.12.22        | 115,20 €           | 3,2 hrs        | Thu 29.12.22       |             |     |     |             |     |     |             |     |     |
| 72 | <b>Cjevarski radovi</b>             | <b>48,57 days</b>  | <b>Tue 20.12.22</b> | <b>52.360,00 €</b> | <b>680 hrs</b> | <b>Fri 24.2.23</b> |             |     |     |             |     |     |             |     |     |
| 73 | Montaža prolaza                     | 8,57 days          | Tue 20.12.22        | 9.240,00 €         | 120 hrs        | Fri 30.12.22       |             |     |     |             |     |     |             |     |     |
| 74 | Montaža nosača                      | 14,29 days         | Fri 30.12.22        | 15.400,00 €        | 200 hrs        | Fri 20.1.23        |             |     |     |             |     |     |             |     |     |
| 75 | Montaža cijevi                      | 25,71 days         | Fri 20.1.23         | 27.720,00 €        | 360 hrs        | Fri 24.2.23        |             |     |     |             |     |     |             |     |     |
| 76 | <b>Bravarski radovi</b>             | <b>21,33 days</b>  | <b>Fri 13.1.23</b>  | <b>7.680,00 €</b>  | <b>256 hrs</b> | <b>Tue 14.2.23</b> |             |     |     |             |     |     |             |     |     |
| 77 | Montaža podnica                     | 8,67 days          | Fri 13.1.23         | 3.120,00 €         | 104 hrs        | Thu 26.1.23        |             |     |     |             |     |     |             |     |     |
| 78 | Montaža ljestvi                     | 8 days             | Thu 26.1.23         | 2.880,00 €         | 96 hrs         | Tue 7.2.23         |             |     |     |             |     |     |             |     |     |
| 79 | Montaža skala                       | 4,67 days          | Tue 7.2.23          | 1.680,00 €         | 56 hrs         | Tue 14.2.23        |             |     |     |             |     |     |             |     |     |
| 80 | <b>Električarski radovi</b>         | <b>57,14 days</b>  | <b>Fri 24.2.23</b>  | <b>67.200,00 €</b> | <b>800 hrs</b> | <b>Wed 17.5.23</b> |             |     |     |             |     |     |             |     |     |
| 81 | Montaža kablskih prolaza            | 5,71 days          | Fri 24.2.23         | 6.720,00 €         | 80 hrs         | Mon 6.3.23         |             |     |     |             |     |     |             |     |     |
| 82 | Montaža kablskih staza              | 17,14 days         | Mon 6.3.23          | 20.160,00 €        | 240 hrs        | Wed 29.3.23        |             |     |     |             |     |     |             |     |     |
| 83 | Provlačenje kabela                  | 34,29 days         | Wed 29.3.23         | 40.320,00 €        | 480 hrs        | Wed 17.5.23        |             |     |     |             |     |     |             |     |     |
| 84 | <b>Limarski radovi</b>              | <b>28,67 days</b>  | <b>Fri 24.3.23</b>  | <b>9.120,00 €</b>  | <b>304 hrs</b> | <b>Thu 4.5.23</b>  |             |     |     |             |     |     |             |     |     |
| 85 | Montaža ventilacijskih prolaza      | 6,67 days          | Fri 24.3.23         | 2.400,00 €         | 80 hrs         | Tue 4.4.23         |             |     |     |             |     |     |             |     |     |
| 86 | Montaža ventilacijskih kanala       | 14 days            | Fri 7.4.23          | 5.040,00 €         | 168 hrs        | Thu 27.4.23        |             |     |     |             |     |     |             |     |     |
| 87 | Montaža zaštita strojeva I uređaja  | 4,67 days          | Thu 27.4.23         | 1.680,00 €         | 56 hrs         | Thu 4.5.23         |             |     |     |             |     |     |             |     |     |
| 88 | <b>Izolaterski radovi</b>           | <b>10 days</b>     | <b>Thu 27.4.23</b>  | <b>3.600,00 €</b>  | <b>120 hrs</b> | <b>Thu 11.5.23</b> |             |     |     |             |     |     |             |     |     |
| 89 | Montaža izolacije                   | 10 days            | Thu 27.4.23         | 3.600,00 €         | 120 hrs        | Thu 11.5.23        |             |     |     |             |     |     |             |     |     |
| 90 | <b>Ispitivanje</b>                  | <b>101,14 days</b> | <b>Thu 26.1.23</b>  | <b>26.880,00 €</b> | <b>760 hrs</b> | <b>Fri 16.6.23</b> |             |     |     |             |     |     |             |     |     |
| 91 | Ispitivanje rada strojeva I uređaja | 1,5 days           | Wed 15.2.23         | 576,00 €           | 24 hrs         | Fri 17.2.23        |             |     |     |             |     |     |             |     |     |
| 92 | <b>Ispitivanje cjevovoda</b>        | <b>24,81 days</b>  | <b>Fri 10.2.23</b>  | <b>11.616,00 €</b> | <b>264 hrs</b> | <b>Fri 17.3.23</b> |             |     |     |             |     |     |             |     |     |
| 93 | Pregled strukture cjevovoda         | 10,53 days         | Fri 10.2.23         | 4.928,00 €         | 112 hrs        | Mon 27.2.23        |             |     |     |             |     |     |             |     |     |

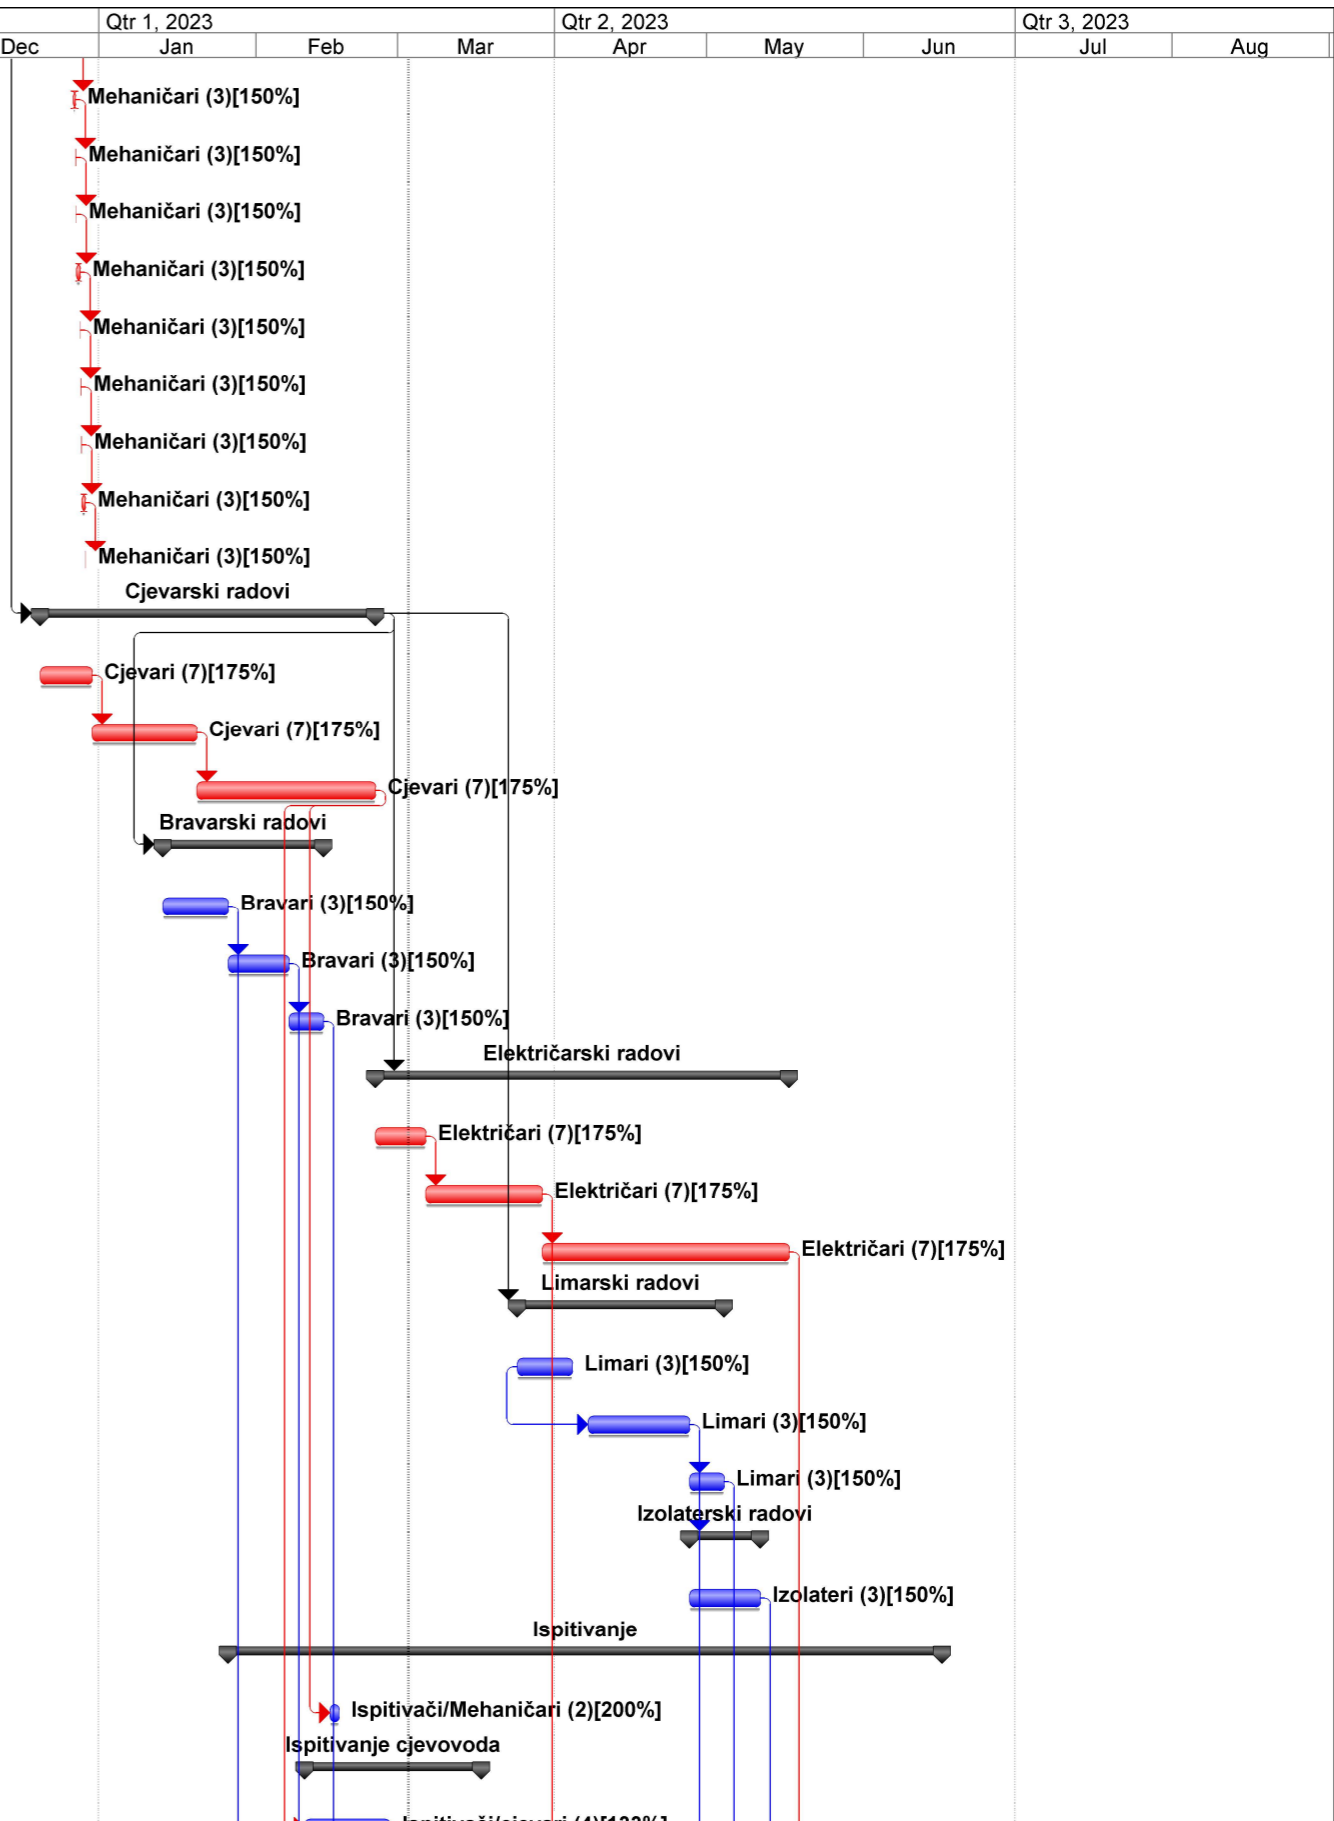

Project: Popis aktivnosti za opremanje  
Date: Fri 3.3.23

|               |  |                |  |                         |  |                 |  |                  |  |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task          |  | Milestone      |  | Rolled Up Critical Task |  | Split           |  | Group By Summary |  |
| Critical Task |  | Summary        |  | Rolled Up Milestone     |  | External Tasks  |  | Deadline         |  |
| Progress      |  | Rolled Up Task |  | Rolled Up Progress      |  | Project Summary |  |                  |  |

| ID  | Task Name                                | Duration          | Start              | Cost               | Work           | Finish             | Timeline |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
|-----|--|-------------------|--------------------|--------------------|----------------|--------------------|----------|-----|-------------|--|--|-------------|--|--|-------------|--|--|--|--|--|--|--|
|     |  |                   |                    |                    |                |                    | Nov      | Dec | Qtr 1, 2023 |  |  | Qtr 2, 2023 |  |  | Qtr 3, 2023 |  |  |  |  |  |  |  |
| 94  | Tlačenje cjevovoda                       | 9,02 days         | Mon 27.2.23        | 4.224,00 €         | 96 hrs         | Fri 10.3.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 95  | Pregled funkcionalnosti cjevovoda        | 5,26 days         | Fri 10.3.23        | 2.464,00 €         | 56 hrs         | Fri 17.3.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 96  | <b>Pregled bravarskih radova</b>         | <b>13,67 days</b> | <b>Thu 26.1.23</b> | <b>1.280,00 €</b>  | <b>64 hrs</b>  | <b>Wed 15.2.23</b> |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 97  | Pregled strukture podnica                | 2 days            | Thu 26.1.23        | 640,00 €           | 32 hrs         | Mon 30.1.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 98  | Pregled strukture ljestvi                | 1 day             | Tue 7.2.23         | 320,00 €           | 16 hrs         | Wed 8.2.23         |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 99  | Pregled strukture skala                  | 1 day             | Tue 14.2.23        | 320,00 €           | 16 hrs         | Wed 15.2.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 100 | <b>Ispitivanje električarskih radova</b> | <b>56,95 days</b> | <b>Wed 29.3.23</b> | <b>11.808,00 €</b> | <b>328 hrs</b> | <b>Fri 16.6.23</b> |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 101 | Pregled strukture kablskih staza         | 4,67 days         | Wed 29.3.23        | 2.016,00 €         | 56 hrs         | Wed 5.4.23         |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 102 | Pregled montaže kabela                   | 6,67 days         | Wed 17.5.23        | 2.880,00 €         | 80 hrs         | Thu 25.5.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 103 | Ispitivanje ožičenja kabela              | 9,33 days         | Thu 25.5.23        | 4.032,00 €         | 112 hrs        | Thu 8.6.23         |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 104 | Test ispitivanja pod naponom             | 6,67 days         | Thu 8.6.23         | 2.880,00 €         | 80 hrs         | Fri 16.6.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 105 | <b>Ispitivanje limarskih radova</b>      | <b>5,17 days</b>  | <b>Thu 27.4.23</b> | <b>1.120,00 €</b>  | <b>56 hrs</b>  | <b>Fri 5.5.23</b>  |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 106 | Pregled strukture ventilacije            | 1 day             | Thu 27.4.23        | 320,00 €           | 16 hrs         | Fri 28.4.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 107 | Pregled funkcionalnosti ventilacije      | 2 days            | Fri 28.4.23        | 640,00 €           | 32 hrs         | Tue 2.5.23         |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 108 | Pregled strukture zaštite strojeva       | 0,5 days          | Thu 4.5.23         | 160,00 €           | 8 hrs          | Fri 5.5.23         |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 109 | <b>Ispitivanje izolaterskih radova</b>   | <b>1,5 days</b>   | <b>Thu 11.5.23</b> | <b>480,00 €</b>    | <b>24 hrs</b>  | <b>Mon 15.5.23</b> |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |
| 110 | Pregled montaže izolacije                | 1,5 days          | Thu 11.5.23        | 480,00 €           | 24 hrs         | Mon 15.5.23        |          |     |             |  |  |             |  |  |             |  |  |  |  |  |  |  |

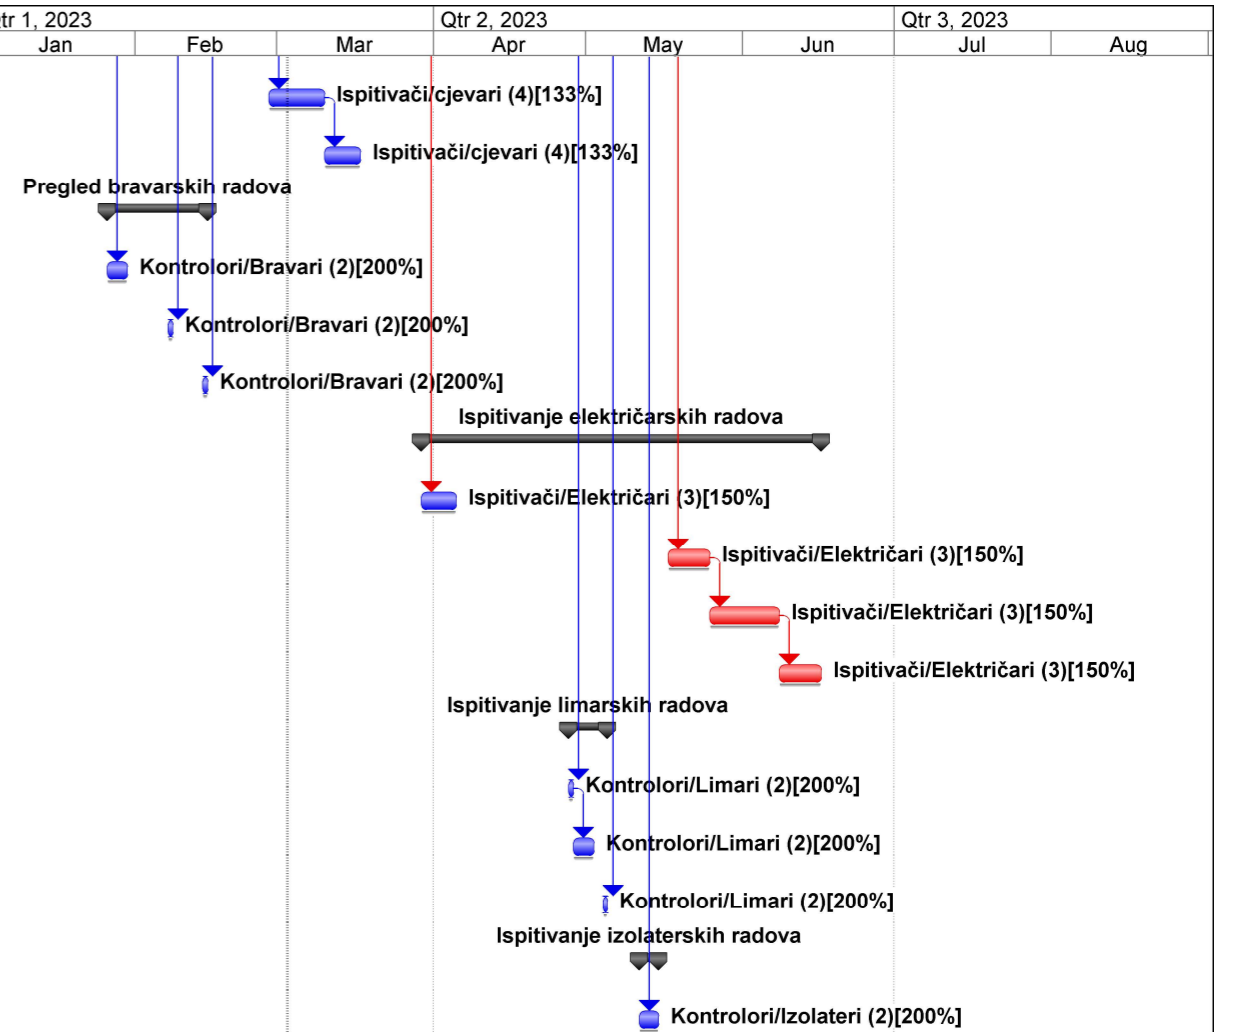

|  |               |  |                |  |                         |  |                 |  |                  |  |
|--|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Project: Popis aktivnosti za opremanje<br>Date: Fri 3.3.23 | Task          |  | Milestone      |  | Rolled Up Critical Task |  | Split           |  | Group By Summary |  |
|  | Critical Task |  | Summary        |  | Rolled Up Milestone     |  | External Tasks  |  | Deadline         |  |
|  | Progress      |  | Rolled Up Task |  | Rolled Up Progress      |  | Project Summary |  |                  |  |
