

Prilog - treći slučaj

Butorac, Lovro

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:797667>

Rights / Prava: [In copyright](#)/[Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-09-06**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jun '23				Jul '23				Aug '23				Sep '23				Oct '23			
									4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15
1	OPREMANJE 2. PLATFORME STROJARNICE	73,38 days	Thu 6.7.23	Tue 17.10.23		\$245.488,00	4.588 hrs		OPREMANJE 2. PLATFORME STROJARNICE																			
2	Montaža temelja	13,88 days	Thu 6.7.23	Tue 25.7.23		\$17.760,00	444 hrs		Montaža temelja																			
3	Montaža temelja 445-003	0,38 days	Thu 6.7.23	Thu 6.7.23		\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 445-003 F B																			
4	Montaža temelja 445-004	0,38 days	Thu 6.7.23	Thu 6.7.23	3	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 445-004 F B																			
5	Montaža temelja 452-001	0,38 days	Thu 6.7.23	Fri 7.7.23	4	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 452-001 F B																			
6	Montaža temelja 452-005	0,38 days	Fri 7.7.23	Fri 7.7.23	5	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 452-005 F B																			
7	Montaža temelja 581-001	0,38 days	Fri 7.7.23	Fri 7.7.23	6	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-001 F B																			
8	Montaža temelja 581-002	0,38 days	Fri 7.7.23	Mon 10.7.23	7	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-002 F B																			
9	Montaža temelja 581-003	0,38 days	Mon 10.7.23	Mon 10.7.23	8	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 581-003 F B																			
10	Montaža temelja 582-001	0,38 days	Mon 10.7.23	Mon 10.7.23	9	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-001 F B																			
11	Montaža temelja 582-003/01	0,38 days	Tue 11.7.23	Tue 11.7.23	10	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-003/01 F B																			
12	Montaža temelja 582-003/02	0,38 days	Tue 11.7.23	Tue 11.7.23	11	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 582-003/02 F B																			
13	Montaža temelja 644-008/01	0,38 days	Tue 11.7.23	Wed 12.7.23	12	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 644-008/01 F B																			
14	Montaža temelja 644-008/02	0,38 days	Wed 12.7.23	Wed 12.7.23	13	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 644-008/02 F B																			
15	Montaža temelja 651-001	0,38 days	Wed 12.7.23	Wed 12.7.23	14	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-001 F B																			
16	Montaža temelja 651-002	0,38 days	Wed 12.7.23	Thu 13.7.23	15	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-002 F B																			
17	Montaža temelja 651-003	0,38 days	Thu 13.7.23	Thu 13.7.23	16	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 651-003 F B																			
18	Montaža temelja 702-001	0,38 days	Thu 13.7.23	Thu 13.7.23	17	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-001 F B																			
19	Montaža temelja 702-004	0,38 days	Fri 14.7.23	Fri 14.7.23	18	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-004 F B																			
20	Montaža temelja 702-005	0,38 days	Fri 14.7.23	Fri 14.7.23	19	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 702-005 F B																			
21	Montaža temelja 703-001	0,38 days	Fri 14.7.23	Mon 17.7.23	20	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 703-001 F B																			
22	Montaža temelja 703-002	0,38 days	Mon 17.7.23	Mon 17.7.23	21	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 703-002 F B																			
23	Montaža temelja 712-001	0,38 days	Mon 17.7.23	Mon 17.7.23	22	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 712-001 F B																			
24	Montaža temelja 713-007	0,38 days	Mon 17.7.23	Tue 18.7.23	23	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 713-007 F B																			
25	Montaža temelja 714-001	0,38 days	Tue 18.7.23	Tue 18.7.23	24	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 714-001 F B																			
26	Montaža temelja 756-001/02	0,38 days	Tue 18.7.23	Tue 18.7.23	25	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 756-001/02 F B																			
27	Montaža temelja 722-011	0,38 days	Wed 19.7.23	Wed 19.7.23	26	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 722-011 F B																			
28	Montaža temelja 731-001/01	0,38 days	Wed 19.7.23	Wed 19.7.23	27	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-001/01 F B																			
29	Montaža temelja 731-001/02	0,38 days	Wed 19.7.23	Thu 20.7.23	28	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-001/02 F B																			
30	Montaža temelja 731-002	0,38 days	Thu 20.7.23	Thu 20.7.23	29	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-002 F B																			
31	Montaža temelja 731-003/01	0,38 days	Thu 20.7.23	Thu 20.7.23	30	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-003/01 F B																			

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23


Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23				Aug '23				Sep '23				Oct '23							
									4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15
32	Montaža temelja 731-003/01	0,38 days	Thu 20.7.23	Fri 21.7.23	31	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 731-003/01 B																			
33	Montaža temelja 733-001	0,38 days	Fri 21.7.23	Fri 21.7.23	32	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 733-001 B																			
34	Montaža temelja 733-012	0,38 days	Fri 21.7.23	Fri 21.7.23	33	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 733-012 B																			
35	Montaža temelja 734-001	0,38 days	Mon 24.7.23	Mon 24.7.23	34	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 734-001 B																			
36	Montaža temelja 743-002	0,38 days	Mon 24.7.23	Mon 24.7.23	35	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 743-002 B																			
37	Montaža temelja 743-003	0,38 days	Mon 24.7.23	Tue 25.7.23	36	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 743-003 B																			
38	Montaža temelja 751-001	0,38 days	Tue 25.7.23	Tue 25.7.23	37	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 751-001 B																			
39	Montaža temelja 756-004	0,38 days	Tue 25.7.23	Tue 25.7.23	38	\$480,00	12 hrs	Bravari (4)[400%]	Montaža temelja 756-004 B																			
40	Montaža strojeva I uređaja	9,25 days	Mon 17.7.23	Mon 31.7.23	2FS-6 days	\$14.208,00	296 hrs		Montaža strojeva I uređaja																			
41	Montaža 445-003	0,25 days	Mon 17.7.23	Tue 18.7.23		\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 445-003 M																			
42	Montaža 445-004	0,25 days	Tue 18.7.23	Tue 18.7.23	41	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 445-004 M																			
43	Montaža 452-001	0,25 days	Tue 18.7.23	Tue 18.7.23	42	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 452-001 M																			
44	Montaža 452-005	0,25 days	Tue 18.7.23	Tue 18.7.23	43	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 452-005 M																			
45	Montaža 581-001	0,25 days	Tue 18.7.23	Wed 19.7.23	44	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 581-001 M																			
46	Montaža 581-002	0,25 days	Wed 19.7.23	Wed 19.7.23	45	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 581-002 M																			
47	Montaža 581-003	0,25 days	Wed 19.7.23	Wed 19.7.23	46	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 581-003 M																			
48	Montaža 582-001	0,25 days	Wed 19.7.23	Wed 19.7.23	47	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 582-001 M																			
49	Montaža 582-003/01	0,25 days	Wed 19.7.23	Thu 20.7.23	48	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 582-003/01 M																			
50	Montaža 582-003/02	0,25 days	Thu 20.7.23	Thu 20.7.23	49	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 582-003/02 M																			
51	Montaža 644-008/01	0,25 days	Thu 20.7.23	Thu 20.7.23	50	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 644-008/01 M																			
52	Montaža 644-008/02	0,25 days	Thu 20.7.23	Thu 20.7.23	51	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 644-008/02 M																			
53	Montaža 651-001	0,25 days	Thu 20.7.23	Fri 21.7.23	52	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 651-001 M																			
54	Montaža 651-002	0,25 days	Fri 21.7.23	Fri 21.7.23	53	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 651-002 M																			
55	Montaža 651-003	0,25 days	Fri 21.7.23	Fri 21.7.23	54	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 651-003 M																			
56	Montaža 702-001	0,25 days	Fri 21.7.23	Fri 21.7.23	55	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 702-001 M																			
57	Montaža 702-004	0,25 days	Fri 21.7.23	Mon 24.7.23	56	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 702-004 M																			
58	Montaža 702-005	0,25 days	Mon 24.7.23	Mon 24.7.23	57	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 702-005 M																			
59	Montaža 703-001	0,25 days	Mon 24.7.23	Mon 24.7.23	58	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 703-001 M																			
60	Montaža 703-002	0,25 days	Mon 24.7.23	Mon 24.7.23	59	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 703-002 M																			
61	Montaža 712-001	0,25 days	Mon 24.7.23	Tue 25.7.23	60	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 712-001 M																			
62	Montaža 713-007	0,25 days	Tue 25.7.23	Tue 25.7.23	61	\$384,00	8 hrs	Mehaničari (4)[400%]	Montaža 713-007 M																			

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	n '23				Jul '23				Aug '23				Sep '23				Oct '23			
									4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15
63	Montaža 714-001	0,25 days	Tue 25.7.23	Tue 25.7.23	62	\$384,00	8 hrs	Mehaničari (4)[400%]																				
64	Montaža 756-001/02	0,25 days	Tue 25.7.23	Tue 25.7.23	63	\$384,00	8 hrs	Mehaničari (4)[400%]																				
65	Montaža 722-011	0,25 days	Tue 25.7.23	Wed 26.7.23	64	\$384,00	8 hrs	Mehaničari (4)[400%]																				
66	Montaža 731-001/01	0,25 days	Wed 26.7.23	Wed 26.7.23	65	\$384,00	8 hrs	Mehaničari (4)[400%]																				
67	Montaža 731-001/02	0,25 days	Wed 26.7.23	Wed 26.7.23	66	\$384,00	8 hrs	Mehaničari (4)[400%]																				
68	Montaža 731-002	0,25 days	Wed 26.7.23	Wed 26.7.23	67	\$384,00	8 hrs	Mehaničari (4)[400%]																				
69	Montaža 731-003/01	0,25 days	Wed 26.7.23	Thu 27.7.23	68	\$384,00	8 hrs	Mehaničari (4)[400%]																				
70	Montaža 731-003/01	0,25 days	Thu 27.7.23	Thu 27.7.23	69	\$384,00	8 hrs	Mehaničari (4)[400%]																				
71	Montaža 733-001	0,25 days	Thu 27.7.23	Thu 27.7.23	70	\$384,00	8 hrs	Mehaničari (4)[400%]																				
72	Montaža 733-012	0,25 days	Thu 27.7.23	Thu 27.7.23	71	\$384,00	8 hrs	Mehaničari (4)[400%]																				
73	Montaža 734-001	0,25 days	Thu 27.7.23	Fri 28.7.23	72	\$384,00	8 hrs	Mehaničari (4)[400%]																				
74	Montaža 743-002	0,25 days	Fri 28.7.23	Fri 28.7.23	73	\$384,00	8 hrs	Mehaničari (4)[400%]																				
75	Montaža 743-003	0,25 days	Fri 28.7.23	Fri 28.7.23	74	\$384,00	8 hrs	Mehaničari (4)[400%]																				
76	Montaža 751-001	0,25 days	Fri 28.7.23	Fri 28.7.23	75	\$384,00	8 hrs	Mehaničari (4)[400%]																				
77	Montaža 756-004	0,25 days	Fri 28.7.23	Mon 31.7.23	76	\$384,00	8 hrs	Mehaničari (4)[400%]																				
78	Cjevarski radovi	18,5 days	Thu 20.7.23	Tue 15.8.23	40FS-7 days	\$58.608,00	888 hrs																					
79	Montaža prolaza	3,5 days	Thu 20.7.23	Tue 25.7.23		\$11.088,00	168 hrs	Cjevari (6)[600%]																				
80	Montaža nosača	5 days	Tue 25.7.23	Tue 1.8.23	79	\$15.840,00	240 hrs	Cjevari (6)[600%]																				
81	Montaža cijevi	10 days	Tue 1.8.23	Tue 15.8.23	80	\$31.680,00	480 hrs	Cjevari (6)[600%]																				
82	Bravarski radovi	13,25 days	Wed 26.7.23	Mon 14.8.23	78FS-14 days	\$16.960,00	424 hrs																					
83	Montaža podnica	5,25 days	Wed 26.7.23	Wed 2.8.23		\$6.720,00	168 hrs	Bravari (4)[400%]																				
84	Montaža ljestvi	4,5 days	Wed 2.8.23	Wed 9.8.23	83	\$5.760,00	144 hrs	Bravari (4)[400%]																				
85	Montaža skala	3,5 days	Wed 9.8.23	Mon 14.8.23	84	\$4.480,00	112 hrs	Bravari (4)[400%]																				
86	Električarski radovi	23,5 days	Tue 1.8.23	Mon 4.9.23	80	\$81.216,00	1.128 hrs																					
87	Montaža kablskih prolaza	3,5 days	Tue 1.8.23	Mon 7.8.23		\$12.096,00	168 hrs	Električari (6)[600%]																				
88	Montaža kablskih staza	7,5 days	Mon 7.8.23	Wed 16.8.23	87	\$25.920,00	360 hrs	Električari (6)[600%]																				
89	Provlačenje kabela	12,5 days	Wed 16.8.23	Mon 4.9.23	88	\$43.200,00	600 hrs	Električari (6)[600%]																				
90	Limarski radovi	44,25 days	Tue 15.8.23	Mon 16.10.23	78	\$16.320,00	408 hrs																					
91	Montaža ventilacijskih prolaza	3,5 days	Tue 15.8.23	Mon 21.8.23		\$4.480,00	112 hrs	Limari (4)[400%]																				
92	Montaža ventilacijskih kanala	7,5 days	Mon 4.9.23	Thu 14.9.23	91SS+14 days	\$9.600,00	240 hrs	Limari (4)[400%]																				
93	Montaža zaštite strojeva I uređaja	1,75 days	Fri 13.10.23	Mon 16.10.23	92FS+21 days	\$2.240,00	56 hrs	Limari (4)[400%]																				

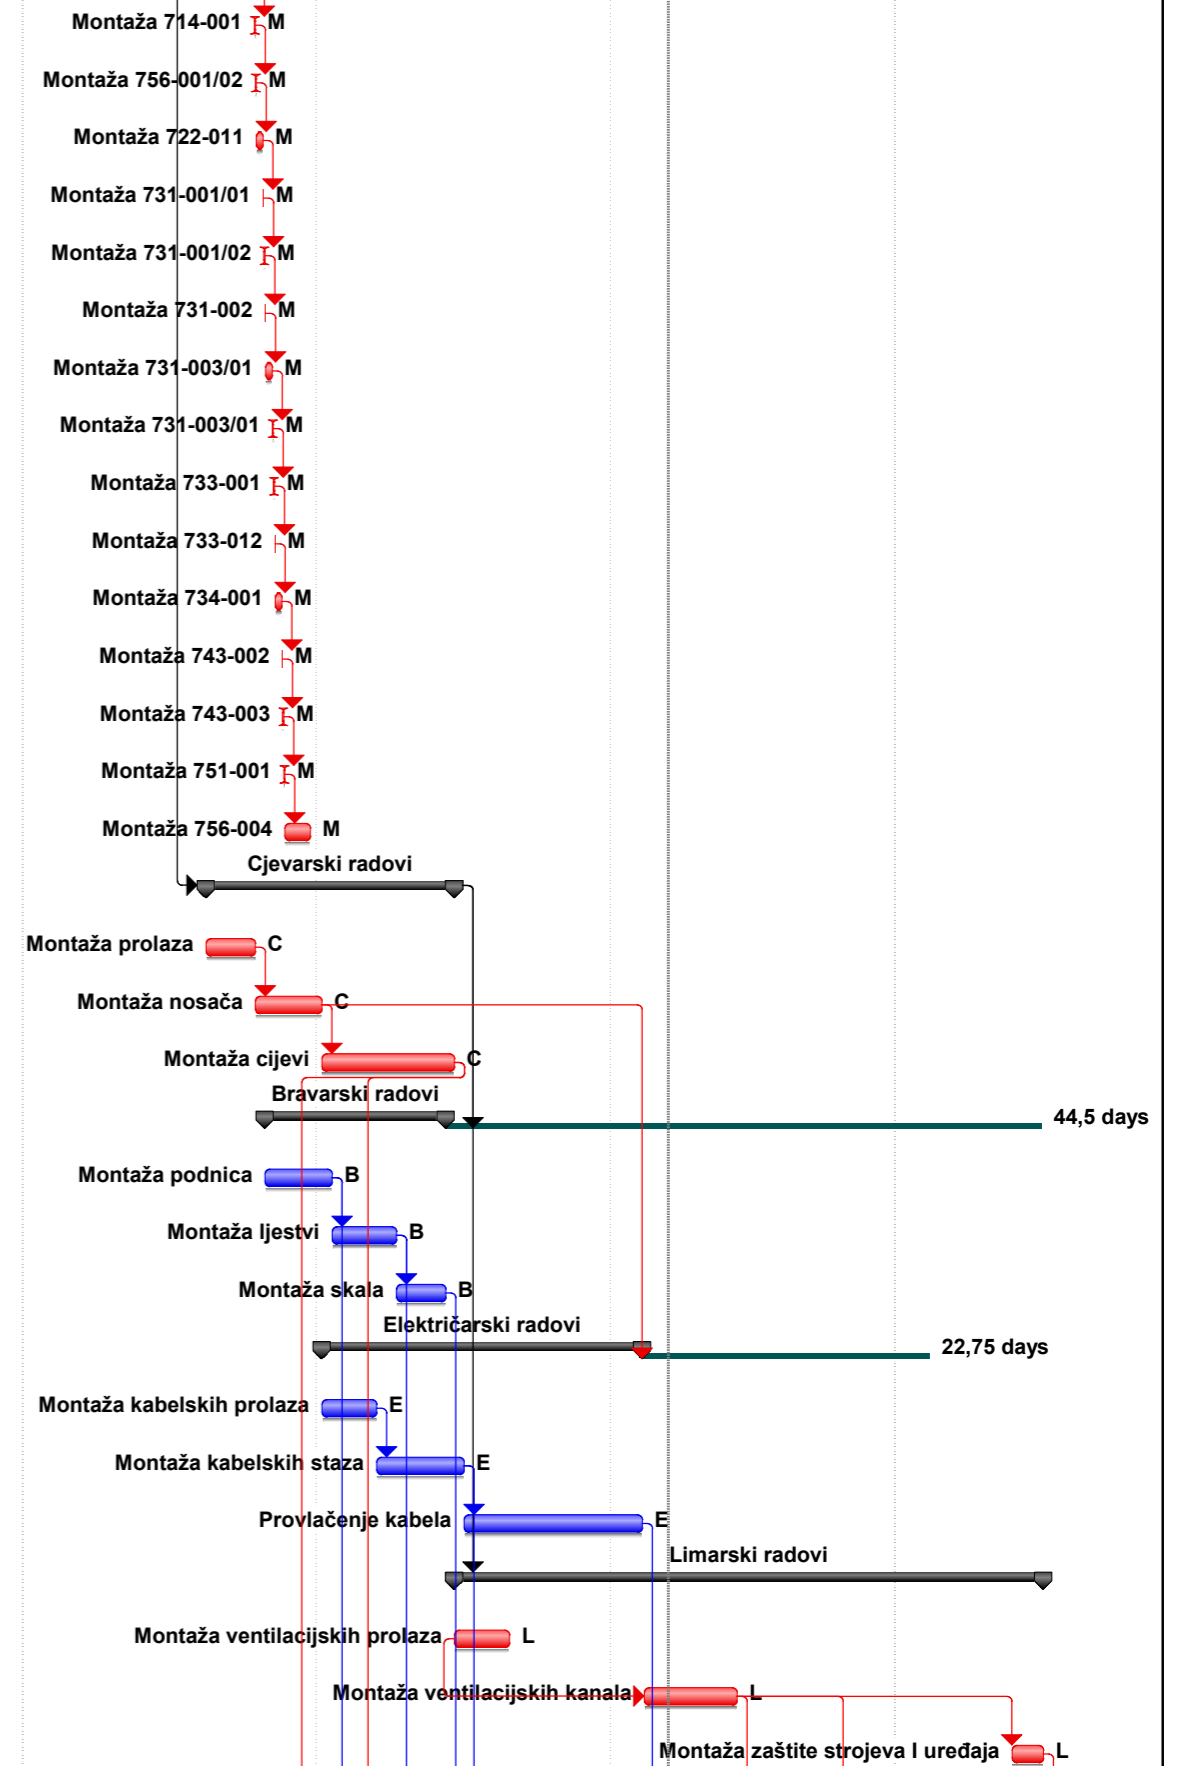

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Legend:

- Critical: Red bar
- Critical Split: Red bar with dashed line
- Task: Blue bar
- Split: Dotted line
- Progress: Grey bar with diagonal lines
- Milestone: Diamond
- Slack: Dotted line
- Slippage: Grey bar with diagonal lines
- Summary: Black bar
- Project Summary: Green bar
- Rolled Up Critical: Green bar with diagonal lines
- Rolled Up Critical (2): Grey bar with diagonal lines
- External Tasks: Grey bar with diagonal lines
- External Milestone: Diamond
- Deadline: Green bar with downward arrow

Page 3

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	n '23				Jul '23				Aug '23				Sep '23			Oct '23				
									4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15
94	Izolaterski radovi	7,5 days	Thu 14.9.23	Mon 25.9.23	92	\$9.600,00	240 hrs																					
95	Montaža izolacije	7,5 days	Thu 14.9.23	Mon 25.9.23		\$9.600,00	240 hrs	Izolateri (4)[400%]																				
96	Ispitivanje	54,75 days	Tue 1.8.23	Tue 17.10.23		\$30.816,00	760 hrs																					
97	Ispitivanje rada strojeva I uređaja	1,5 days	Tue 8.8.23	Thu 10.8.23	81FS-5 days	\$576,00	24 hrs	Ispitivači/Mehaničari (2)[200%]																				
98	Ispitivanje cjevovoda	8,25 days	Tue 1.8.23	Fri 11.8.23		\$11.616,00	264 hrs																					
99	Pregled strukture cjevovoda	3,5 days	Tue 1.8.23	Mon 7.8.23	81FS-10 days	\$4.928,00	112 hrs	Ispitivači/cjevvari (4)[400%]																				
100	Tlačenje cjevovoda	3 days	Mon 7.8.23	Thu 10.8.23	99	\$4.224,00	96 hrs	Ispitivači/cjevvari (4)[400%]																				
101	Pregled funkcionalnosti cjevovoda	1,75 days	Thu 10.8.23	Fri 11.8.23	100	\$2.464,00	56 hrs	Ispitivači/cjevvari (4)[400%]																				
102	Pregled bravarskih radova	9 days	Wed 2.8.23	Tue 15.8.23		\$1.280,00	64 hrs																					
103	Pregled strukture podnica	2 days	Wed 2.8.23	Fri 4.8.23	83	\$640,00	32 hrs	Kontrolori/Bravari (2)[200%]																				
104	Pregled strukture ljestvi	1 day	Wed 9.8.23	Thu 10.8.23	84	\$320,00	16 hrs	Kontrolori/Bravari (2)[200%]																				
105	Pregled strukture skala	1 day	Mon 14.8.23	Tue 15.8.23	85	\$320,00	16 hrs	Kontrolori/Bravari (2)[200%]																				
106	Ispitivanje električarskih radova	21 days	Wed 16.8.23	Thu 14.9.23		\$15.744,00	328 hrs																					
107	Pregled strukture kablskih staza	1,75 days	Wed 16.8.23	Fri 18.8.23	88	\$2.688,00	56 hrs	Ispitivači/Električari (4)[400%]																				
108	Pregled montaže kabela	2,5 days	Mon 4.9.23	Wed 6.9.23	89	\$3.840,00	80 hrs	Ispitivači/Električari (4)[400%]																				
109	Ispitivanje ožičenja kabela	3,5 days	Wed 6.9.23	Tue 12.9.23	108	\$5.376,00	112 hrs	Ispitivači/Električari (4)[400%]																				
110	Test ispitivanja pod naponom	2,5 days	Tue 12.9.23	Thu 14.9.23	109	\$3.840,00	80 hrs	Ispitivači/Električari (4)[400%]																				
111	Ispitivanje limarskih radova	23,25 days	Thu 14.9.23	Tue 17.10.23		\$1.120,00	56 hrs																					
112	Pregled strukture ventilacije	1 day	Thu 14.9.23	Fri 15.9.23	92	\$320,00	16 hrs	Kontrolori/Limari (2)[200%]																				
113	Pregled funkcionalnosti ventilacije	2 days	Fri 15.9.23	Tue 19.9.23	112	\$640,00	32 hrs	Kontrolori/Limari (2)[200%]																				
114	Pregled strukture zaštite strojeva	0,5 days	Mon 16.10.23	Tue 17.10.23	93	\$160,00	8 hrs	Kontrolori/Limari (2)[200%]																				
115	Ispitivanje izolaterskih radova	1,5 days	Mon 25.9.23	Wed 27.9.23		\$480,00	24 hrs																					
116	Pregled montaže izolacije	1,5 days	Mon 25.9.23	Wed 27.9.23	95	\$480,00	24 hrs	Kontrolori/Izolateri (2)[200%]																				

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	
