

Prilog - treći slučaj

Butorac, Lovro

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:797667>

Rights / Prava: [In copyright](#)/[Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2025-01-26**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



| ID | Task Name | Duration | Start | Finish | Predecessors | Cost | Work | Resources | Jun '23 | | | | Jul '23 | | | | Aug '23 | | | | Sep '23 | | | | Oct '23 | | | |
|----|---|-------------------|-------------------|---------------------|--------------|---------------------|------------------|-------------------|---|----|----|----|---------|---|----|----|---------|---|----|----|---------|---|----|----|---------|---|---|----|
| | | | | | | | | | 4 | 11 | 18 | 25 | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 3 | 10 | 17 | 24 | 1 | 8 | 15 |
| 1 | OPREMANJE 2. PLATFORME STROJARNICE | 73,38 days | Thu 6.7.23 | Tue 17.10.23 | | \$245.488,00 | 4.588 hrs | | OPREMANJE 2. PLATFORME STROJARNICE | | | | | | | | | | | | | | | | | | | |
| 2 | Montaža temelja | 13,88 days | Thu 6.7.23 | Tue 25.7.23 | | \$17.760,00 | 444 hrs | | Montaža temelja | | | | | | | | | | | | | | | | | | | |
| 3 | Montaža temelja 445-003 | 0,38 days | Thu 6.7.23 | Thu 6.7.23 | | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 445-003 F B | | | | | | | | | | | | | | | | | | | |
| 4 | Montaža temelja 445-004 | 0,38 days | Thu 6.7.23 | Thu 6.7.23 | 3 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 445-004 F B | | | | | | | | | | | | | | | | | | | |
| 5 | Montaža temelja 452-001 | 0,38 days | Thu 6.7.23 | Fri 7.7.23 | 4 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 452-001 F B | | | | | | | | | | | | | | | | | | | |
| 6 | Montaža temelja 452-005 | 0,38 days | Fri 7.7.23 | Fri 7.7.23 | 5 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 452-005 F B | | | | | | | | | | | | | | | | | | | |
| 7 | Montaža temelja 581-001 | 0,38 days | Fri 7.7.23 | Fri 7.7.23 | 6 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 581-001 F B | | | | | | | | | | | | | | | | | | | |
| 8 | Montaža temelja 581-002 | 0,38 days | Fri 7.7.23 | Mon 10.7.23 | 7 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 581-002 F B | | | | | | | | | | | | | | | | | | | |
| 9 | Montaža temelja 581-003 | 0,38 days | Mon 10.7.23 | Mon 10.7.23 | 8 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 581-003 F B | | | | | | | | | | | | | | | | | | | |
| 10 | Montaža temelja 582-001 | 0,38 days | Mon 10.7.23 | Mon 10.7.23 | 9 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 582-001 F B | | | | | | | | | | | | | | | | | | | |
| 11 | Montaža temelja 582-003/01 | 0,38 days | Tue 11.7.23 | Tue 11.7.23 | 10 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 582-003/01 F B | | | | | | | | | | | | | | | | | | | |
| 12 | Montaža temelja 582-003/02 | 0,38 days | Tue 11.7.23 | Tue 11.7.23 | 11 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 582-003/02 F B | | | | | | | | | | | | | | | | | | | |
| 13 | Montaža temelja 644-008/01 | 0,38 days | Tue 11.7.23 | Wed 12.7.23 | 12 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 644-008/01 F B | | | | | | | | | | | | | | | | | | | |
| 14 | Montaža temelja 644-008/02 | 0,38 days | Wed 12.7.23 | Wed 12.7.23 | 13 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 644-008/02 F B | | | | | | | | | | | | | | | | | | | |
| 15 | Montaža temelja 651-001 | 0,38 days | Wed 12.7.23 | Wed 12.7.23 | 14 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 651-001 F B | | | | | | | | | | | | | | | | | | | |
| 16 | Montaža temelja 651-002 | 0,38 days | Wed 12.7.23 | Thu 13.7.23 | 15 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 651-002 F B | | | | | | | | | | | | | | | | | | | |
| 17 | Montaža temelja 651-003 | 0,38 days | Thu 13.7.23 | Thu 13.7.23 | 16 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 651-003 F B | | | | | | | | | | | | | | | | | | | |
| 18 | Montaža temelja 702-001 | 0,38 days | Thu 13.7.23 | Thu 13.7.23 | 17 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 702-001 F B | | | | | | | | | | | | | | | | | | | |
| 19 | Montaža temelja 702-004 | 0,38 days | Fri 14.7.23 | Fri 14.7.23 | 18 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 702-004 F B | | | | | | | | | | | | | | | | | | | |
| 20 | Montaža temelja 702-005 | 0,38 days | Fri 14.7.23 | Fri 14.7.23 | 19 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 702-005 F B | | | | | | | | | | | | | | | | | | | |
| 21 | Montaža temelja 703-001 | 0,38 days | Fri 14.7.23 | Mon 17.7.23 | 20 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 703-001 F B | | | | | | | | | | | | | | | | | | | |
| 22 | Montaža temelja 703-002 | 0,38 days | Mon 17.7.23 | Mon 17.7.23 | 21 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 703-002 F B | | | | | | | | | | | | | | | | | | | |
| 23 | Montaža temelja 712-001 | 0,38 days | Mon 17.7.23 | Mon 17.7.23 | 22 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 712-001 F B | | | | | | | | | | | | | | | | | | | |
| 24 | Montaža temelja 713-007 | 0,38 days | Mon 17.7.23 | Tue 18.7.23 | 23 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 713-007 F B | | | | | | | | | | | | | | | | | | | |
| 25 | Montaža temelja 714-001 | 0,38 days | Tue 18.7.23 | Tue 18.7.23 | 24 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 714-001 F B | | | | | | | | | | | | | | | | | | | |
| 26 | Montaža temelja 756-001/02 | 0,38 days | Tue 18.7.23 | Tue 18.7.23 | 25 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 756-001/02 F B | | | | | | | | | | | | | | | | | | | |
| 27 | Montaža temelja 722-011 | 0,38 days | Wed 19.7.23 | Wed 19.7.23 | 26 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 722-011 F B | | | | | | | | | | | | | | | | | | | |
| 28 | Montaža temelja 731-001/01 | 0,38 days | Wed 19.7.23 | Wed 19.7.23 | 27 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 731-001/01 F B | | | | | | | | | | | | | | | | | | | |
| 29 | Montaža temelja 731-001/02 | 0,38 days | Wed 19.7.23 | Thu 20.7.23 | 28 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 731-001/02 F B | | | | | | | | | | | | | | | | | | | |
| 30 | Montaža temelja 731-002 | 0,38 days | Thu 20.7.23 | Thu 20.7.23 | 29 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 731-002 F B | | | | | | | | | | | | | | | | | | | |
| 31 | Montaža temelja 731-003/01 | 0,38 days | Thu 20.7.23 | Thu 20.7.23 | 30 | \$480,00 | 12 hrs | Bravari (4)[400%] | Montaža temelja 731-003/01 F B | | | | | | | | | | | | | | | | | | | |

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23


| | | | | | | | | | |
|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Critical | | Split | | Slack | | Project Summary | | External Tasks | |
| Critical Split | | Progress | | Slippage | | Rolled Up Critical | | External Milestone | |
| Task | | Milestone | | Summary | | Rolled Up Critical | | Deadline | |

| ID | Task Name | Duration | Start | Finish | Predecessors | Cost | Work | Resources | Jun '23 | | | | Jul '23 | | | | Aug '23 | | | | Sep '23 | | | | Oct '23 | | | | | | | |
|----|-----------------------------------|------------------|--------------------|--------------------|-------------------|--------------------|----------------|----------------------|---------|----|----|----|---------|---|----|----|---------|---|----|----|---------|---|----|----|---------|---|---|----|----|--|--|--|
| | | | | | | | | | 4 | 11 | 18 | 25 | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 3 | 10 | 17 | 24 | 1 | 8 | 15 | 22 | | | |
| 32 | Montaža temelja 731-003/01 | 0,38 days | Thu 20.7.23 | Fri 21.7.23 | 31 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 33 | Montaža temelja 733-001 | 0,38 days | Fri 21.7.23 | Fri 21.7.23 | 32 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 34 | Montaža temelja 733-012 | 0,38 days | Fri 21.7.23 | Fri 21.7.23 | 33 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 35 | Montaža temelja 734-001 | 0,38 days | Mon 24.7.23 | Mon 24.7.23 | 34 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 36 | Montaža temelja 743-002 | 0,38 days | Mon 24.7.23 | Mon 24.7.23 | 35 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 37 | Montaža temelja 743-003 | 0,38 days | Mon 24.7.23 | Tue 25.7.23 | 36 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 38 | Montaža temelja 751-001 | 0,38 days | Tue 25.7.23 | Tue 25.7.23 | 37 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 39 | Montaža temelja 756-004 | 0,38 days | Tue 25.7.23 | Tue 25.7.23 | 38 | \$480,00 | 12 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 40 | Montaža strojeva I uređaja | 9,25 days | Mon 17.7.23 | Mon 31.7.23 | 2FS-6 days | \$14.208,00 | 296 hrs | | | | | | | | | | | | | | | | | | | | | | | | | |
| 41 | Montaža 445-003 | 0,25 days | Mon 17.7.23 | Tue 18.7.23 | | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 42 | Montaža 445-004 | 0,25 days | Tue 18.7.23 | Tue 18.7.23 | 41 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 43 | Montaža 452-001 | 0,25 days | Tue 18.7.23 | Tue 18.7.23 | 42 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 44 | Montaža 452-005 | 0,25 days | Tue 18.7.23 | Tue 18.7.23 | 43 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 45 | Montaža 581-001 | 0,25 days | Tue 18.7.23 | Wed 19.7.23 | 44 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 46 | Montaža 581-002 | 0,25 days | Wed 19.7.23 | Wed 19.7.23 | 45 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 47 | Montaža 581-003 | 0,25 days | Wed 19.7.23 | Wed 19.7.23 | 46 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 48 | Montaža 582-001 | 0,25 days | Wed 19.7.23 | Wed 19.7.23 | 47 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 49 | Montaža 582-003/01 | 0,25 days | Wed 19.7.23 | Thu 20.7.23 | 48 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 50 | Montaža 582-003/02 | 0,25 days | Thu 20.7.23 | Thu 20.7.23 | 49 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 51 | Montaža 644-008/01 | 0,25 days | Thu 20.7.23 | Thu 20.7.23 | 50 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 52 | Montaža 644-008/02 | 0,25 days | Thu 20.7.23 | Thu 20.7.23 | 51 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 53 | Montaža 651-001 | 0,25 days | Thu 20.7.23 | Fri 21.7.23 | 52 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 54 | Montaža 651-002 | 0,25 days | Fri 21.7.23 | Fri 21.7.23 | 53 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 55 | Montaža 651-003 | 0,25 days | Fri 21.7.23 | Fri 21.7.23 | 54 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 56 | Montaža 702-001 | 0,25 days | Fri 21.7.23 | Fri 21.7.23 | 55 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 57 | Montaža 702-004 | 0,25 days | Fri 21.7.23 | Mon 24.7.23 | 56 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 58 | Montaža 702-005 | 0,25 days | Mon 24.7.23 | Mon 24.7.23 | 57 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 59 | Montaža 703-001 | 0,25 days | Mon 24.7.23 | Mon 24.7.23 | 58 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 60 | Montaža 703-002 | 0,25 days | Mon 24.7.23 | Mon 24.7.23 | 59 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 61 | Montaža 712-001 | 0,25 days | Mon 24.7.23 | Tue 25.7.23 | 60 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |
| 62 | Montaža 713-007 | 0,25 days | Tue 25.7.23 | Tue 25.7.23 | 61 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | | | | | |

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

| | | | | | | | | | |
|--|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|
| | Critical | | Split | | Slack | | Project Summary | | External Tasks |
| | Critical Split | | Progress | | Slippage | | Rolled Up Critical | | External Milestone |
| | Task | | Milestone | | Summary | | Rolled Up Critical | | Deadline |

| ID | Task Name | Duration | Start | Finish | Predecessors | Cost | Work | Resources | n '23 | | | | Jul '23 | | | | Aug '23 | | | | Sep '23 | | | | Oct '23 | | | |
|----|------------------------------------|-------------------|--------------------|---------------------|---------------------|--------------------|------------------|-----------------------|-------|----|----|----|---------|---|----|----|---------|---|----|----|---------|---|----|----|---------|---|---|----|
| | | | | | | | | | 4 | 11 | 18 | 25 | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 3 | 10 | 17 | 24 | 1 | 8 | 15 |
| 63 | Montaža 714-001 | 0,25 days | Tue 25.7.23 | Tue 25.7.23 | 62 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 64 | Montaža 756-001/02 | 0,25 days | Tue 25.7.23 | Tue 25.7.23 | 63 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 65 | Montaža 722-011 | 0,25 days | Tue 25.7.23 | Wed 26.7.23 | 64 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 66 | Montaža 731-001/01 | 0,25 days | Wed 26.7.23 | Wed 26.7.23 | 65 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 67 | Montaža 731-001/02 | 0,25 days | Wed 26.7.23 | Wed 26.7.23 | 66 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 68 | Montaža 731-002 | 0,25 days | Wed 26.7.23 | Wed 26.7.23 | 67 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 69 | Montaža 731-003/01 | 0,25 days | Wed 26.7.23 | Thu 27.7.23 | 68 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 70 | Montaža 731-003/01 | 0,25 days | Thu 27.7.23 | Thu 27.7.23 | 69 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 71 | Montaža 733-001 | 0,25 days | Thu 27.7.23 | Thu 27.7.23 | 70 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 72 | Montaža 733-012 | 0,25 days | Thu 27.7.23 | Thu 27.7.23 | 71 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 73 | Montaža 734-001 | 0,25 days | Thu 27.7.23 | Fri 28.7.23 | 72 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 74 | Montaža 743-002 | 0,25 days | Fri 28.7.23 | Fri 28.7.23 | 73 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 75 | Montaža 743-003 | 0,25 days | Fri 28.7.23 | Fri 28.7.23 | 74 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 76 | Montaža 751-001 | 0,25 days | Fri 28.7.23 | Fri 28.7.23 | 75 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 77 | Montaža 756-004 | 0,25 days | Fri 28.7.23 | Mon 31.7.23 | 76 | \$384,00 | 8 hrs | Mehaničari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 78 | Cjevarski radovi | 18,5 days | Thu 20.7.23 | Tue 15.8.23 | 40FS-7 days | \$58.608,00 | 888 hrs | | | | | | | | | | | | | | | | | | | | | |
| 79 | Montaža prolaza | 3,5 days | Thu 20.7.23 | Tue 25.7.23 | | \$11.088,00 | 168 hrs | Cjevari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 80 | Montaža nosača | 5 days | Tue 25.7.23 | Tue 1.8.23 | 79 | \$15.840,00 | 240 hrs | Cjevari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 81 | Montaža cijevi | 10 days | Tue 1.8.23 | Tue 15.8.23 | 80 | \$31.680,00 | 480 hrs | Cjevari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 82 | Bravarski radovi | 13,25 days | Wed 26.7.23 | Mon 14.8.23 | 78FS-14 days | \$16.960,00 | 424 hrs | | | | | | | | | | | | | | | | | | | | | |
| 83 | Montaža podnica | 5,25 days | Wed 26.7.23 | Wed 2.8.23 | | \$6.720,00 | 168 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 84 | Montaža ljestvi | 4,5 days | Wed 2.8.23 | Wed 9.8.23 | 83 | \$5.760,00 | 144 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 85 | Montaža skala | 3,5 days | Wed 9.8.23 | Mon 14.8.23 | 84 | \$4.480,00 | 112 hrs | Bravari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 86 | Električarski radovi | 23,5 days | Tue 1.8.23 | Mon 4.9.23 | 80 | \$81.216,00 | 1.128 hrs | | | | | | | | | | | | | | | | | | | | | |
| 87 | Montaža kablskih prolaza | 3,5 days | Tue 1.8.23 | Mon 7.8.23 | | \$12.096,00 | 168 hrs | Električari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 88 | Montaža kablskih staza | 7,5 days | Mon 7.8.23 | Wed 16.8.23 | 87 | \$25.920,00 | 360 hrs | Električari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 89 | Provlačenje kabela | 12,5 days | Wed 16.8.23 | Mon 4.9.23 | 88 | \$43.200,00 | 600 hrs | Električari (6)[600%] | | | | | | | | | | | | | | | | | | | | |
| 90 | Limarski radovi | 44,25 days | Tue 15.8.23 | Mon 16.10.23 | 78 | \$16.320,00 | 408 hrs | | | | | | | | | | | | | | | | | | | | | |
| 91 | Montaža ventilacijskih prolaza | 3,5 days | Tue 15.8.23 | Mon 21.8.23 | | \$4.480,00 | 112 hrs | Limari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 92 | Montaža ventilacijskih kanala | 7,5 days | Mon 4.9.23 | Thu 14.9.23 | 91SS+14 days | \$9.600,00 | 240 hrs | Limari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 93 | Montaža zaštite strojeva I uređaja | 1,75 days | Fri 13.10.23 | Mon 16.10.23 | 92FS+21 days | \$2.240,00 | 56 hrs | Limari (4)[400%] | | | | | | | | | | | | | | | | | | | | |

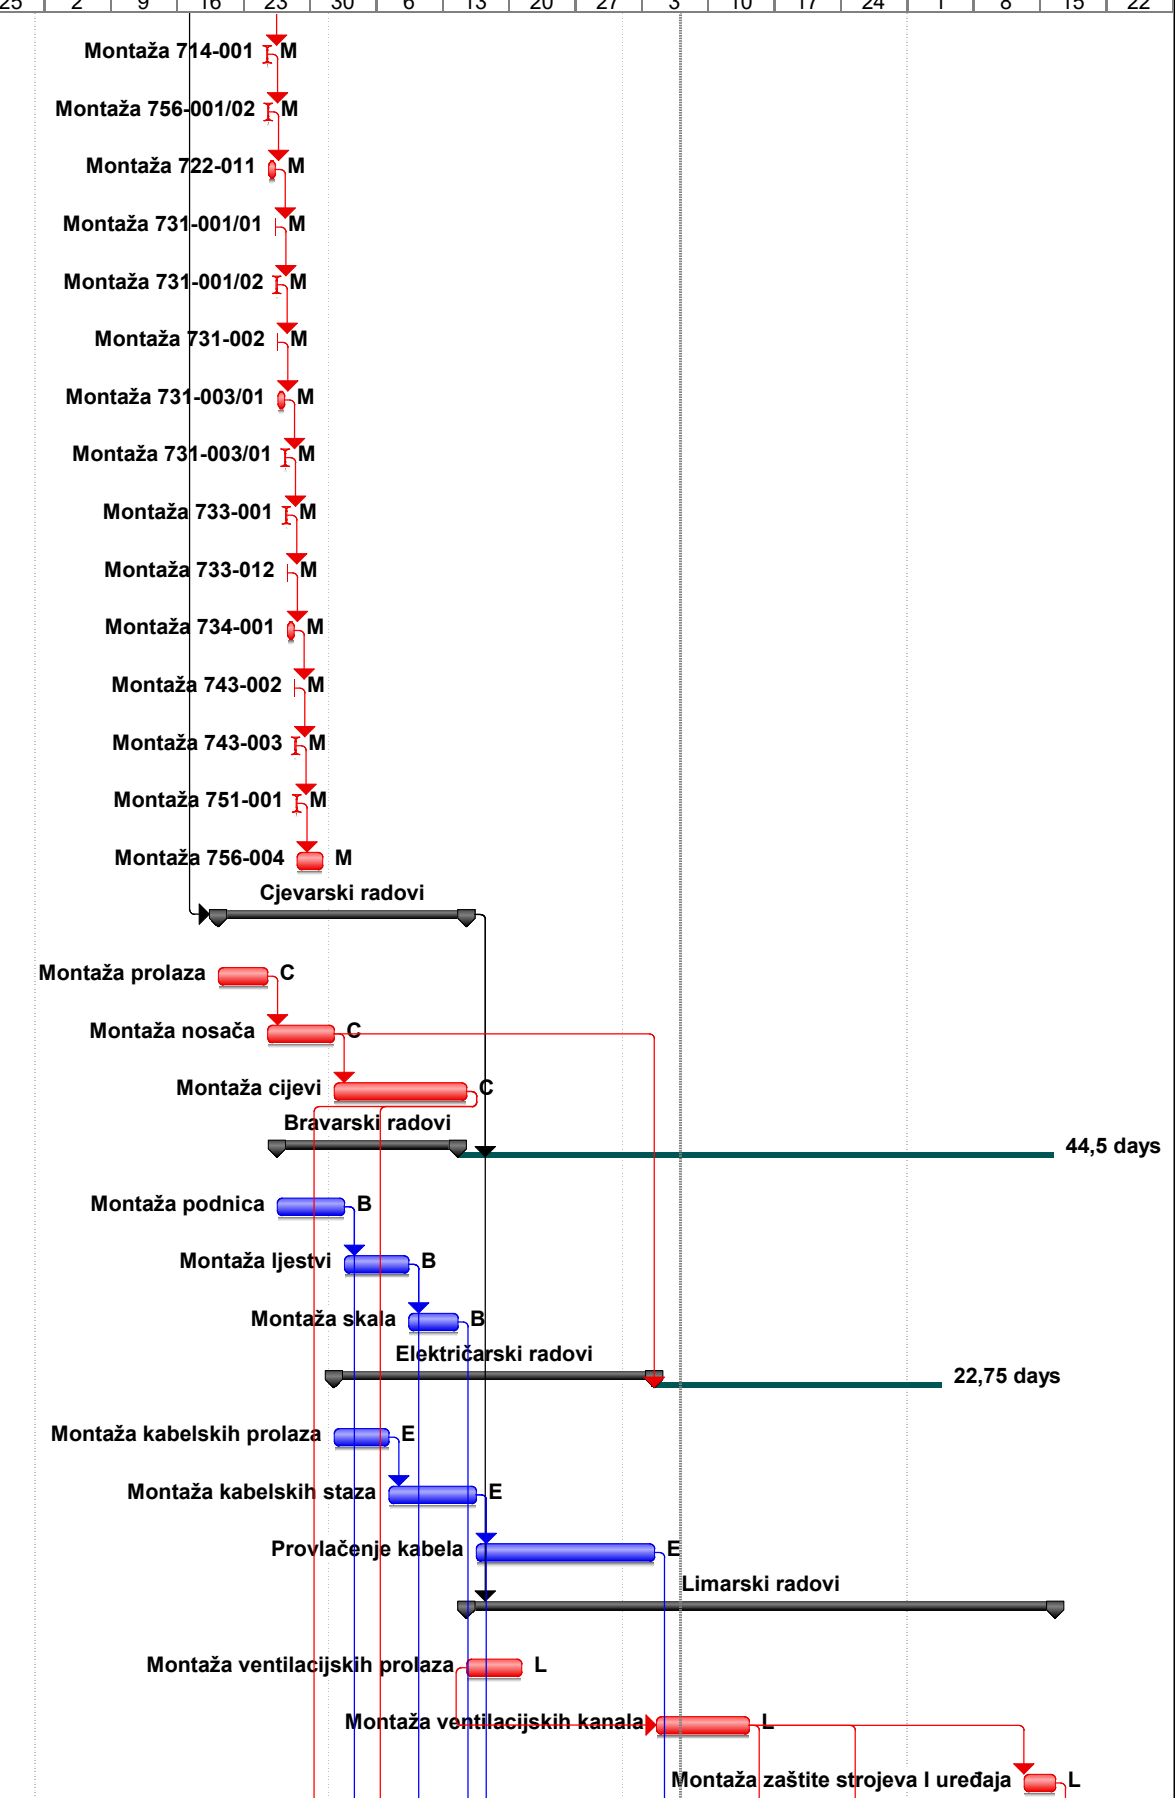

| | | | | | | | | | | |
|--|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Project: OPREMANJE 2 PLATFORME Date: Thu 7.9.23 | Critical | | Split | | Slack | | Project Summary | | External Tasks | |
| | Critical Split | | Progress | | Slippage | | Rolled Up Critical | | External Milestone | |
| | Task | | Milestone | | Summary | | Rolled Up Critical | | Deadline | |

| ID | Task Name | Duration | Start | Finish | Predecessors | Cost | Work | Resources | Jun '23 | | | | Jul '23 | | | | Aug '23 | | | | Sep '23 | | | Oct '23 | | | | |
|-----|--|-------------------|--------------------|---------------------|--------------|--------------------|----------------|----------------------------------|---------|----|----|----|---------|---|----|----|---------|---|----|----|---------|---|----|---------|----|---|---|----|
| | | | | | | | | | 4 | 11 | 18 | 25 | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 3 | 10 | 17 | 24 | 1 | 8 | 15 |
| 94 | Izolaterski radovi | 7,5 days | Thu 14.9.23 | Mon 25.9.23 | 92 | \$9.600,00 | 240 hrs | | | | | | | | | | | | | | | | | | | | | |
| 95 | Montaža izolacije | 7,5 days | Thu 14.9.23 | Mon 25.9.23 | | \$9.600,00 | 240 hrs | Izolateri (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 96 | Ispitivanje | 54,75 days | Tue 1.8.23 | Tue 17.10.23 | | \$30.816,00 | 760 hrs | | | | | | | | | | | | | | | | | | | | | |
| 97 | Ispitivanje rada strojeva I uređaja | 1,5 days | Tue 8.8.23 | Thu 10.8.23 | 81FS-5 days | \$576,00 | 24 hrs | Ispitivači/Mehaničari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 98 | Ispitivanje cjevovoda | 8,25 days | Tue 1.8.23 | Fri 11.8.23 | | \$11.616,00 | 264 hrs | | | | | | | | | | | | | | | | | | | | | |
| 99 | Pregled strukture cjevovoda | 3,5 days | Tue 1.8.23 | Mon 7.8.23 | 81FS-10 days | \$4.928,00 | 112 hrs | Ispitivači/cjevvari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 100 | Tlačenje cjevovoda | 3 days | Mon 7.8.23 | Thu 10.8.23 | 99 | \$4.224,00 | 96 hrs | Ispitivači/cjevvari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 101 | Pregled funkcionalnosti cjevovoda | 1,75 days | Thu 10.8.23 | Fri 11.8.23 | 100 | \$2.464,00 | 56 hrs | Ispitivači/cjevvari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 102 | Pregled bravarskih radova | 9 days | Wed 2.8.23 | Tue 15.8.23 | | \$1.280,00 | 64 hrs | | | | | | | | | | | | | | | | | | | | | |
| 103 | Pregled strukture podnica | 2 days | Wed 2.8.23 | Fri 4.8.23 | 83 | \$640,00 | 32 hrs | Kontrolori/Bravari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 104 | Pregled strukture ljestvi | 1 day | Wed 9.8.23 | Thu 10.8.23 | 84 | \$320,00 | 16 hrs | Kontrolori/Bravari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 105 | Pregled strukture skala | 1 day | Mon 14.8.23 | Tue 15.8.23 | 85 | \$320,00 | 16 hrs | Kontrolori/Bravari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 106 | Ispitivanje električarskih radova | 21 days | Wed 16.8.23 | Thu 14.9.23 | | \$15.744,00 | 328 hrs | | | | | | | | | | | | | | | | | | | | | |
| 107 | Pregled strukture kablskih staza | 1,75 days | Wed 16.8.23 | Fri 18.8.23 | 88 | \$2.688,00 | 56 hrs | Ispitivači/Električari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 108 | Pregled montaže kabela | 2,5 days | Mon 4.9.23 | Wed 6.9.23 | 89 | \$3.840,00 | 80 hrs | Ispitivači/Električari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 109 | Ispitivanje ožičenja kabela | 3,5 days | Wed 6.9.23 | Tue 12.9.23 | 108 | \$5.376,00 | 112 hrs | Ispitivači/Električari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 110 | Test ispitivanja pod naponom | 2,5 days | Tue 12.9.23 | Thu 14.9.23 | 109 | \$3.840,00 | 80 hrs | Ispitivači/Električari (4)[400%] | | | | | | | | | | | | | | | | | | | | |
| 111 | Ispitivanje limarskih radova | 23,25 days | Thu 14.9.23 | Tue 17.10.23 | | \$1.120,00 | 56 hrs | | | | | | | | | | | | | | | | | | | | | |
| 112 | Pregled strukture ventilacije | 1 day | Thu 14.9.23 | Fri 15.9.23 | 92 | \$320,00 | 16 hrs | Kontrolori/Limari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 113 | Pregled funkcionalnosti ventilacije | 2 days | Fri 15.9.23 | Tue 19.9.23 | 112 | \$640,00 | 32 hrs | Kontrolori/Limari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 114 | Pregled strukture zaštite strojeva | 0,5 days | Mon 16.10.23 | Tue 17.10.23 | 93 | \$160,00 | 8 hrs | Kontrolori/Limari (2)[200%] | | | | | | | | | | | | | | | | | | | | |
| 115 | Ispitivanje izolaterskih radova | 1,5 days | Mon 25.9.23 | Wed 27.9.23 | | \$480,00 | 24 hrs | | | | | | | | | | | | | | | | | | | | | |
| 116 | Pregled montaže izolacije | 1,5 days | Mon 25.9.23 | Wed 27.9.23 | 95 | \$480,00 | 24 hrs | Kontrolori/Izolateri (2)[200%] | | | | | | | | | | | | | | | | | | | | |

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

| | | | | | | | | | |
|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Critical | | Split | | Slack | | Project Summary | | External Tasks | |
| Critical Split | | Progress | | Slippage | | Rolled Up Critical | | External Milestone | |
| Task | | Milestone | | Summary | | Rolled Up Critical | | Deadline | |
