

# Prilog - peti slučaj

---

**Butorac, Lovro**

**Supplement / Prilog**

*Publication year / Godina izdavanja:* **2023**

*Permanent link / Trajna poveznica:* <https://urn.nsk.hr/urn:nbn:hr:190:889398>

*Rights / Prava:* [In copyright](#)/[Zaštićeno autorskim pravom.](#)

*Download date / Datum preuzimanja:* **2024-09-06**



*Repository / Repozitorij:*

[Repository of the University of Rijeka, Faculty of Engineering](#)




| ID | Task Name                                 | Duration          | Start             | Finish             | Predecessors | Cost                | Work             | Resources          | Jul '23                                   |    |    |   |   |    |    | Aug '23 |   |    |    | Sep '23 |   |    | Oct '23 |    |   |  |
|----|---|-------------------|-------------------|--------------------|--------------|---------------------|------------------|--------------------|---|----|----|---|---|----|----|---------|---|----|----|---------|---|----|---------|----|---|--|
|    |   |                   |                   |                    |              |                     |                  |                    | 11  | 18 | 25 | 2 | 9 | 16 | 23 | 30      | 6 | 13 | 20 | 27      | 3 | 10 | 17      | 24 | 1 |  |
| 1  | <b>OPREMANJE 2. PLATFORME STROJARNICE</b> | <b>59 days</b>    | <b>Thu 6.7.23</b> | <b>Tue 26.9.23</b> |              | <b>\$148.928,00</b> | <b>4.588 hrs</b> |                    | <b>OPREMANJE 2. PLATFORME STROJARNICE</b> |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 2  | <b>Montaža temelja</b>                    | <b>14,25 days</b> | <b>Thu 6.7.23</b> | <b>Wed 26.7.23</b> |              | <b>\$8.880,00</b>   | <b>444 hrs</b>   |                    | <b>Montaža temelja</b>                    |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 3  | Montaža temelja 445-003                   | 0,75 days         | Thu 6.7.23        | Thu 6.7.23         |              | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 445-003 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 4  | Montaža temelja 445-004                   | 0,75 days         | Thu 6.7.23        | Thu 6.7.23         |              | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 445-004 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 5  | Montaža temelja 452-001                   | 0,75 days         | Thu 6.7.23        | Fri 7.7.23         | 3            | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 452-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 6  | Montaža temelja 452-005                   | 0,75 days         | Thu 6.7.23        | Fri 7.7.23         | 4            | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 452-005 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 7  | Montaža temelja 581-001                   | 0,75 days         | Fri 7.7.23        | Mon 10.7.23        | 5            | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 581-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 8  | Montaža temelja 581-002                   | 0,75 days         | Fri 7.7.23        | Mon 10.7.23        | 6            | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 581-002 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 9  | Montaža temelja 581-003                   | 0,75 days         | Mon 10.7.23       | Mon 10.7.23        | 7            | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 581-003 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 10 | Montaža temelja 582-001                   | 0,75 days         | Mon 10.7.23       | Mon 10.7.23        | 8            | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 582-001 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 11 | Montaža temelja 582-003/01                | 0,75 days         | Tue 11.7.23       | Tue 11.7.23        | 9            | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 582-003/01 B1             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 12 | Montaža temelja 582-003/02                | 0,75 days         | Tue 11.7.23       | Tue 11.7.23        | 10           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 582-003/02 B2             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 13 | Montaža temelja 644-008/01                | 0,75 days         | Tue 11.7.23       | Wed 12.7.23        | 11           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 644-008/01 B1             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 14 | Montaža temelja 644-008/02                | 0,75 days         | Tue 11.7.23       | Wed 12.7.23        | 12           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 644-008/02 B2             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 15 | Montaža temelja 651-001                   | 0,75 days         | Wed 12.7.23       | Thu 13.7.23        | 13           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 651-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 16 | Montaža temelja 651-002                   | 0,75 days         | Wed 12.7.23       | Thu 13.7.23        | 14           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 651-002 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 17 | Montaža temelja 651-003                   | 0,75 days         | Thu 13.7.23       | Thu 13.7.23        | 15           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 651-003 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 18 | Montaža temelja 702-001                   | 0,75 days         | Thu 13.7.23       | Thu 13.7.23        | 16           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 702-001 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 19 | Montaža temelja 702-004                   | 0,75 days         | Fri 14.7.23       | Fri 14.7.23        | 17           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 702-004 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 20 | Montaža temelja 702-005                   | 0,75 days         | Fri 14.7.23       | Fri 14.7.23        | 18           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 702-005 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 21 | Montaža temelja 703-001                   | 0,75 days         | Fri 14.7.23       | Mon 17.7.23        | 19           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 703-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 22 | Montaža temelja 703-002                   | 0,75 days         | Fri 14.7.23       | Mon 17.7.23        | 20           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 703-002 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 23 | Montaža temelja 712-001                   | 0,75 days         | Mon 17.7.23       | Tue 18.7.23        | 21           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 712-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 24 | Montaža temelja 713-007                   | 0,75 days         | Mon 17.7.23       | Tue 18.7.23        | 22           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 713-007 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 25 | Montaža temelja 714-001                   | 0,75 days         | Tue 18.7.23       | Tue 18.7.23        | 23           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 714-001 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 26 | Montaža temelja 756-001/02                | 0,75 days         | Tue 18.7.23       | Tue 18.7.23        | 24           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 756-001/02 B2             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 27 | Montaža temelja 722-011                   | 0,75 days         | Wed 19.7.23       | Wed 19.7.23        | 25           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 722-011 B1                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 28 | Montaža temelja 731-001/01                | 0,75 days         | Wed 19.7.23       | Wed 19.7.23        | 26           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 731-001/01 B2             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 29 | Montaža temelja 731-001/02                | 0,75 days         | Wed 19.7.23       | Thu 20.7.23        | 27           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 731-001/02 B1             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 30 | Montaža temelja 731-002                   | 0,75 days         | Wed 19.7.23       | Thu 20.7.23        | 28           | \$240,00            | 12 hrs           | Bravari2 (2)[200%] | Montaža temelja 731-002 B2                |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |
| 31 | Montaža temelja 731-003/01                | 0,75 days         | Thu 20.7.23       | Fri 21.7.23        | 29           | \$240,00            | 12 hrs           | Bravari1 (2)[200%] | Montaža temelja 731-003/01 B1             |    |    |   |   |    |    |         |   |    |    |         |   |    |         |    |   |  |

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

|                |  |           |  |          |  |                    |  |                    |  |
|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Critical       |  | Split     |  | Slack    |  | Project Summary    |  | External Tasks     |  |
| Critical Split |  | Progress  |  | Slippage |  | Rolled Up Critical |  | External Milestone |  |
| Task           |  | Milestone |  | Summary  |  | Rolled Up Critical |  | Deadline           |  |


| ID | Task Name                         | Duration        | Start              | Finish             | Predecessors      | Cost              | Work           | Resources             | Jul '23 |    |    |   |   |    |    | Aug '23 |   |    |    |    |   |    | Sep '23 |    |   | Oct '23 |  |  |  |  |  |  |  |  |  |
|----|-----------------------------------|-----------------|--------------------|--------------------|-------------------|-------------------|----------------|-----------------------|---------|----|----|---|---|----|----|---------|---|----|----|----|---|----|---------|----|---|---------|--|--|--|--|--|--|--|--|--|
|    |                                   |                 |                    |                    |                   |                   |                |                       | 11      | 18 | 25 | 2 | 9 | 16 | 23 | 30      | 6 | 13 | 20 | 27 | 3 | 10 | 17      | 24 | 1 |         |  |  |  |  |  |  |  |  |  |
| 32 | Montaža temelja 731-003/01        | 0,75 days       | Thu 20.7.23        | Fri 21.7.23        | 30                | \$240,00          | 12 hrs         | Bravari2 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 33 | Montaža temelja 733-001           | 0,75 days       | Fri 21.7.23        | Fri 21.7.23        | 31                | \$240,00          | 12 hrs         | Bravari1 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 34 | Montaža temelja 733-012           | 0,75 days       | Fri 21.7.23        | Fri 21.7.23        | 32                | \$240,00          | 12 hrs         | Bravari2 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 35 | Montaža temelja 734-001           | 0,75 days       | Mon 24.7.23        | Mon 24.7.23        | 33                | \$240,00          | 12 hrs         | Bravari1 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 36 | Montaža temelja 743-002           | 0,75 days       | Mon 24.7.23        | Mon 24.7.23        | 34                | \$240,00          | 12 hrs         | Bravari2 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 37 | Montaža temelja 743-003           | 0,75 days       | Mon 24.7.23        | Tue 25.7.23        | 35                | \$240,00          | 12 hrs         | Bravari1 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 38 | Montaža temelja 751-001           | 0,75 days       | Mon 24.7.23        | Tue 25.7.23        | 36                | \$240,00          | 12 hrs         | Bravari2 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 39 | Montaža temelja 756-004           | 0,75 days       | Tue 25.7.23        | Wed 26.7.23        | 37                | \$240,00          | 12 hrs         | Bravari1 (2)[200%]    |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 40 | <b>Montaža strojeva I uređaja</b> | <b>9,5 days</b> | <b>Mon 17.7.23</b> | <b>Fri 28.7.23</b> | <b>2FS-7 days</b> | <b>\$7.104,00</b> | <b>296 hrs</b> |                       |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 41 | Montaža 445-003                   | 0,5 days        | Mon 17.7.23        | Mon 17.7.23        |                   | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 42 | Montaža 445-004                   | 0,5 days        | Mon 17.7.23        | Mon 17.7.23        |                   | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 43 | Montaža 452-001                   | 0,5 days        | Mon 17.7.23        | Tue 18.7.23        | 41                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 44 | Montaža 452-005                   | 0,5 days        | Mon 17.7.23        | Tue 18.7.23        | 42                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 45 | Montaža 581-001                   | 0,5 days        | Tue 18.7.23        | Tue 18.7.23        | 43                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 46 | Montaža 581-002                   | 0,5 days        | Tue 18.7.23        | Tue 18.7.23        | 44                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 47 | Montaža 581-003                   | 0,5 days        | Tue 18.7.23        | Wed 19.7.23        | 45                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 48 | Montaža 582-001                   | 0,5 days        | Tue 18.7.23        | Wed 19.7.23        | 46                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 49 | Montaža 582-003/01                | 0,5 days        | Wed 19.7.23        | Wed 19.7.23        | 47                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 50 | Montaža 582-003/02                | 0,5 days        | Wed 19.7.23        | Wed 19.7.23        | 48                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 51 | Montaža 644-008/01                | 0,5 days        | Wed 19.7.23        | Thu 20.7.23        | 49                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 52 | Montaža 644-008/02                | 0,5 days        | Wed 19.7.23        | Thu 20.7.23        | 50                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 53 | Montaža 651-001                   | 0,5 days        | Thu 20.7.23        | Thu 20.7.23        | 51                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 54 | Montaža 651-002                   | 0,5 days        | Thu 20.7.23        | Thu 20.7.23        | 52                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 55 | Montaža 651-003                   | 0,5 days        | Thu 20.7.23        | Fri 21.7.23        | 53                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 56 | Montaža 702-001                   | 0,5 days        | Thu 20.7.23        | Fri 21.7.23        | 54                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 57 | Montaža 702-004                   | 0,5 days        | Fri 21.7.23        | Fri 21.7.23        | 55                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 58 | Montaža 702-005                   | 0,5 days        | Fri 21.7.23        | Fri 21.7.23        | 56                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 59 | Montaža 703-001                   | 0,5 days        | Fri 21.7.23        | Mon 24.7.23        | 57                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 60 | Montaža 703-002                   | 0,5 days        | Fri 21.7.23        | Mon 24.7.23        | 58                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 61 | Montaža 712-001                   | 0,5 days        | Mon 24.7.23        | Mon 24.7.23        | 59                | \$192,00          | 8 hrs          | Mehaničari1 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |
| 62 | Montaža 713-007                   | 0,5 days        | Mon 24.7.23        | Mon 24.7.23        | 60                | \$192,00          | 8 hrs          | Mehaničari2 (2)[200%] |         |    |    |   |   |    |    |         |   |    |    |    |   |    |         |    |   |         |  |  |  |  |  |  |  |  |  |

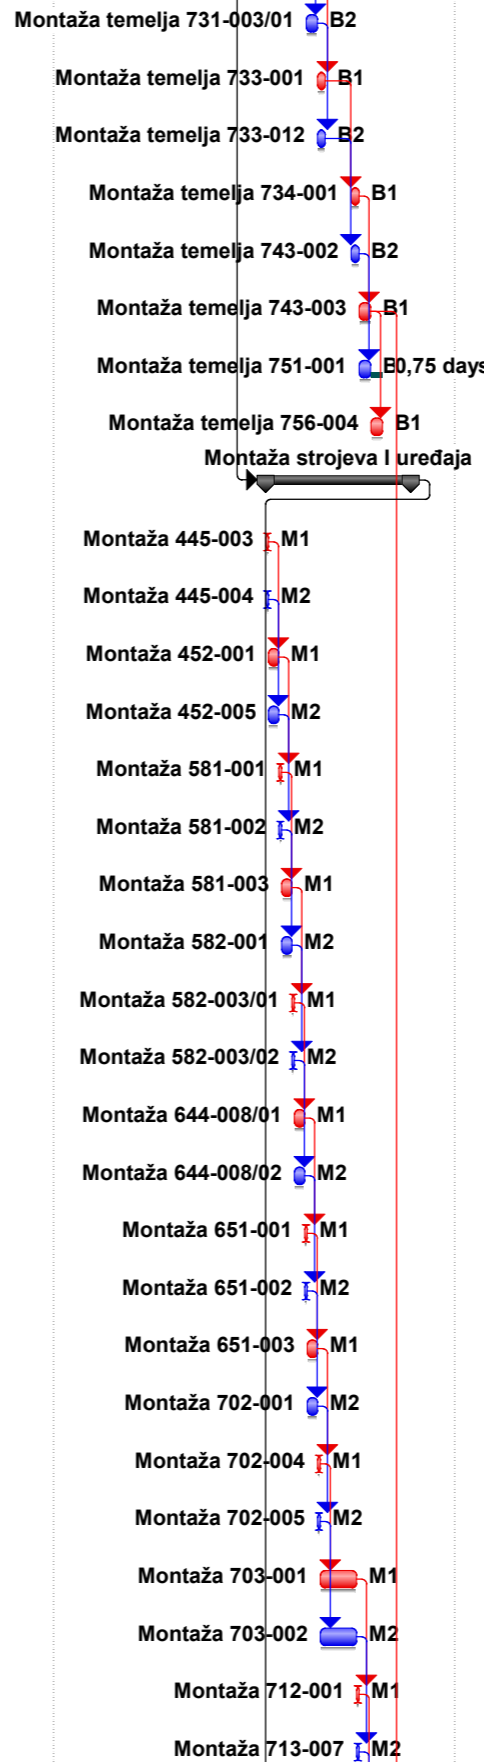

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23


|                |  |           |  |          |  |                    |  |                    |  |
|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Critical       |  | Split     |  | Slack    |  | Project Summary    |  | External Tasks     |  |
| Critical Split |  | Progress  |  | Slippage |  | Rolled Up Critical |  | External Milestone |  |
| Task           |  | Milestone |  | Summary  |  | Rolled Up Critical |  | Deadline           |  |

| ID | Task Name                          | Duration          | Start              | Finish             | Predecessors        | Cost               | Work             | Resources              | Jul '23 |    |    |   | Aug '23 |    |    |    | Sep '23 |    |    | Oct '23 |   |    |    |
|----|------------------------------------|-------------------|--------------------|--------------------|---------------------|--------------------|------------------|------------------------|---------|----|----|---|---------|----|----|----|---------|----|----|---------|---|----|----|
|    |                                    |                   |                    |                    |                     |                    |                  |                        | 11      | 18 | 25 | 2 | 9       | 16 | 23 | 30 | 6       | 13 | 20 | 27      | 3 | 10 | 17 |
| 63 | Montaža 714-001                    | 0,5 days          | Mon 24.7.23        | Tue 25.7.23        | 61                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 64 | Montaža 756-001/02                 | 0,5 days          | Mon 24.7.23        | Tue 25.7.23        | 62                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 65 | Montaža 722-011                    | 0,5 days          | Tue 25.7.23        | Tue 25.7.23        | 63                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 66 | Montaža 731-001/01                 | 0,5 days          | Tue 25.7.23        | Tue 25.7.23        | 64                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 67 | Montaža 731-001/02                 | 0,5 days          | Tue 25.7.23        | Wed 26.7.23        | 65                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 68 | Montaža 731-002                    | 0,5 days          | Tue 25.7.23        | Wed 26.7.23        | 66                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 69 | Montaža 731-003/01                 | 0,5 days          | Wed 26.7.23        | Wed 26.7.23        | 67                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 70 | Montaža 731-003/01                 | 0,5 days          | Wed 26.7.23        | Wed 26.7.23        | 68                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 71 | Montaža 733-001                    | 0,5 days          | Wed 26.7.23        | Thu 27.7.23        | 69                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 72 | Montaža 733-012                    | 0,5 days          | Wed 26.7.23        | Thu 27.7.23        | 70                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 73 | Montaža 734-001                    | 0,5 days          | Thu 27.7.23        | Thu 27.7.23        | 71                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 74 | Montaža 743-002                    | 0,5 days          | Thu 27.7.23        | Thu 27.7.23        | 72                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 75 | Montaža 743-003                    | 0,5 days          | Thu 27.7.23        | Fri 28.7.23        | 73                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 76 | Montaža 751-001                    | 0,5 days          | Thu 27.7.23        | Fri 28.7.23        | 74                  | \$192,00           | 8 hrs            | Mehaničari2 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 77 | Montaža 756-004                    | 0,5 days          | Fri 28.7.23        | Fri 28.7.23        | 75                  | \$192,00           | 8 hrs            | Mehaničari1 (2)[200%]  |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 78 | <b>Cjevarski radovi</b>            | <b>20,25 days</b> | <b>Wed 19.7.23</b> | <b>Wed 16.8.23</b> | <b>40FS-7 days</b>  | <b>\$39.072,00</b> | <b>888 hrs</b>   |                        |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 79 | Montaža prolaza                    | 5,25 days         | Wed 19.7.23        | Wed 26.7.23        |                     | \$7.392,00         | 168 hrs          | Cjevari1 (4)[400%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 80 | Montaža nosača                     | 7,5 days          | Thu 20.7.23        | Mon 31.7.23        | 79FS-5 days         | \$10.560,00        | 240 hrs          | Cjevari2 (4)[400%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 81 | Montaža cijevi                     | 15 days           | Thu 27.7.23        | Wed 16.8.23        | 79                  | \$21.120,00        | 480 hrs          | Cjevari1 (4)[400%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 82 | <b>Bravarski radovi</b>            | <b>17,5 days</b>  | <b>Wed 26.7.23</b> | <b>Fri 18.8.23</b> | <b>78FS-16 days</b> | <b>\$8.480,00</b>  | <b>424 hrs</b>   |                        |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 83 | Montaža podnica                    | 10,5 days         | Wed 26.7.23        | Wed 9.8.23         |                     | \$3.360,00         | 168 hrs          | Bravari2 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 84 | Montaža ljestvi                    | 9 days            | Thu 27.7.23        | Wed 9.8.23         | 37FS+2 days         | \$2.880,00         | 144 hrs          | Bravari1 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 85 | Montaža skala                      | 7 days            | Wed 9.8.23         | Fri 18.8.23        | 83                  | \$2.240,00         | 112 hrs          | Bravari2 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 86 | <b>Električarski radovi</b>        | <b>24 days</b>    | <b>Mon 31.7.23</b> | <b>Fri 1.9.23</b>  | <b>80</b>           | <b>\$54.144,00</b> | <b>1.128 hrs</b> |                        |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 87 | Montaža kablskih prolaza           | 5,25 days         | Mon 31.7.23        | Mon 7.8.23         |                     | \$8.064,00         | 168 hrs          | Električari1 (4)[400%] |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 88 | Montaža kablskih staza             | 11,25 days        | Mon 7.8.23         | Tue 22.8.23        | 87                  | \$17.280,00        | 360 hrs          | Električari1 (4)[400%] |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 89 | Provlačenje kabela                 | 18,75 days        | Mon 7.8.23         | Fri 1.9.23         | 87                  | \$28.800,00        | 600 hrs          | Električari2 (4)[400%] |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 90 | <b>Limarski radovi</b>             | <b>15 days</b>    | <b>Thu 31.8.23</b> | <b>Wed 20.9.23</b> | <b>78FS+10 days</b> | <b>\$8.160,00</b>  | <b>408 hrs</b>   |                        |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 91 | Montaža ventilacijskih prolaza     | 7 days            | Thu 31.8.23        | Fri 8.9.23         |                     | \$2.240,00         | 112 hrs          | Limari2 (2)[200%]      |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 92 | Montaža ventilacijskih kanala      | 15 days           | Thu 31.8.23        | Wed 20.9.23        |                     | \$4.800,00         | 240 hrs          | Limari1 (2)[200%]      |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |
| 93 | Montaža zaštite strojeva I uređaja | 3,5 days          | Mon 11.9.23        | Thu 14.9.23        | 91                  | \$1.120,00         | 56 hrs           | Limari2 (2)[200%]      |         |    |    |   |         |    |    |    |         |    |    |         |   |    |    |

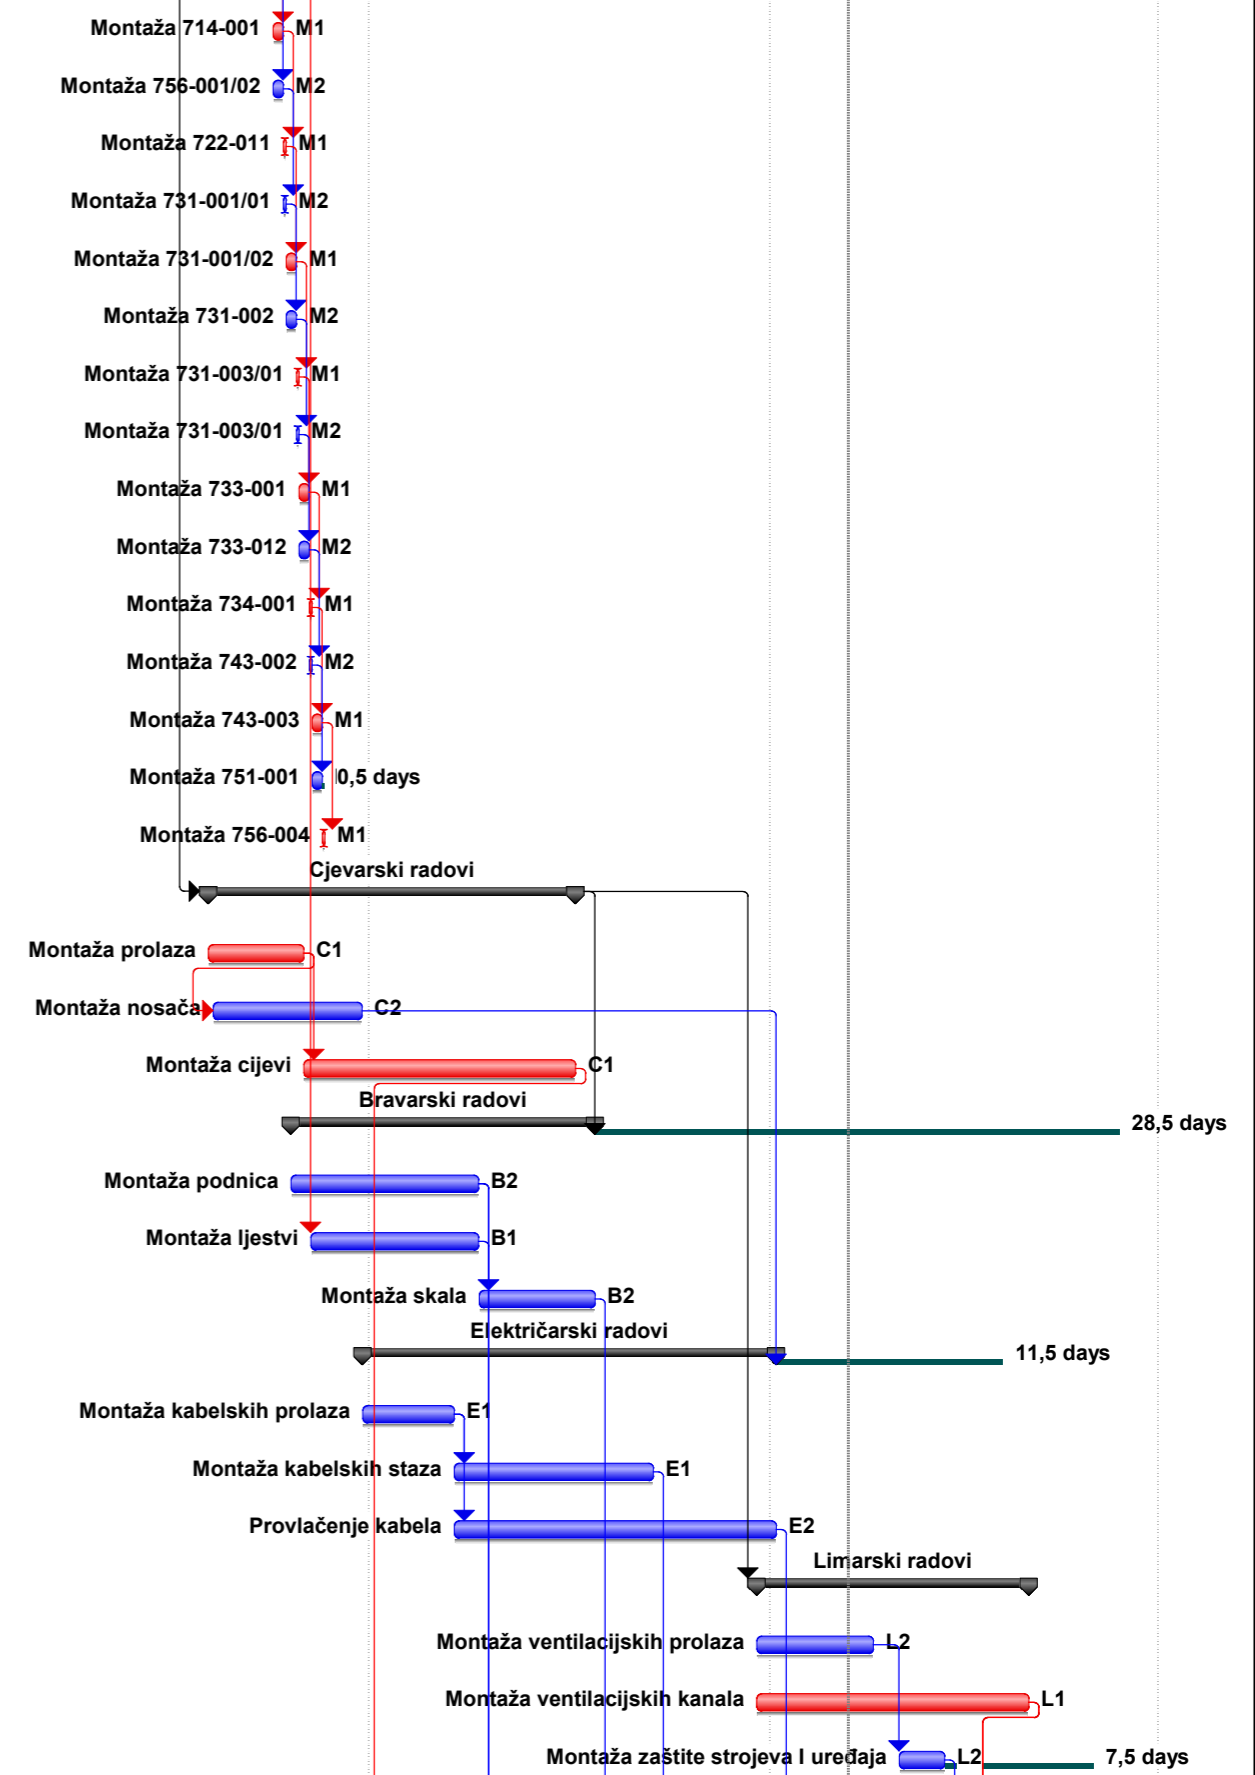

|  |                |  |           |  |          |  |                    |  |                    |  |
|--|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Project: OPREMANJE 2 PLATFORME<br>Date: Thu 7.9.23 | Critical       |  | Split     |  | Slack    |  | Project Summary    |  | External Tasks     |  |
|  | Critical Split |  | Progress  |  | Slippage |  | Rolled Up Critical |  | External Milestone |  |
|  | Task           |  | Milestone |  | Summary  |  | Rolled Up Critical |  | Deadline           |  |

| ID  | Task Name                                | Duration         | Start              | Finish             | Predecessors        | Cost               | Work           | Resources                         | Jul '23 |    |    |   | Aug '23 |    |    |    | Sep '23 |    |    |    | Oct '23 |
|-----|--|------------------|--------------------|--------------------|---------------------|--------------------|----------------|-----------------------------------|---------|----|----|---|---------|----|----|----|---------|----|----|----|---------|
|     |  |                  |                    |                    |                     |                    |                |                                   | 11      | 18 | 25 | 2 | 9       | 16 | 23 | 30 | 6       | 13 | 20 | 27 | 3       |
| 94  | <b>Izolaterski radovi</b>                | <b>10 days</b>   | <b>Tue 5.9.23</b>  | <b>Mon 18.9.23</b> | <b>92FS-12 days</b> | <b>\$7.200,00</b>  | <b>240 hrs</b> |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 95  | Montaža izolacije                        | 10 days          | Tue 5.9.23         | Mon 18.9.23        |                     | \$7.200,00         | 240 hrs        | Izolateri (3)[300%]               |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 96  | <b>Ispitivanje</b>                       | <b>39 days</b>   | <b>Thu 3.8.23</b>  | <b>Tue 26.9.23</b> |                     | <b>\$15.888,00</b> | <b>760 hrs</b> |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 97  | <b>Ispitivanje cjevovoda</b>             | <b>13,5 days</b> | <b>Thu 3.8.23</b>  | <b>Tue 22.8.23</b> |                     | <b>\$5.808,00</b>  | <b>264 hrs</b> |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 98  | Pregled strukture cjevovoda              | 7 days           | Thu 3.8.23         | Fri 11.8.23        | 81FS-10 days        | \$2.464,00         | 112 hrs        | Ispitivači/cjevari1 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 99  | Tlačenje cjevovoda                       | 6 days           | Mon 14.8.23        | Mon 21.8.23        | 98                  | \$2.112,00         | 96 hrs         | Ispitivači/cjevari1 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 100 | Pregled funkcionalnosti cjevovoda        | 3,5 days         | Thu 17.8.23        | Tue 22.8.23        | 99SS+3 days         | \$1.232,00         | 56 hrs         | Ispitivači/cjevari2 (2)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 101 | Ispitivanje rada strojeva I uređaja      | 1,5 days         | Tue 22.8.23        | Wed 23.8.23        | 100                 | \$288,00           | 24 hrs         | Ispitivači/Mehaničari (1)[200%]   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 102 | <b>Pregled bravarskih radova</b>         | <b>8 days</b>    | <b>Wed 9.8.23</b>  | <b>Mon 21.8.23</b> |                     | <b>\$640,00</b>    | <b>64 hrs</b>  |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 103 | Pregled strukture podnica                | 2 days           | Wed 9.8.23         | Fri 11.8.23        | 83                  | \$320,00           | 32 hrs         | Kontrolori/Bravari2 (1)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 104 | Pregled strukture ljestvi                | 1 day            | Wed 9.8.23         | Thu 10.8.23        | 84                  | \$160,00           | 16 hrs         | Kontrolori/Bravari1 (1)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 105 | Pregled strukture skala                  | 1 day            | Fri 18.8.23        | Mon 21.8.23        | 85                  | \$160,00           | 16 hrs         | Kontrolori/Bravari2 (1)[200%]     |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 106 | <b>Ispitivanje električarskih radova</b> | <b>15,5 days</b> | <b>Wed 23.8.23</b> | <b>Wed 13.9.23</b> |                     | <b>\$7.872,00</b>  | <b>328 hrs</b> |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 107 | Pregled strukture kablinskih staza       | 3,5 days         | Wed 23.8.23        | Mon 28.8.23        | 88                  | \$1.344,00         | 56 hrs         | Ispitivači/Električari1 (2)[200%] |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 108 | Pregled montaže kabela                   | 5 days           | Fri 1.9.23         | Fri 8.9.23         | 89                  | \$1.920,00         | 80 hrs         | Ispitivači/Električari1 (2)[200%] |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 109 | Ispitivanje ožičenja kabela              | 7 days           | Mon 28.8.23        | Wed 6.9.23         | 107                 | \$2.688,00         | 112 hrs        | Ispitivači/Električari2 (2)[200%] |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 110 | Test ispitivanja pod naponom             | 5 days           | Wed 6.9.23         | Wed 13.9.23        | 109                 | \$1.920,00         | 80 hrs         | Ispitivači/Električari2 (2)[200%] |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 111 | <b>Ispitivanje limarskih radova</b>      | <b>8,5 days</b>  | <b>Thu 14.9.23</b> | <b>Tue 26.9.23</b> |                     | <b>\$560,00</b>    | <b>56 hrs</b>  |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 112 | Pregled strukture ventilacije            | 2 days           | Tue 19.9.23        | Wed 20.9.23        | 92FS-2 days         | \$160,00           | 16 hrs         | Kontrolori/Limari1 (1)            |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 113 | Pregled funkcionalnosti ventilacije      | 4 days           | Thu 21.9.23        | Tue 26.9.23        | 112                 | \$320,00           | 32 hrs         | Kontrolori/Limari1 (1)            |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 114 | Pregled strukture zaštite strojeva       | 1 day            | Thu 14.9.23        | Fri 15.9.23        | 93                  | \$80,00            | 8 hrs          | Kontrolori/Limari2 (1)            |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 115 | <b>Ispitivanje izolaterskih radova</b>   | <b>3 days</b>    | <b>Tue 19.9.23</b> | <b>Thu 21.9.23</b> |                     | <b>\$720,00</b>    | <b>24 hrs</b>  |                                   |         |    |    |   |         |    |    |    |         |    |    |    |         |
| 116 | Pregled montaže izolacije                | 3 days           | Tue 19.9.23        | Thu 21.9.23        | 95                  | \$720,00           | 24 hrs         | Izolateri (3)                     |         |    |    |   |         |    |    |    |         |    |    |    |         |

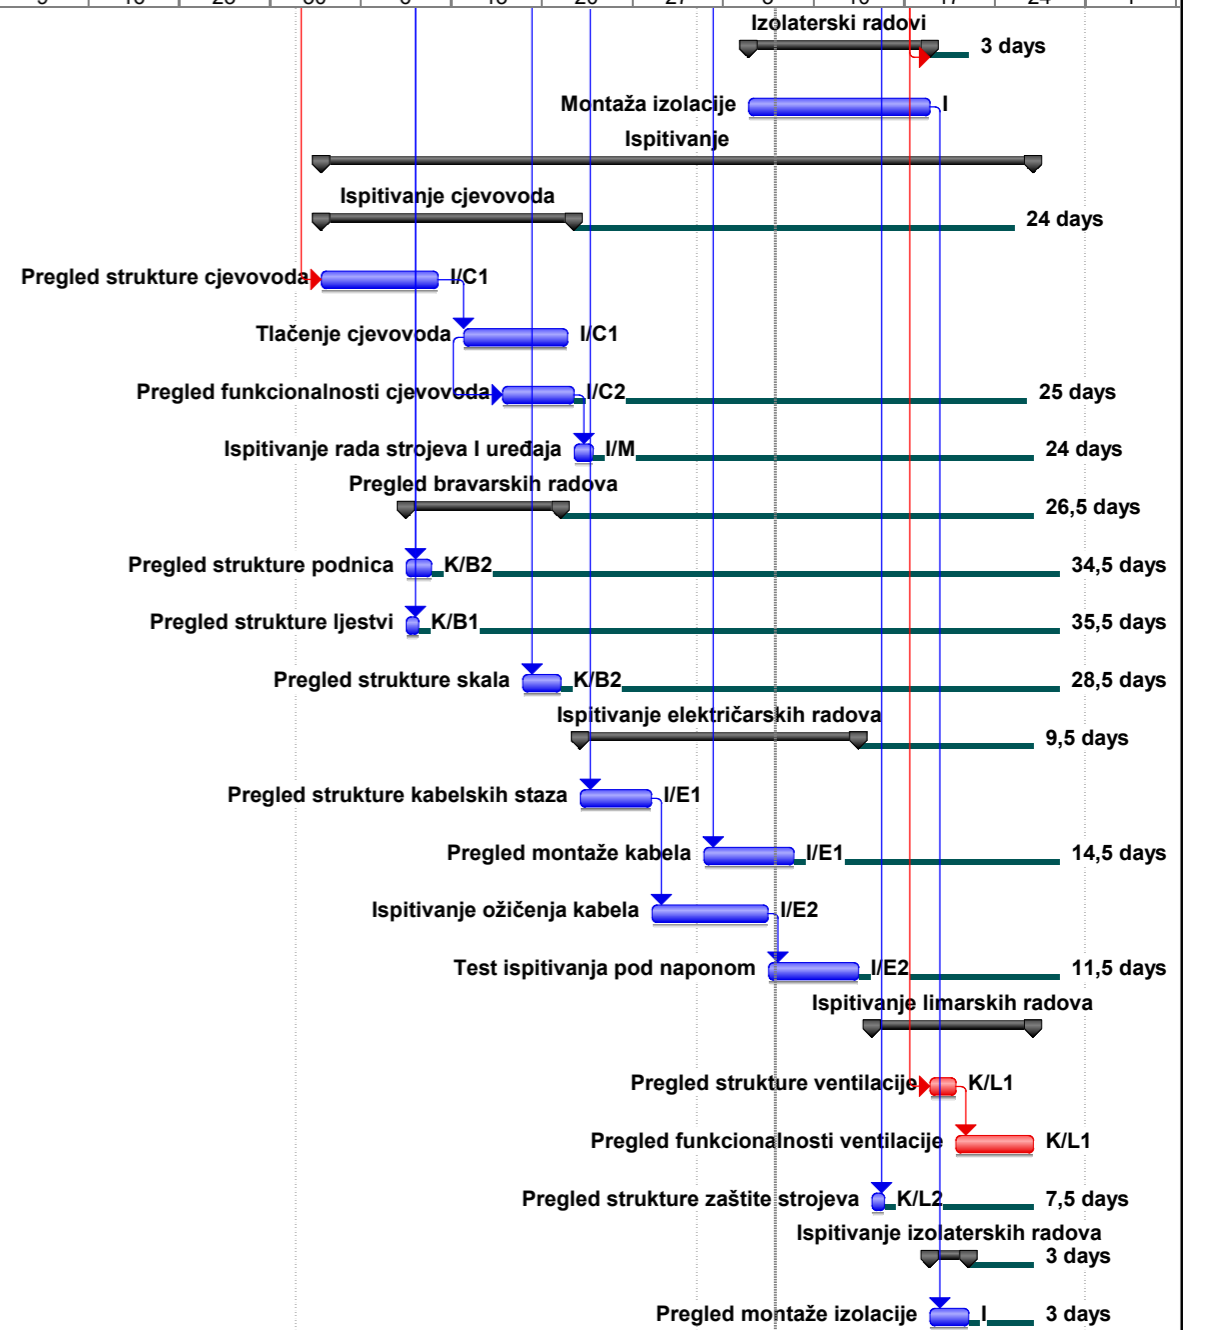

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

|                |  |           |  |          |  |                    |  |                    |  |
|----------------|--|-----------|--|----------|--|--------------------|--|--------------------|--|
| Critical       |  | Split     |  | Slack    |  | Project Summary    |  | External Tasks     |  |
| Critical Split |  | Progress  |  | Slippage |  | Rolled Up Critical |  | External Milestone |  |
| Task           |  | Milestone |  | Summary  |  | Rolled Up Critical |  | Deadline           |  |

Page 4
