

Prilog - peti slučaj

Butorac, Lovro

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:889398>

Rights / Prava: [In copyright](#)/[Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-06-26**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)




ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23							Aug '23				Sep '23			Oct '23				
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1		
1	OPREMANJE 2. PLATFORME STROJARNICE	59 days	Thu 6.7.23	Tue 26.9.23		\$148.928,00	4.588 hrs		OPREMANJE 2. PLATFORME STROJARNICE																		
2	Montaža temelja	14,25 days	Thu 6.7.23	Wed 26.7.23		\$8.880,00	444 hrs		Montaža temelja																		
3	Montaža temelja 445-003	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari1 (2)[200%]																			
4	Montaža temelja 445-004	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari2 (2)[200%]																			
5	Montaža temelja 452-001	0,75 days	Thu 6.7.23	Fri 7.7.23	3	\$240,00	12 hrs	Bravari1 (2)[200%]																			
6	Montaža temelja 452-005	0,75 days	Thu 6.7.23	Fri 7.7.23	4	\$240,00	12 hrs	Bravari2 (2)[200%]																			
7	Montaža temelja 581-001	0,75 days	Fri 7.7.23	Mon 10.7.23	5	\$240,00	12 hrs	Bravari1 (2)[200%]																			
8	Montaža temelja 581-002	0,75 days	Fri 7.7.23	Mon 10.7.23	6	\$240,00	12 hrs	Bravari2 (2)[200%]																			
9	Montaža temelja 581-003	0,75 days	Mon 10.7.23	Mon 10.7.23	7	\$240,00	12 hrs	Bravari1 (2)[200%]																			
10	Montaža temelja 582-001	0,75 days	Mon 10.7.23	Mon 10.7.23	8	\$240,00	12 hrs	Bravari2 (2)[200%]																			
11	Montaža temelja 582-003/01	0,75 days	Tue 11.7.23	Tue 11.7.23	9	\$240,00	12 hrs	Bravari1 (2)[200%]																			
12	Montaža temelja 582-003/02	0,75 days	Tue 11.7.23	Tue 11.7.23	10	\$240,00	12 hrs	Bravari2 (2)[200%]																			
13	Montaža temelja 644-008/01	0,75 days	Tue 11.7.23	Wed 12.7.23	11	\$240,00	12 hrs	Bravari1 (2)[200%]																			
14	Montaža temelja 644-008/02	0,75 days	Tue 11.7.23	Wed 12.7.23	12	\$240,00	12 hrs	Bravari2 (2)[200%]																			
15	Montaža temelja 651-001	0,75 days	Wed 12.7.23	Thu 13.7.23	13	\$240,00	12 hrs	Bravari1 (2)[200%]																			
16	Montaža temelja 651-002	0,75 days	Wed 12.7.23	Thu 13.7.23	14	\$240,00	12 hrs	Bravari2 (2)[200%]																			
17	Montaža temelja 651-003	0,75 days	Thu 13.7.23	Thu 13.7.23	15	\$240,00	12 hrs	Bravari1 (2)[200%]																			
18	Montaža temelja 702-001	0,75 days	Thu 13.7.23	Thu 13.7.23	16	\$240,00	12 hrs	Bravari2 (2)[200%]																			
19	Montaža temelja 702-004	0,75 days	Fri 14.7.23	Fri 14.7.23	17	\$240,00	12 hrs	Bravari1 (2)[200%]																			
20	Montaža temelja 702-005	0,75 days	Fri 14.7.23	Fri 14.7.23	18	\$240,00	12 hrs	Bravari2 (2)[200%]																			
21	Montaža temelja 703-001	0,75 days	Fri 14.7.23	Mon 17.7.23	19	\$240,00	12 hrs	Bravari1 (2)[200%]																			
22	Montaža temelja 703-002	0,75 days	Fri 14.7.23	Mon 17.7.23	20	\$240,00	12 hrs	Bravari2 (2)[200%]																			
23	Montaža temelja 712-001	0,75 days	Mon 17.7.23	Tue 18.7.23	21	\$240,00	12 hrs	Bravari1 (2)[200%]																			
24	Montaža temelja 713-007	0,75 days	Mon 17.7.23	Tue 18.7.23	22	\$240,00	12 hrs	Bravari2 (2)[200%]																			
25	Montaža temelja 714-001	0,75 days	Tue 18.7.23	Tue 18.7.23	23	\$240,00	12 hrs	Bravari1 (2)[200%]																			
26	Montaža temelja 756-001/02	0,75 days	Tue 18.7.23	Tue 18.7.23	24	\$240,00	12 hrs	Bravari2 (2)[200%]																			
27	Montaža temelja 722-011	0,75 days	Wed 19.7.23	Wed 19.7.23	25	\$240,00	12 hrs	Bravari1 (2)[200%]																			
28	Montaža temelja 731-001/01	0,75 days	Wed 19.7.23	Wed 19.7.23	26	\$240,00	12 hrs	Bravari2 (2)[200%]																			
29	Montaža temelja 731-001/02	0,75 days	Wed 19.7.23	Thu 20.7.23	27	\$240,00	12 hrs	Bravari1 (2)[200%]																			
30	Montaža temelja 731-002	0,75 days	Wed 19.7.23	Thu 20.7.23	28	\$240,00	12 hrs	Bravari2 (2)[200%]																			
31	Montaža temelja 731-003/01	0,75 days	Thu 20.7.23	Fri 21.7.23	29	\$240,00	12 hrs	Bravari1 (2)[200%]																			

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	


ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23					Aug '23					Sep '23			Oct '23					
									11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1		
32	Montaža temelja 731-003/01	0,75 days	Thu 20.7.23	Fri 21.7.23	30	\$240,00	12 hrs	Bravari2 (2)[200%]																			
33	Montaža temelja 733-001	0,75 days	Fri 21.7.23	Fri 21.7.23	31	\$240,00	12 hrs	Bravari1 (2)[200%]																			
34	Montaža temelja 733-012	0,75 days	Fri 21.7.23	Fri 21.7.23	32	\$240,00	12 hrs	Bravari2 (2)[200%]																			
35	Montaža temelja 734-001	0,75 days	Mon 24.7.23	Mon 24.7.23	33	\$240,00	12 hrs	Bravari1 (2)[200%]																			
36	Montaža temelja 743-002	0,75 days	Mon 24.7.23	Mon 24.7.23	34	\$240,00	12 hrs	Bravari2 (2)[200%]																			
37	Montaža temelja 743-003	0,75 days	Mon 24.7.23	Tue 25.7.23	35	\$240,00	12 hrs	Bravari1 (2)[200%]																			
38	Montaža temelja 751-001	0,75 days	Mon 24.7.23	Tue 25.7.23	36	\$240,00	12 hrs	Bravari2 (2)[200%]																			
39	Montaža temelja 756-004	0,75 days	Tue 25.7.23	Wed 26.7.23	37	\$240,00	12 hrs	Bravari1 (2)[200%]																			
40	Montaža strojeva I uređaja	9,5 days	Mon 17.7.23	Fri 28.7.23	2FS-7 days	\$7.104,00	296 hrs																				
41	Montaža 445-003	0,5 days	Mon 17.7.23	Mon 17.7.23		\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
42	Montaža 445-004	0,5 days	Mon 17.7.23	Mon 17.7.23		\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
43	Montaža 452-001	0,5 days	Mon 17.7.23	Tue 18.7.23	41	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
44	Montaža 452-005	0,5 days	Mon 17.7.23	Tue 18.7.23	42	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
45	Montaža 581-001	0,5 days	Tue 18.7.23	Tue 18.7.23	43	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
46	Montaža 581-002	0,5 days	Tue 18.7.23	Tue 18.7.23	44	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
47	Montaža 581-003	0,5 days	Tue 18.7.23	Wed 19.7.23	45	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
48	Montaža 582-001	0,5 days	Tue 18.7.23	Wed 19.7.23	46	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
49	Montaža 582-003/01	0,5 days	Wed 19.7.23	Wed 19.7.23	47	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
50	Montaža 582-003/02	0,5 days	Wed 19.7.23	Wed 19.7.23	48	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
51	Montaža 644-008/01	0,5 days	Wed 19.7.23	Thu 20.7.23	49	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
52	Montaža 644-008/02	0,5 days	Wed 19.7.23	Thu 20.7.23	50	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
53	Montaža 651-001	0,5 days	Thu 20.7.23	Thu 20.7.23	51	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
54	Montaža 651-002	0,5 days	Thu 20.7.23	Thu 20.7.23	52	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
55	Montaža 651-003	0,5 days	Thu 20.7.23	Fri 21.7.23	53	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
56	Montaža 702-001	0,5 days	Thu 20.7.23	Fri 21.7.23	54	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
57	Montaža 702-004	0,5 days	Fri 21.7.23	Fri 21.7.23	55	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
58	Montaža 702-005	0,5 days	Fri 21.7.23	Fri 21.7.23	56	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
59	Montaža 703-001	0,5 days	Fri 21.7.23	Mon 24.7.23	57	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
60	Montaža 703-002	0,5 days	Fri 21.7.23	Mon 24.7.23	58	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			
61	Montaža 712-001	0,5 days	Mon 24.7.23	Mon 24.7.23	59	\$192,00	8 hrs	Mehaničari1 (2)[200%]																			
62	Montaža 713-007	0,5 days	Mon 24.7.23	Mon 24.7.23	60	\$192,00	8 hrs	Mehaničari2 (2)[200%]																			

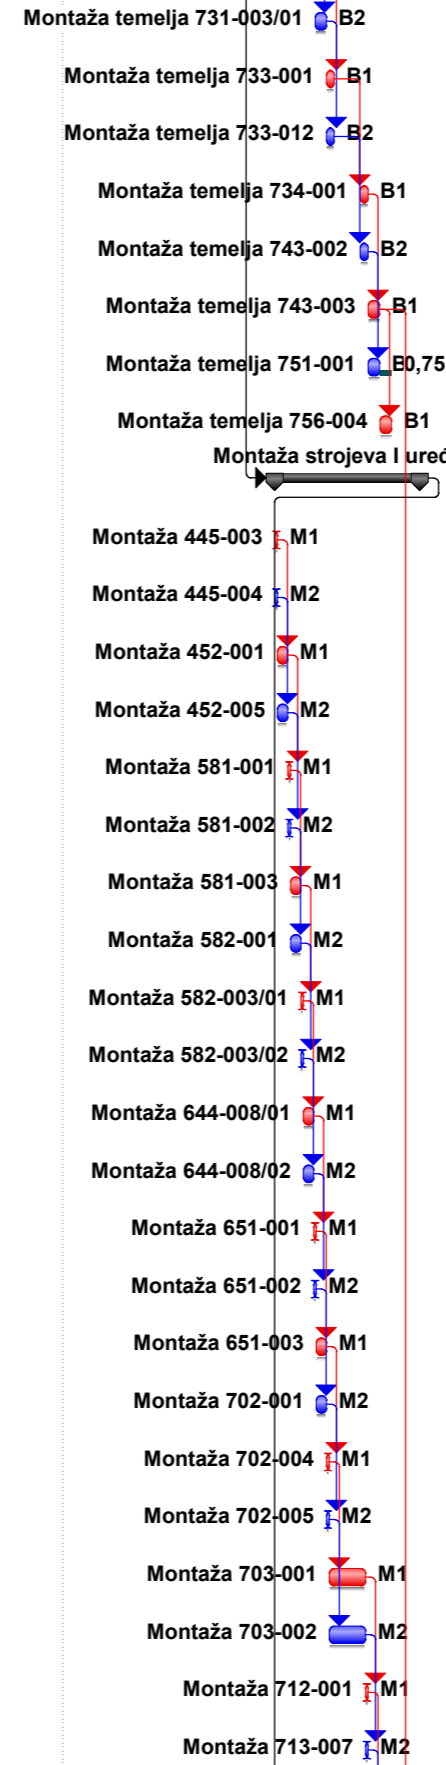

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23


Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Jul '23			Aug '23				Sep '23			Oct '23	
									11	18	25	2	9	16	23	30	6	13	20	27
63	Montaža 714-001	0,5 days	Mon 24.7.23	Tue 25.7.23	61	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
64	Montaža 756-001/02	0,5 days	Mon 24.7.23	Tue 25.7.23	62	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
65	Montaža 722-011	0,5 days	Tue 25.7.23	Tue 25.7.23	63	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
66	Montaža 731-001/01	0,5 days	Tue 25.7.23	Tue 25.7.23	64	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
67	Montaža 731-001/02	0,5 days	Tue 25.7.23	Wed 26.7.23	65	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
68	Montaža 731-002	0,5 days	Tue 25.7.23	Wed 26.7.23	66	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
69	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	67	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
70	Montaža 731-003/01	0,5 days	Wed 26.7.23	Wed 26.7.23	68	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
71	Montaža 733-001	0,5 days	Wed 26.7.23	Thu 27.7.23	69	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
72	Montaža 733-012	0,5 days	Wed 26.7.23	Thu 27.7.23	70	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
73	Montaža 734-001	0,5 days	Thu 27.7.23	Thu 27.7.23	71	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
74	Montaža 743-002	0,5 days	Thu 27.7.23	Thu 27.7.23	72	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
75	Montaža 743-003	0,5 days	Thu 27.7.23	Fri 28.7.23	73	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
76	Montaža 751-001	0,5 days	Thu 27.7.23	Fri 28.7.23	74	\$192,00	8 hrs	Mehaničari2 (2)[200%]												
77	Montaža 756-004	0,5 days	Fri 28.7.23	Fri 28.7.23	75	\$192,00	8 hrs	Mehaničari1 (2)[200%]												
78	Cjevarski radovi	20,25 days	Wed 19.7.23	Wed 16.8.23	40FS-7 days	\$39.072,00	888 hrs													
79	Montaža prolaza	5,25 days	Wed 19.7.23	Wed 26.7.23		\$7.392,00	168 hrs	Cjevari1 (4)[400%]												
80	Montaža nosača	7,5 days	Thu 20.7.23	Mon 31.7.23	79FS-5 days	\$10.560,00	240 hrs	Cjevari2 (4)[400%]												
81	Montaža cijevi	15 days	Thu 27.7.23	Wed 16.8.23	79	\$21.120,00	480 hrs	Cjevari1 (4)[400%]												
82	Bravarski radovi	17,5 days	Wed 26.7.23	Fri 18.8.23	78FS-16 days	\$8.480,00	424 hrs													
83	Montaža podnica	10,5 days	Wed 26.7.23	Wed 9.8.23		\$3.360,00	168 hrs	Bravari2 (2)[200%]												
84	Montaža ljestvi	9 days	Thu 27.7.23	Wed 9.8.23	37FS+2 days	\$2.880,00	144 hrs	Bravari1 (2)[200%]												
85	Montaža skala	7 days	Wed 9.8.23	Fri 18.8.23	83	\$2.240,00	112 hrs	Bravari2 (2)[200%]												
86	Električarski radovi	24 days	Mon 31.7.23	Fri 1.9.23	80	\$54.144,00	1.128 hrs													
87	Montaža kablinskih prolaza	5,25 days	Mon 31.7.23	Mon 7.8.23		\$8.064,00	168 hrs	Električari1 (4)[400%]												
88	Montaža kablinskih staza	11,25 days	Mon 7.8.23	Tue 22.8.23	87	\$17.280,00	360 hrs	Električari1 (4)[400%]												
89	Provlačenje kabela	18,75 days	Mon 7.8.23	Fri 1.9.23	87	\$28.800,00	600 hrs	Električari2 (4)[400%]												
90	Limarski radovi	15 days	Thu 31.8.23	Wed 20.9.23	78FS+10 days	\$8.160,00	408 hrs													
91	Montaža ventilacijskih prolaza	7 days	Thu 31.8.23	Fri 8.9.23		\$2.240,00	112 hrs	Limari2 (2)[200%]												
92	Montaža ventilacijskih kanala	15 days	Thu 31.8.23	Wed 20.9.23		\$4.800,00	240 hrs	Limari1 (2)[200%]												
93	Montaža zaštite strojeva I uređaja	3,5 days	Mon 11.9.23	Thu 14.9.23	91	\$1.120,00	56 hrs	Limari2 (2)[200%]												

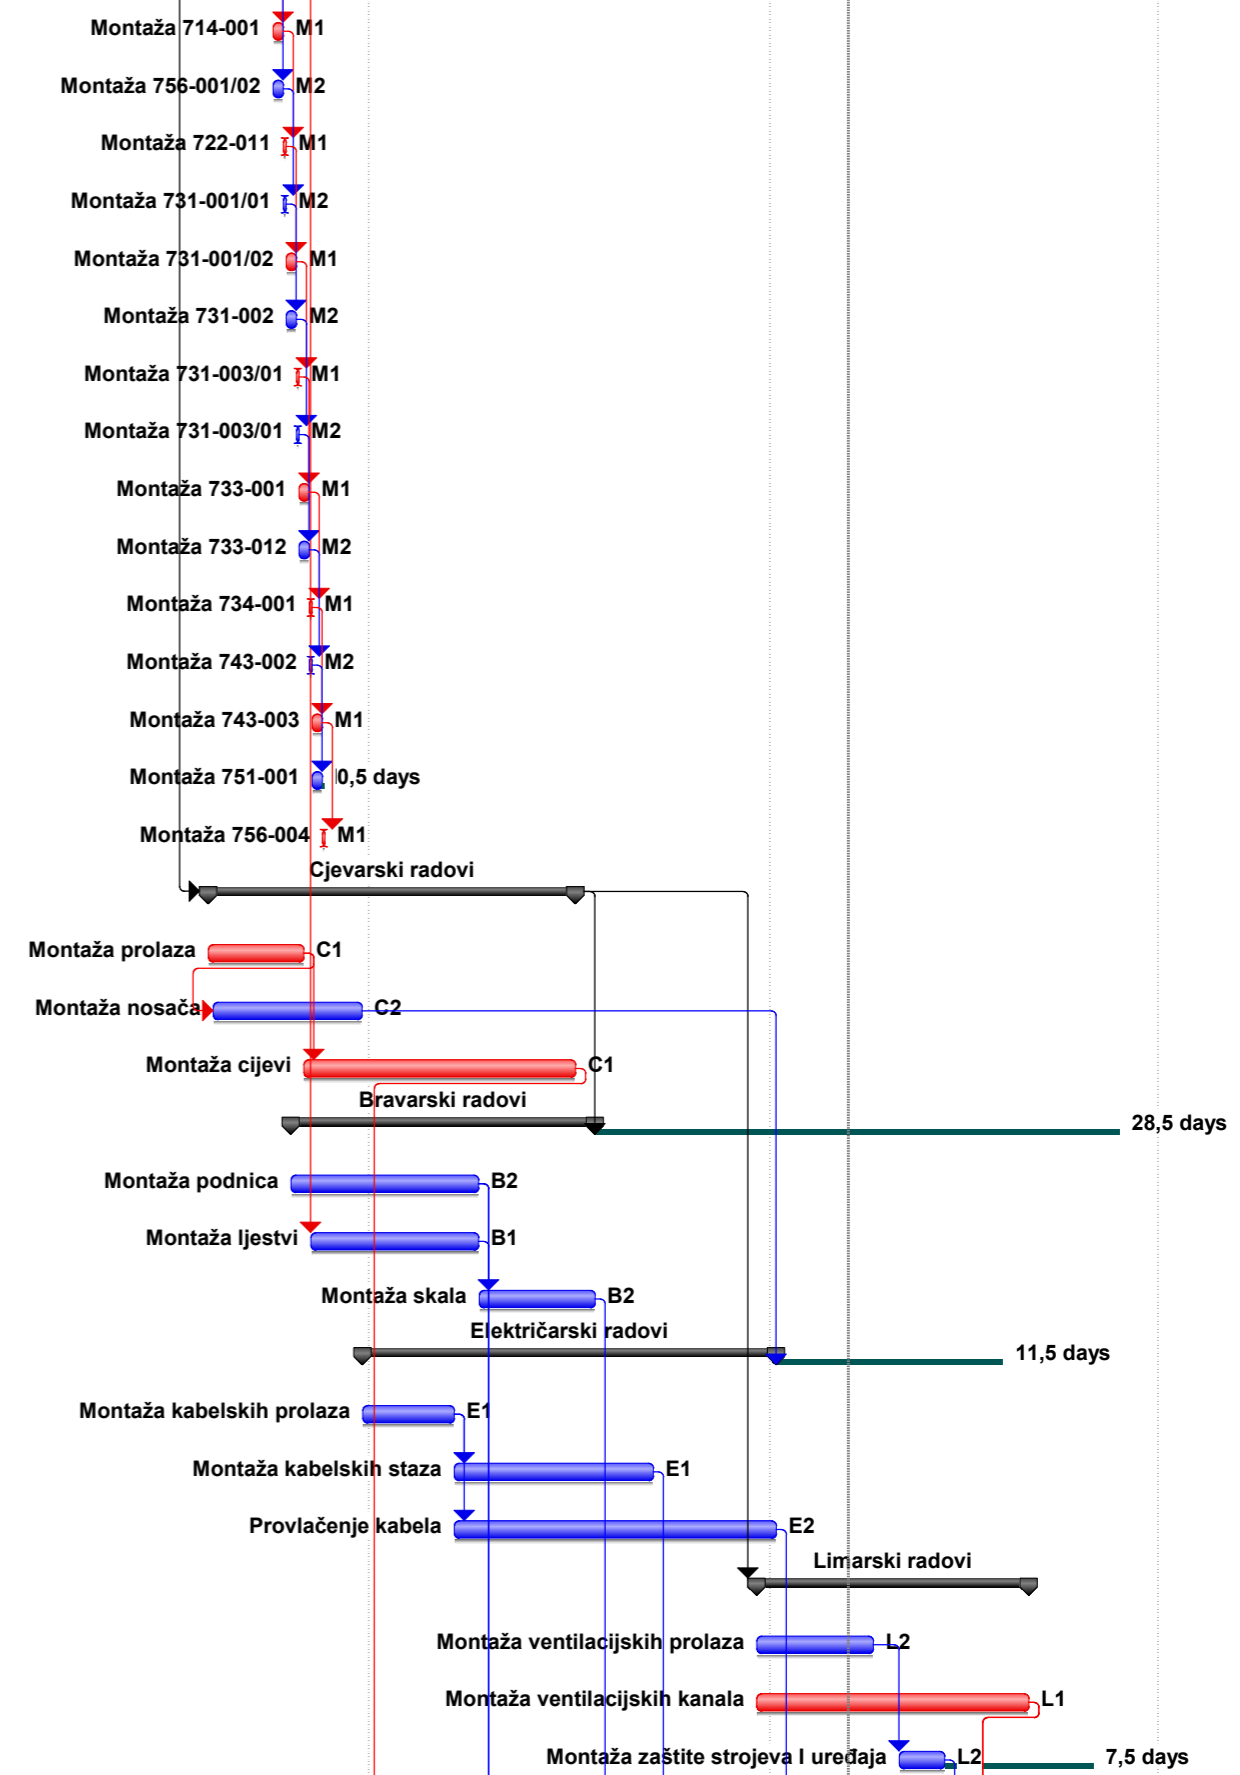

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

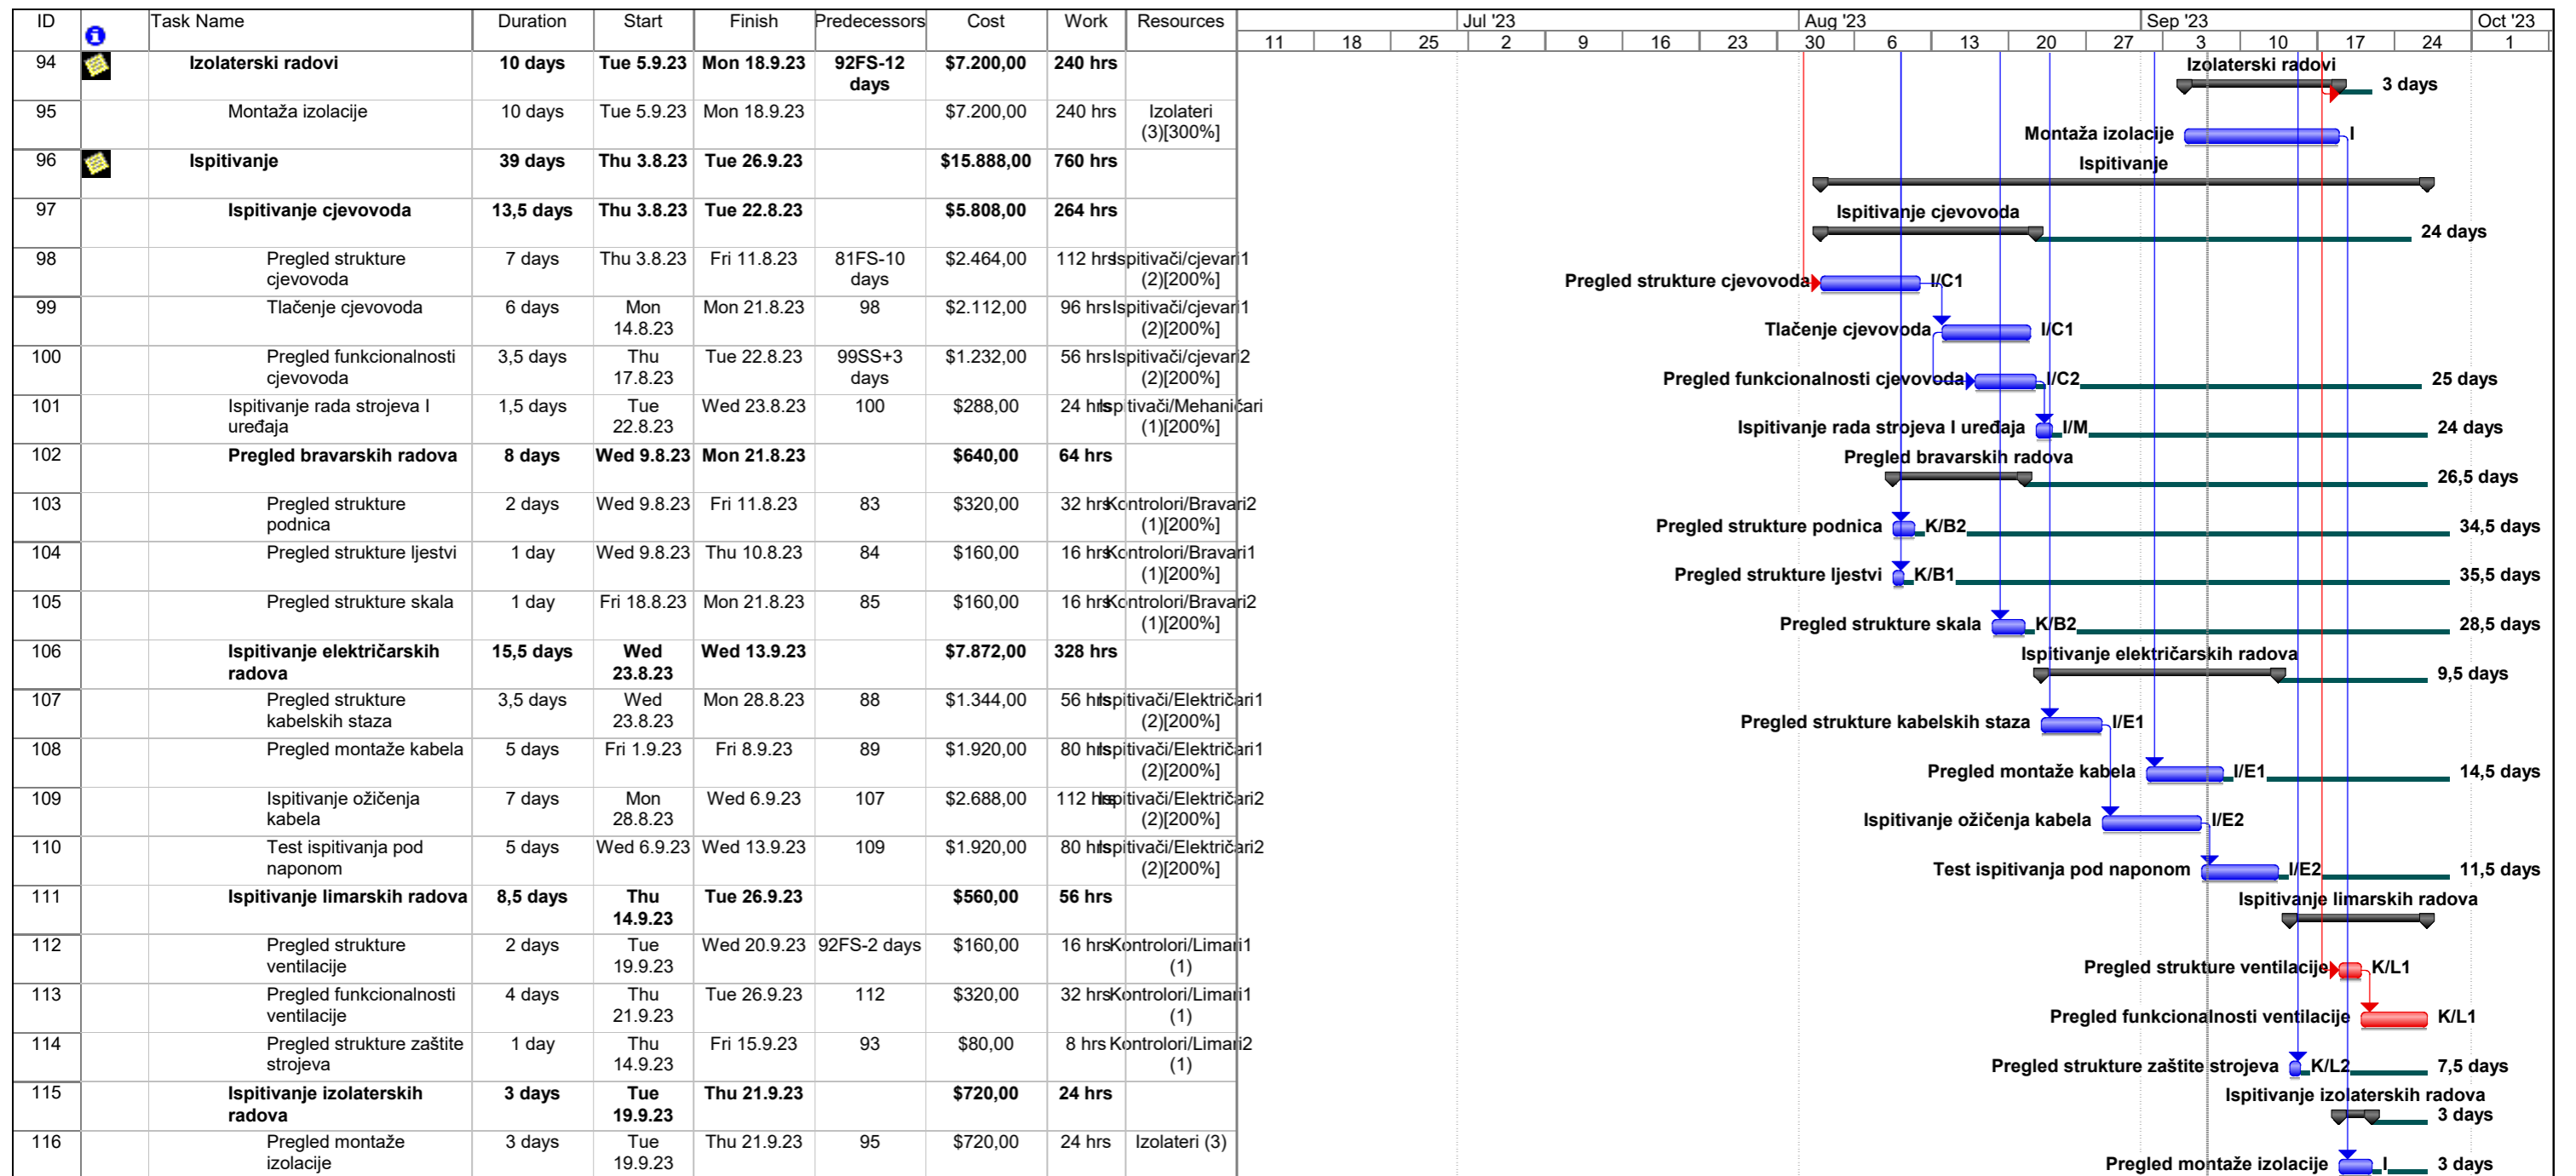

Project: OPREMANJE 2 PLATFORME
Date: Thu 7.9.23

