

Prilog 1

Ćosić, Matej

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:670294>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2024-12-12**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023		Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023		Qtr 1, 202
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
1	OPREMANJE KROVA DVODNA STROJARNICE	235,6 days	Mon 12.12.22	105.563,20 €	3.164,8 hrs	Mon 6.11.23	OPREMANJE KROVA DVODNA STROJARNICE										
2	Montaža temelja	17 days	Mon 12.12.22	2.720,00 €	136 hrs	Tue 3.1.23	Montaža temelja										
3	Montaža temelja 382-002/01	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	↓ Bravari (2)										
4	Montaža temelja 382-002/02	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	↓ Bravari (2)										
5	Montaža temelja 601-001	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	↓ Bravari (2)										
6	Montaža temelja 601-019	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	↓ Bravari (2)										
7	Montaža temelja 631-014	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	↓ Bravari (2)										
8	Montaža temelja 631-015	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	↓ Bravari (2)										
9	Montaža temelja 631-016	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	↓ Bravari (2)										
10	Montaža temelja 631-022	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	↓ Bravari (2)										
11	Montaža temelja 701-001/01	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	↓ Bravari (2)										
12	Montaža temelja 701-001/02	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	↓ Bravari (2)										
13	Montaža temelja 701-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	↓ Bravari (2)										
14	Montaža temelja 702-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	↓ Bravari (2)										
15	Montaža temelja 702-003	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	↓ Bravari (2)										
16	Montaža temelja 711-001	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	↓ Bravari (2)										
17	Montaža temelja 712-002/01	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	↓ Bravari (2)										
18	Montaža temelja 712-002/02	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	↓ Bravari (2)										
19	Montaža temelja 713-001/01	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22	↓ Bravari (2)										
20	Montaža temelja 713-001/02	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22	↓ Bravari (2)										
21	Montaža temelja 713-009	0,5 days	Fri 23.12.22	80,00 €	4 hrs	Fri 23.12.22	↓ Bravari (2)										
22	Montaža temelja 721-001/01	0,5 days	Fri 23.12.22	80,00 €	4 hrs	Fri 23.12.22	↓ Bravari (2)										
23	Montaža temelja 721-001/02	0,5 days	Mon 26.12.22	80,00 €	4 hrs	Mon 26.12.22	↓ Bravari (2)										
24	Montaža temelja 721-001/03	0,5 days	Mon 26.12.22	80,00 €	4 hrs	Mon 26.12.22	↓ Bravari (2)										
25	Montaža temelja 756-001/01	0,5 days	Tue 27.12.22	80,00 €	4 hrs	Tue 27.12.22	↓ Bravari (2)										
26	Montaža temelja 756-001/02	0,5 days	Tue 27.12.22	80,00 €	4 hrs	Tue 27.12.22	↓ Bravari (2)										
27	Montaža temelja 756-002/01	0,5 days	Wed 28.12.22	80,00 €	4 hrs	Wed 28.12.22	↓ Bravari (2)										
28	Montaža temelja 756-002/02	0,5 days	Wed 28.12.22	80,00 €	4 hrs	Wed 28.12.22	↓ Bravari (2)										
29	Montaža temelja 756-003	0,5 days	Thu 29.12.22	80,00 €	4 hrs	Thu 29.12.22	↓ Bravari (2)										
30	Montaža temelja 761-002	0,5 days	Thu 29.12.22	80,00 €	4 hrs	Thu 29.12.22	↓ Bravari (2)										
31	Montaža temelja 803-001	0,5 days	Fri 30.12.22	80,00 €	4 hrs	Fri 30.12.22	↓ Bravari (2)										

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023		Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 202	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
32	Montaža temelja 803-002	0,5 days	Fri 30.12.22	80,00 €	4 hrs	Fri 30.12.22													
33	Montaža temelja 803-003	0,5 days	Mon 2.1.23	80,00 €	4 hrs	Mon 2.1.23													
34	Montaža temelja 803-004	0,5 days	Mon 2.1.23	80,00 €	4 hrs	Mon 2.1.23													
35	Montaža temelja 813-001/01	0,5 days	Tue 3.1.23	80,00 €	4 hrs	Tue 3.1.23													
36	Montaža temelja 813-001/02	0,5 days	Tue 3.1.23	80,00 €	4 hrs	Tue 3.1.23													
37	Montaža strojeva I uređaja	13,6 days	Mon 26.12.22	2.611,20 €	108,8 hrs	Thu 12.1.23													
38	Montaža 382-002/01	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Mon 26.12.22													
39	Montaža 382-002/02	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Mon 26.12.22													
40	Montaža 601-001	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Tue 27.12.22													
41	Montaža 601-019	0,4 days	Tue 27.12.22	76,80 €	3,2 hrs	Tue 27.12.22													
42	Montaža 631-014	0,4 days	Tue 27.12.22	76,80 €	3,2 hrs	Tue 27.12.22													
43	Montaža 631-015	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Wed 28.12.22													
44	Montaža 631-016	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Wed 28.12.22													
45	Montaža 631-022	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Thu 29.12.22													
46	Montaža 701-001/01	0,4 days	Thu 29.12.22	76,80 €	3,2 hrs	Thu 29.12.22													
47	Montaža 701-001/02	0,4 days	Thu 29.12.22	76,80 €	3,2 hrs	Thu 29.12.22													
48	Montaža 701-002	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Fri 30.12.22													
49	Montaža 702-002	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Fri 30.12.22													
50	Montaža 702-003	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Mon 2.1.23													
51	Montaža 711-001	0,4 days	Mon 2.1.23	76,80 €	3,2 hrs	Mon 2.1.23													
52	Montaža 712-002/01	0,4 days	Mon 2.1.23	76,80 €	3,2 hrs	Mon 2.1.23													
53	Montaža 712-002/02	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Tue 3.1.23													
54	Montaža 713-001/01	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Tue 3.1.23													
55	Montaža 713-001/02	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Wed 4.1.23													
56	Montaža 713-009	0,4 days	Wed 4.1.23	76,80 €	3,2 hrs	Wed 4.1.23													
57	Montaža 721-001/01	0,4 days	Wed 4.1.23	76,80 €	3,2 hrs	Wed 4.1.23													
58	Montaža 721-001/02	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Thu 5.1.23													
59	Montaža 721-001/03	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Thu 5.1.23													
60	Montaža 756-001/01	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Fri 6.1.23													
61	Montaža 756-001/02	0,4 days	Fri 6.1.23	76,80 €	3,2 hrs	Fri 6.1.23													
62	Montaža 756-002/01	0,4 days	Fri 6.1.23	76,80 €	3,2 hrs	Fri 6.1.23													

Montaža strojeva I uređaja

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			


ID	Task Name	Duration	Start	Cost	Work	Finish	Nov		Dec		Qtr 1, 2023		Qtr 2, 2023		Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2022			
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan			
63	Montaža 756-002/02	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Mon 9.1.23																		
64	Montaža 756-003	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Mon 9.1.23																		
65	Montaža 761-002	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Tue 10.1.23																		
66	Montaža 803-001	0,4 days	Tue 10.1.23	76,80 €	3,2 hrs	Tue 10.1.23																		
67	Montaža 803-002	0,4 days	Tue 10.1.23	76,80 €	3,2 hrs	Tue 10.1.23																		
68	Montaža 803-003	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Wed 11.1.23																		
69	Montaža 803-004	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Wed 11.1.23																		
70	Montaža 813-001/01	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Thu 12.1.23																		
71	Montaža 813-001/02	0,4 days	Thu 12.1.23	76,80 €	3,2 hrs	Thu 12.1.23																		
72	Cjevarski radovi	85 days	Tue 3.1.23	29.920,00 €	680 hrs	Tue 2.5.23																		
73	Montaža prolaza	15 days	Tue 3.1.23	5.280,00 €	120 hrs	Tue 24.1.23																		
74	Montaža nosača	25 days	Tue 24.1.23	8.800,00 €	200 hrs	Tue 28.2.23																		
75	Montaža cijevi	45 days	Tue 28.2.23	15.840,00 €	360 hrs	Tue 2.5.23																		
76	Bravarski radovi	32 days	Tue 21.3.23	5.120,00 €	256 hrs	Thu 4.5.23																		
77	Montaža podnica	13 days	Tue 21.3.23	2.080,00 €	104 hrs	Fri 7.4.23																		
78	Montaža ljestvi	12 days	Fri 7.4.23	1.920,00 €	96 hrs	Tue 25.4.23																		
79	Montaža skala	7 days	Tue 25.4.23	1.120,00 €	56 hrs	Thu 4.5.23																		
80	Električarski radovi	100 days	Tue 2.5.23	38.400,00 €	800 hrs	Tue 19.9.23																		
81	Montaža kablskih prolaza	10 days	Tue 2.5.23	3.840,00 €	80 hrs	Tue 16.5.23																		
82	Montaža kablskih staza	30 days	Tue 16.5.23	11.520,00 €	240 hrs	Tue 27.6.23																		
83	Provlačenje kabela	60 days	Tue 27.6.23	23.040,00 €	480 hrs	Tue 19.9.23																		
84	Limarski radovi	38 days	Tue 30.5.23	6.080,00 €	304 hrs	Fri 21.7.23																		
85	Montaža ventilacijskih prolaza	10 days	Tue 30.5.23	1.600,00 €	80 hrs	Tue 13.6.23																		
86	Montaža ventilacijskih kanala	21 days	Tue 13.6.23	3.360,00 €	168 hrs	Wed 12.7.23																		
87	Montaža zaštita strojeva I uređaja	7 days	Wed 12.7.23	1.120,00 €	56 hrs	Fri 21.7.23																		
88	Izolaterski radovi	15 days	Wed 12.7.23	2.400,00 €	120 hrs	Wed 2.8.23																		
89	Montaža izolacije	15 days	Wed 12.7.23	2.400,00 €	120 hrs	Wed 2.8.23																		
90	Ispitivanje	151 days	Fri 7.4.23	18.312,00 €	760 hrs	Mon 6.11.23																		
91	Ispitivanje rada strojeva I uređaja	3 days	Fri 21.4.23	288,00 €	24 hrs	Wed 26.4.23																		
92	Ispitivanje cjevovoda	33 days	Tue 18.4.23	8.712,00 €	264 hrs	Fri 2.6.23																		
93	Pregled strukture cjevovoda	14 days	Tue 18.4.23	3.696,00 €	112 hrs	Mon 8.5.23																		



Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023		Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2022	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
94	Tlačenje cjevovoda	12 days	Mon 8.5.23	3.168,00 €	96 hrs	Wed 24.5.23													
95	Pregled funkcionalnosti cjevovoda	7 days	Wed 24.5.23	1.848,00 €	56 hrs	Fri 2.6.23													
96	Pregled bravarskih radova	21 days	Fri 7.4.23	640,00 €	64 hrs	Mon 8.5.23													
97	Pregled strukture podnica	4 days	Fri 7.4.23	320,00 €	32 hrs	Thu 13.4.23													
98	Pregled strukture ljestvi	2 days	Tue 25.4.23	160,00 €	16 hrs	Thu 27.4.23													
99	Pregled strukture skala	2 days	Thu 4.5.23	160,00 €	16 hrs	Mon 8.5.23													
100	Ispitivanje električarskih radova	94 days	Tue 27.6.23	7.872,00 €	328 hrs	Mon 6.11.23													
101	Pregled strukture kablskih staza	7 days	Tue 27.6.23	1.344,00 €	56 hrs	Thu 6.7.23													
102	Pregled montaže kabela	10 days	Tue 19.9.23	1.920,00 €	80 hrs	Tue 3.10.23													
103	Ispitivanje ožičenja kabela	14 days	Tue 3.10.23	2.688,00 €	112 hrs	Mon 23.10.23													
104	Test ispitivanja pod naponom	10 days	Mon 23.10.23	1.920,00 €	80 hrs	Mon 6.11.23													
105	Ispitivanje limarskih radova	8 days	Wed 12.7.23	560,00 €	56 hrs	Mon 24.7.23													
106	Pregled strukture ventilacije	2 days	Wed 12.7.23	160,00 €	16 hrs	Fri 14.7.23													
107	Pregled funkcionalnosti ventilacije	4 days	Fri 14.7.23	320,00 €	32 hrs	Thu 20.7.23													
108	Pregled strukture zaštite strojeva	1 day	Fri 21.7.23	80,00 €	8 hrs	Mon 24.7.23													
109	Ispitivanje izolaterskih radova	3 days	Wed 2.8.23	240,00 €	24 hrs	Mon 7.8.23													
110	Pregled montaže izolacije	3 days	Wed 2.8.23	240,00 €	24 hrs	Mon 7.8.23													

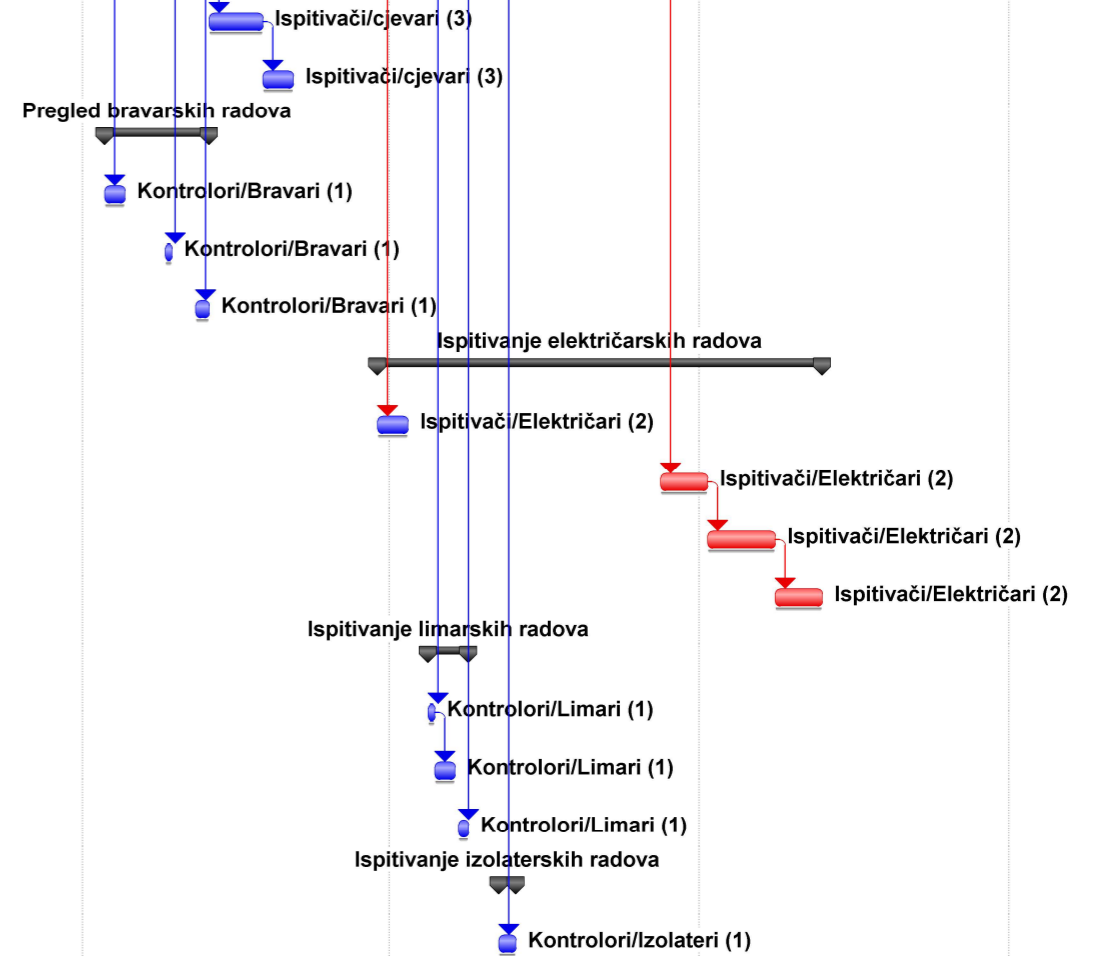

Project: Popis aktivnosti za opremanje Date: Fri 3.3.23	Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
	Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
	Progress		Rolled Up Task		Rolled Up Progress		Project Summary			
