

Prilog 2

Ćosić, Matej

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:824190>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2025-03-10**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



ID	Task Name	Duration	Start	Cost	Work	Finish	OPREMANJE KROVA DVODNA STROJARNICE											
							Nov	Dec	Qtr 1, 2023			Feb	Mar	Qtr 2, 2023		May	Jun	Qtr 3, 2023
1	OPREMANJE KROVA DVODNA STROJARNICE	134,78 days	Mon 12.12.22	174.836,80 €	3.164,8 hrs	Fri 16.6.23	OPREMANJE KROVA DVODNA STROJARNICE											
2	Montaža temelja	11,33 days	Mon 12.12.22	4.080,00 €	136 hrs	Tue 27.12.22	Montaža temelja											
3	Montaža temelja 382-002/01	0,33 days	Mon 12.12.22	120,00 €	4 hrs	Mon 12.12.22	Bravari (3)[150%]											
4	Montaža temelja 382-002/02	0,33 days	Mon 12.12.22	120,00 €	4 hrs	Mon 12.12.22	Bravari (3)[150%]											
5	Montaža temelja 601-001	0,33 days	Mon 12.12.22	120,00 €	4 hrs	Mon 12.12.22	Bravari (3)[150%]											
6	Montaža temelja 601-019	0,33 days	Tue 13.12.22	120,00 €	4 hrs	Tue 13.12.22	Bravari (3)[150%]											
7	Montaža temelja 631-014	0,33 days	Tue 13.12.22	120,00 €	4 hrs	Tue 13.12.22	Bravari (3)[150%]											
8	Montaža temelja 631-015	0,33 days	Tue 13.12.22	120,00 €	4 hrs	Tue 13.12.22	Bravari (3)[150%]											
9	Montaža temelja 631-016	0,33 days	Wed 14.12.22	120,00 €	4 hrs	Wed 14.12.22	Bravari (3)[150%]											
10	Montaža temelja 631-022	0,33 days	Wed 14.12.22	120,00 €	4 hrs	Wed 14.12.22	Bravari (3)[150%]											
11	Montaža temelja 701-001/01	0,33 days	Wed 14.12.22	120,00 €	4 hrs	Wed 14.12.22	Bravari (3)[150%]											
12	Montaža temelja 701-001/02	0,33 days	Thu 15.12.22	120,00 €	4 hrs	Thu 15.12.22	Bravari (3)[150%]											
13	Montaža temelja 701-002	0,33 days	Thu 15.12.22	120,00 €	4 hrs	Thu 15.12.22	Bravari (3)[150%]											
14	Montaža temelja 702-002	0,33 days	Thu 15.12.22	120,00 €	4 hrs	Thu 15.12.22	Bravari (3)[150%]											
15	Montaža temelja 702-003	0,33 days	Fri 16.12.22	120,00 €	4 hrs	Fri 16.12.22	Bravari (3)[150%]											
16	Montaža temelja 711-001	0,33 days	Fri 16.12.22	120,00 €	4 hrs	Fri 16.12.22	Bravari (3)[150%]											
17	Montaža temelja 712-002/01	0,33 days	Fri 16.12.22	120,00 €	4 hrs	Fri 16.12.22	Bravari (3)[150%]											
18	Montaža temelja 712-002/02	0,33 days	Mon 19.12.22	120,00 €	4 hrs	Mon 19.12.22	Bravari (3)[150%]											
19	Montaža temelja 713-001/01	0,33 days	Mon 19.12.22	120,00 €	4 hrs	Mon 19.12.22	Bravari (3)[150%]											
20	Montaža temelja 713-001/02	0,33 days	Mon 19.12.22	120,00 €	4 hrs	Mon 19.12.22	Bravari (3)[150%]											
21	Montaža temelja 713-009	0,33 days	Tue 20.12.22	120,00 €	4 hrs	Tue 20.12.22	Bravari (3)[150%]											
22	Montaža temelja 721-001/01	0,33 days	Tue 20.12.22	120,00 €	4 hrs	Tue 20.12.22	Bravari (3)[150%]											
23	Montaža temelja 721-001/02	0,33 days	Tue 20.12.22	120,00 €	4 hrs	Tue 20.12.22	Bravari (3)[150%]											
24	Montaža temelja 721-001/03	0,33 days	Wed 21.12.22	120,00 €	4 hrs	Wed 21.12.22	Bravari (3)[150%]											
25	Montaža temelja 756-001/01	0,33 days	Wed 21.12.22	120,00 €	4 hrs	Wed 21.12.22	Bravari (3)[150%]											
26	Montaža temelja 756-001/02	0,33 days	Wed 21.12.22	120,00 €	4 hrs	Wed 21.12.22	Bravari (3)[150%]											
27	Montaža temelja 756-002/01	0,33 days	Thu 22.12.22	120,00 €	4 hrs	Thu 22.12.22	Bravari (3)[150%]											
28	Montaža temelja 756-002/02	0,33 days	Thu 22.12.22	120,00 €	4 hrs	Thu 22.12.22	Bravari (3)[150%]											
29	Montaža temelja 756-003	0,33 days	Thu 22.12.22	120,00 €	4 hrs	Thu 22.12.22	Bravari (3)[150%]											
30	Montaža temelja 761-002	0,33 days	Fri 23.12.22	120,00 €	4 hrs	Fri 23.12.22	Bravari (3)[150%]											
31	Montaža temelja 803-001	0,33 days	Fri 23.12.22	120,00 €	4 hrs	Fri 23.12.22	Bravari (3)[150%]											

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23


Task Milestone Rolled Up Critical Task Split Group By Summary

Critical Task Summary Rolled Up Milestone External Tasks Deadline

Progress Rolled Up Task Rolled Up Progress Project Summary

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023		
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
32	Montaža temelja 803-002	0,33 days	Fri 23.12.22	120,00 €	4 hrs	Fri 23.12.22									
33	Montaža temelja 803-003	0,33 days	Mon 26.12.22	120,00 €	4 hrs	Mon 26.12.22									
34	Montaža temelja 803-004	0,33 days	Mon 26.12.22	120,00 €	4 hrs	Mon 26.12.22									
35	Montaža temelja 813-001/01	0,33 days	Mon 26.12.22	120,00 €	4 hrs	Mon 26.12.22									
36	Montaža temelja 813-001/02	0,33 days	Tue 27.12.22	120,00 €	4 hrs	Tue 27.12.22									
37	Montaža strojeva I uređaja	9,07 days	Fri 16.12.22	3.916,80 €	108,8 hrs	Thu 29.12.22									
38	Montaža 382-002/01	0,27 days	Fri 16.12.22	115,20 €	3,2 hrs	Fri 16.12.22									
39	Montaža 382-002/02	0,27 days	Fri 16.12.22	115,20 €	3,2 hrs	Fri 16.12.22									
40	Montaža 601-001	0,27 days	Fri 16.12.22	115,20 €	3,2 hrs	Mon 19.12.22									
41	Montaža 601-019	0,27 days	Mon 19.12.22	115,20 €	3,2 hrs	Mon 19.12.22									
42	Montaža 631-014	0,27 days	Mon 19.12.22	115,20 €	3,2 hrs	Mon 19.12.22									
43	Montaža 631-015	0,27 days	Mon 19.12.22	115,20 €	3,2 hrs	Mon 19.12.22									
44	Montaža 631-016	0,27 days	Mon 19.12.22	115,20 €	3,2 hrs	Tue 20.12.22									
45	Montaža 631-022	0,27 days	Tue 20.12.22	115,20 €	3,2 hrs	Tue 20.12.22									
46	Montaža 701-001/01	0,27 days	Tue 20.12.22	115,20 €	3,2 hrs	Tue 20.12.22									
47	Montaža 701-001/02	0,27 days	Tue 20.12.22	115,20 €	3,2 hrs	Tue 20.12.22									
48	Montaža 701-002	0,27 days	Wed 21.12.22	115,20 €	3,2 hrs	Wed 21.12.22									
49	Montaža 702-002	0,27 days	Wed 21.12.22	115,20 €	3,2 hrs	Wed 21.12.22									
50	Montaža 702-003	0,27 days	Wed 21.12.22	115,20 €	3,2 hrs	Wed 21.12.22									
51	Montaža 711-001	0,27 days	Wed 21.12.22	115,20 €	3,2 hrs	Thu 22.12.22									
52	Montaža 712-002/01	0,27 days	Thu 22.12.22	115,20 €	3,2 hrs	Thu 22.12.22									
53	Montaža 712-002/02	0,27 days	Thu 22.12.22	115,20 €	3,2 hrs	Thu 22.12.22									
54	Montaža 713-001/01	0,27 days	Thu 22.12.22	115,20 €	3,2 hrs	Thu 22.12.22									
55	Montaža 713-001/02	0,27 days	Thu 22.12.22	115,20 €	3,2 hrs	Fri 23.12.22									
56	Montaža 713-009	0,27 days	Fri 23.12.22	115,20 €	3,2 hrs	Fri 23.12.22									
57	Montaža 721-001/01	0,27 days	Fri 23.12.22	115,20 €	3,2 hrs	Fri 23.12.22									
58	Montaža 721-001/02	0,27 days	Fri 23.12.22	115,20 €	3,2 hrs	Fri 23.12.22									
59	Montaža 721-001/03	0,27 days	Fri 23.12.22	115,20 €	3,2 hrs	Mon 26.12.22									
60	Montaža 756-001/01	0,27 days	Mon 26.12.22	115,20 €	3,2 hrs	Mon 26.12.22									
61	Montaža 756-001/02	0,27 days	Mon 26.12.22	115,20 €	3,2 hrs	Mon 26.12.22									
62	Montaža 756-002/01	0,27 days	Mon 26.12.22	115,20 €	3,2 hrs	Mon 26.12.22									


Montaža strojeva I uređaja

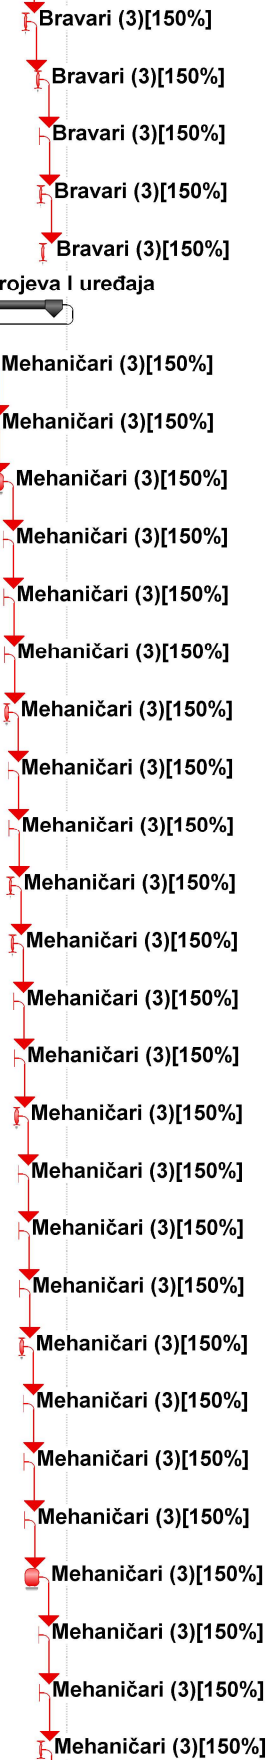

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			


ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023		
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
63	Montaža 756-002/02	0,27 days	Tue 27.12.22	115,20 €	3,2 hrs	Tue 27.12.22									
64	Montaža 756-003	0,27 days	Tue 27.12.22	115,20 €	3,2 hrs	Tue 27.12.22									
65	Montaža 761-002	0,27 days	Tue 27.12.22	115,20 €	3,2 hrs	Tue 27.12.22									
66	Montaža 803-001	0,27 days	Tue 27.12.22	115,20 €	3,2 hrs	Wed 28.12.22									
67	Montaža 803-002	0,27 days	Wed 28.12.22	115,20 €	3,2 hrs	Wed 28.12.22									
68	Montaža 803-003	0,27 days	Wed 28.12.22	115,20 €	3,2 hrs	Wed 28.12.22									
69	Montaža 803-004	0,27 days	Wed 28.12.22	115,20 €	3,2 hrs	Wed 28.12.22									
70	Montaža 813-001/01	0,27 days	Wed 28.12.22	115,20 €	3,2 hrs	Thu 29.12.22									
71	Montaža 813-001/02	0,27 days	Thu 29.12.22	115,20 €	3,2 hrs	Thu 29.12.22									
72	Cjevarski radovi	48,57 days	Tue 20.12.22	52.360,00 €	680 hrs	Fri 24.2.23									
73	Montaža prolaza	8,57 days	Tue 20.12.22	9.240,00 €	120 hrs	Fri 30.12.22									
74	Montaža nosača	14,29 days	Fri 30.12.22	15.400,00 €	200 hrs	Fri 20.1.23									
75	Montaža cijevi	25,71 days	Fri 20.1.23	27.720,00 €	360 hrs	Fri 24.2.23									
76	Bravarski radovi	21,33 days	Fri 13.1.23	7.680,00 €	256 hrs	Tue 14.2.23									
77	Montaža podnica	8,67 days	Fri 13.1.23	3.120,00 €	104 hrs	Thu 26.1.23									
78	Montaža ljestvi	8 days	Thu 26.1.23	2.880,00 €	96 hrs	Tue 7.2.23									
79	Montaža skala	4,67 days	Tue 7.2.23	1.680,00 €	56 hrs	Tue 14.2.23									
80	Električarski radovi	57,14 days	Fri 24.2.23	67.200,00 €	800 hrs	Wed 17.5.23									
81	Montaža kablinskih prolaza	5,71 days	Fri 24.2.23	6.720,00 €	80 hrs	Mon 6.3.23									
82	Montaža kablinskih staza	17,14 days	Mon 6.3.23	20.160,00 €	240 hrs	Wed 29.3.23									
83	Provlačenje kabela	34,29 days	Wed 29.3.23	40.320,00 €	480 hrs	Wed 17.5.23									
84	Limarski radovi	28,67 days	Fri 24.3.23	9.120,00 €	304 hrs	Thu 4.5.23									
85	Montaža ventilacijskih prolaza	6,67 days	Fri 24.3.23	2.400,00 €	80 hrs	Tue 4.4.23									
86	Montaža ventilacijskih kanala	14 days	Fri 7.4.23	5.040,00 €	168 hrs	Thu 27.4.23									
87	Montaža zaštita strojeva I uređaja	4,67 days	Thu 27.4.23	1.680,00 €	56 hrs	Thu 4.5.23									
88	Izolaterski radovi	10 days	Thu 27.4.23	3.600,00 €	120 hrs	Thu 11.5.23									
89	Montaža izolacije	10 days	Thu 27.4.23	3.600,00 €	120 hrs	Thu 11.5.23									
90	Ispitivanje	101,14 days	Thu 26.1.23	26.880,00 €	760 hrs	Fri 16.6.23									
91	Ispitivanje rada strojeva I uređaja	1,5 days	Wed 15.2.23	576,00 €	24 hrs	Fri 17.2.23									
92	Ispitivanje cjevovoda	24,81 days	Fri 10.2.23	11.616,00 €	264 hrs	Fri 17.3.23									
93	Pregled strukture cjevovoda	10,53 days	Fri 10.2.23	4.928,00 €	112 hrs	Mon 27.2.23									

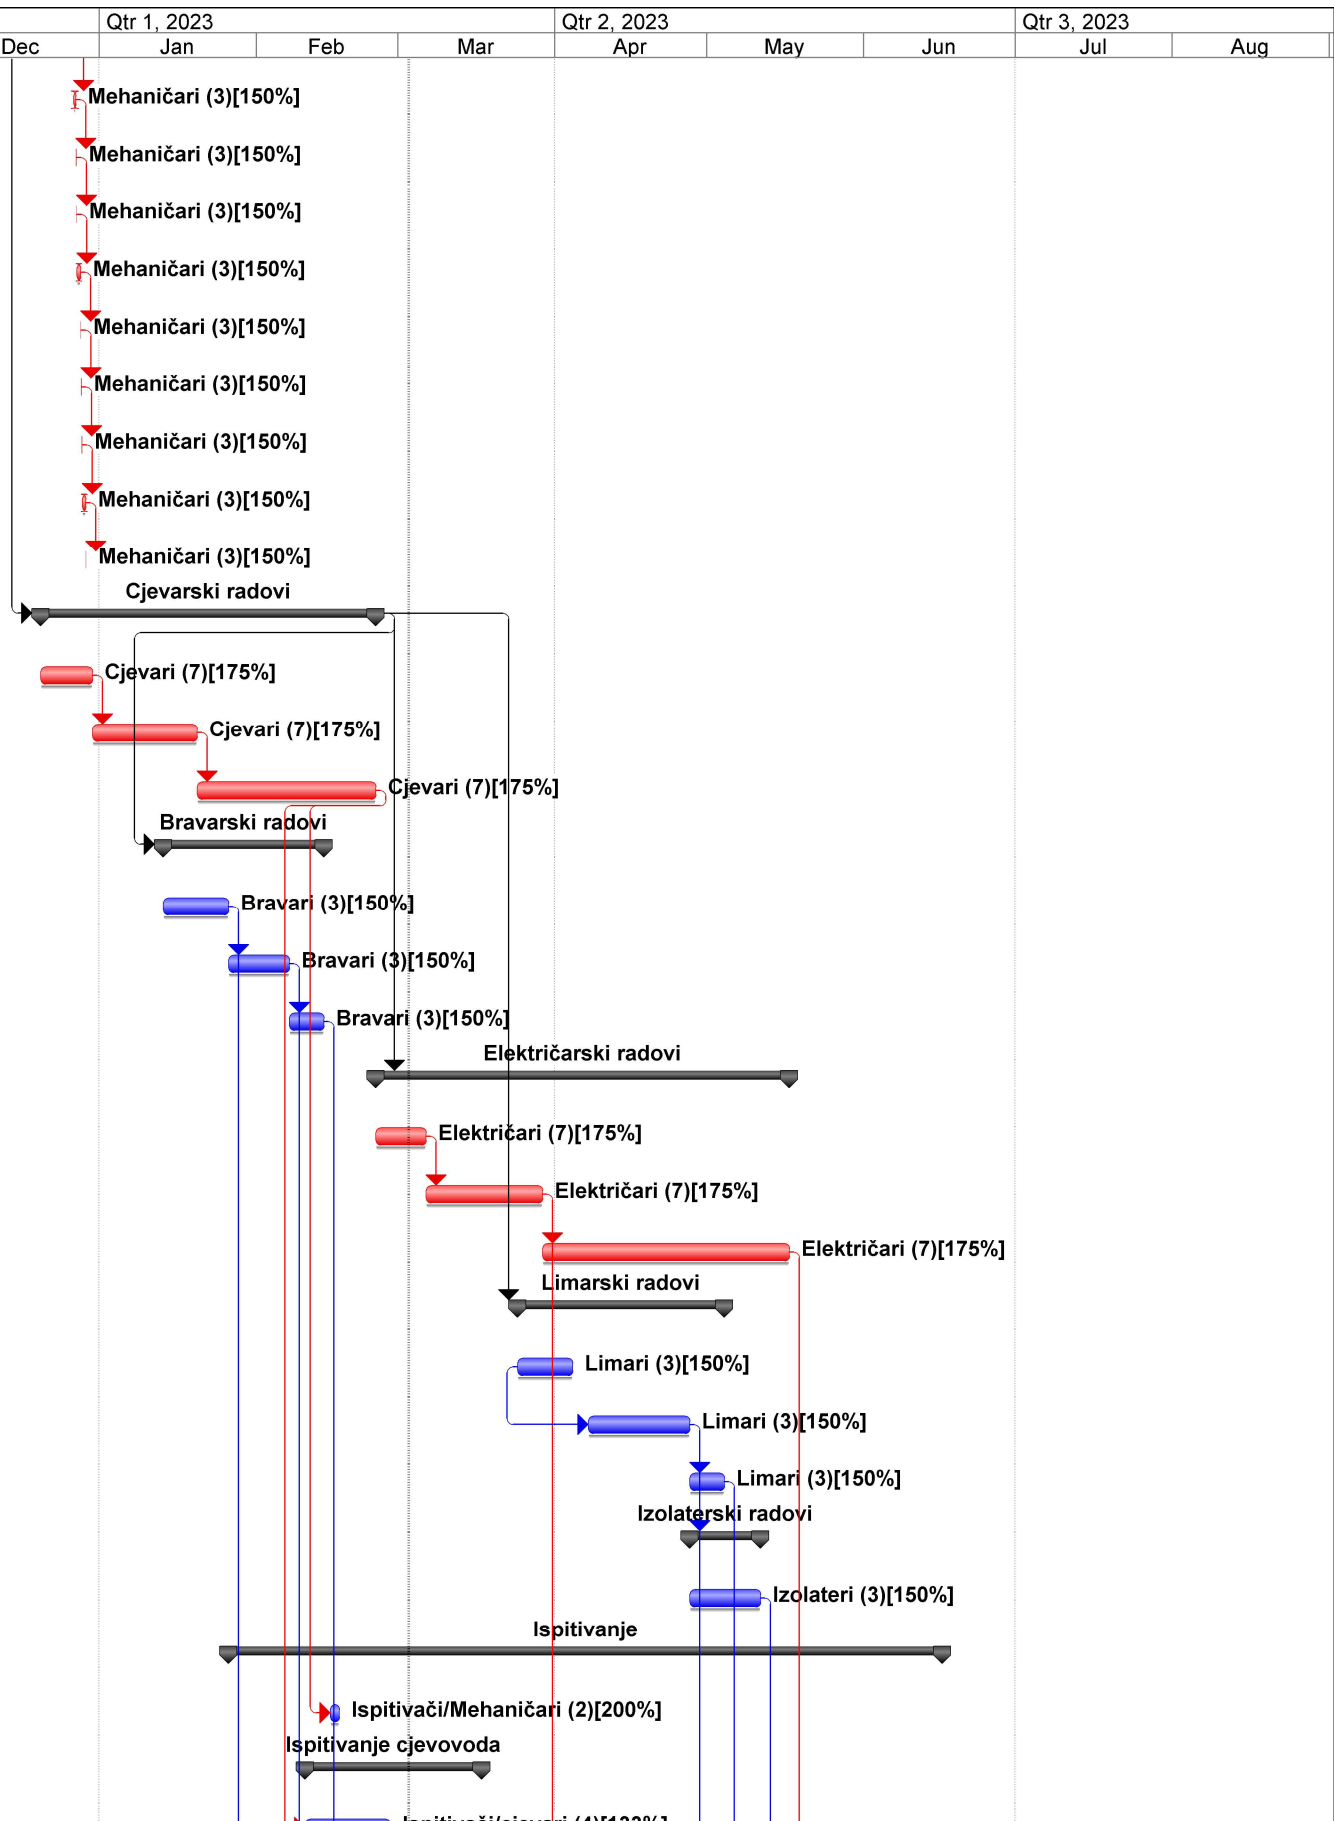

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Nov		Dec		Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023	
									Jan	Feb	Mar	Apr	May	Jun	Jul	Aug		
94	Tlačenje cjevovoda	9,02 days	Mon 27.2.23	4.224,00 €	96 hrs	Fri 10.3.23												
95	Pregled funkcionalnosti cjevovoda	5,26 days	Fri 10.3.23	2.464,00 €	56 hrs	Fri 17.3.23												
96	Pregled bravarskih radova	13,67 days	Thu 26.1.23	1.280,00 €	64 hrs	Wed 15.2.23												
97	Pregled strukture podnica	2 days	Thu 26.1.23	640,00 €	32 hrs	Mon 30.1.23												
98	Pregled strukture ljestvi	1 day	Tue 7.2.23	320,00 €	16 hrs	Wed 8.2.23												
99	Pregled strukture skala	1 day	Tue 14.2.23	320,00 €	16 hrs	Wed 15.2.23												
100	Ispitivanje električarskih radova	56,95 days	Wed 29.3.23	11.808,00 €	328 hrs	Fri 16.6.23												
101	Pregled strukture kablskih staza	4,67 days	Wed 29.3.23	2.016,00 €	56 hrs	Wed 5.4.23												
102	Pregled montaže kabela	6,67 days	Wed 17.5.23	2.880,00 €	80 hrs	Thu 25.5.23												
103	Ispitivanje ožičenja kabela	9,33 days	Thu 25.5.23	4.032,00 €	112 hrs	Thu 8.6.23												
104	Test ispitivanja pod naponom	6,67 days	Thu 8.6.23	2.880,00 €	80 hrs	Fri 16.6.23												
105	Ispitivanje limarskih radova	5,17 days	Thu 27.4.23	1.120,00 €	56 hrs	Fri 5.5.23												
106	Pregled strukture ventilacije	1 day	Thu 27.4.23	320,00 €	16 hrs	Fri 28.4.23												
107	Pregled funkcionalnosti ventilacije	2 days	Fri 28.4.23	640,00 €	32 hrs	Tue 2.5.23												
108	Pregled strukture zaštite strojeva	0,5 days	Thu 4.5.23	160,00 €	8 hrs	Fri 5.5.23												
109	Ispitivanje izolaterskih radova	1,5 days	Thu 11.5.23	480,00 €	24 hrs	Mon 15.5.23												
110	Pregled montaže izolacije	1,5 days	Thu 11.5.23	480,00 €	24 hrs	Mon 15.5.23												

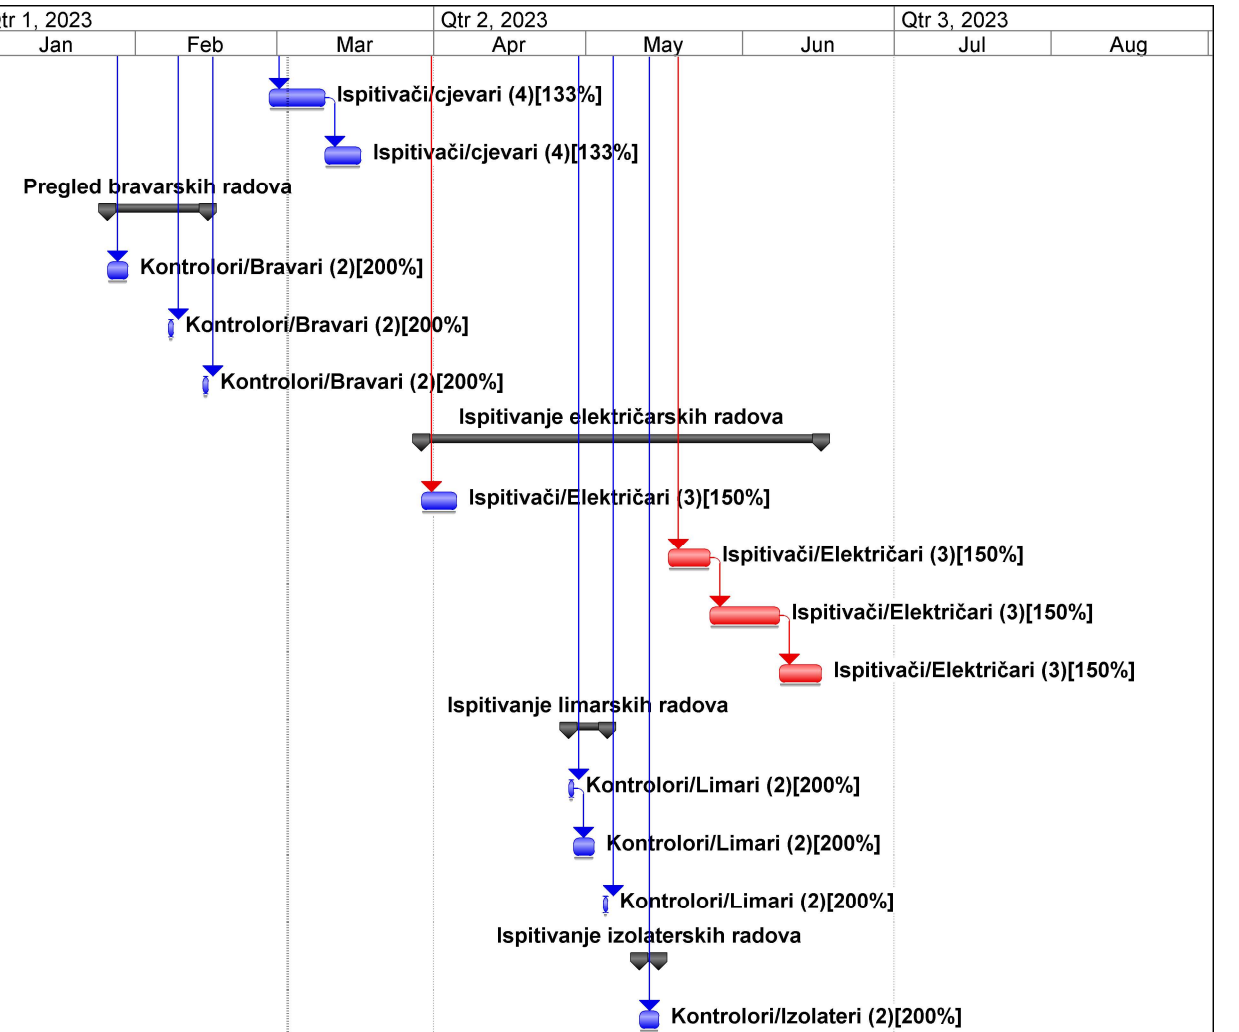

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			
