

Prilog 3

Ćosić, Matej

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:661130>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom](#).

Download date / Datum preuzimanja: **2025-01-06**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)




ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023					
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
1	OPREMANJE KROVA DVODNA STROJARNICE	147,41 days	Mon 12.12.22	164.339,20 €	3.164,8 hrs	Wed 5.7.23	OPREMANJE KROVA DVODNA STROJARNICE											
2	Montaža temelja	17 days	Mon 12.12.22	2.720,00 €	136 hrs	Tue 3.1.23	Montaža temelja											
3	Montaža temelja 382-002/01	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	↓ Bravari (2)											
4	Montaža temelja 382-002/02	0,5 days	Mon 12.12.22	80,00 €	4 hrs	Mon 12.12.22	↓ Bravari (2)											
5	Montaža temelja 601-001	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	↓ Bravari (2)											
6	Montaža temelja 601-019	0,5 days	Tue 13.12.22	80,00 €	4 hrs	Tue 13.12.22	↓ Bravari (2)											
7	Montaža temelja 631-014	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	↓ Bravari (2)											
8	Montaža temelja 631-015	0,5 days	Wed 14.12.22	80,00 €	4 hrs	Wed 14.12.22	↓ Bravari (2)											
9	Montaža temelja 631-016	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	↓ Bravari (2)											
10	Montaža temelja 631-022	0,5 days	Thu 15.12.22	80,00 €	4 hrs	Thu 15.12.22	↓ Bravari (2)											
11	Montaža temelja 701-001/01	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	↓ Bravari (2)											
12	Montaža temelja 701-001/02	0,5 days	Fri 16.12.22	80,00 €	4 hrs	Fri 16.12.22	↓ Bravari (2)											
13	Montaža temelja 701-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	↓ Bravari (2)											
14	Montaža temelja 702-002	0,5 days	Mon 19.12.22	80,00 €	4 hrs	Mon 19.12.22	↓ Bravari (2)											
15	Montaža temelja 702-003	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	↓ Bravari (2)											
16	Montaža temelja 711-001	0,5 days	Tue 20.12.22	80,00 €	4 hrs	Tue 20.12.22	↓ Bravari (2)											
17	Montaža temelja 712-002/01	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	↓ Bravari (2)											
18	Montaža temelja 712-002/02	0,5 days	Wed 21.12.22	80,00 €	4 hrs	Wed 21.12.22	↓ Bravari (2)											
19	Montaža temelja 713-001/01	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22	↓ Bravari (2)											
20	Montaža temelja 713-001/02	0,5 days	Thu 22.12.22	80,00 €	4 hrs	Thu 22.12.22	↓ Bravari (2)											
21	Montaža temelja 713-009	0,5 days	Fri 23.12.22	80,00 €	4 hrs	Fri 23.12.22	↓ Bravari (2)											
22	Montaža temelja 721-001/01	0,5 days	Fri 23.12.22	80,00 €	4 hrs	Fri 23.12.22	↓ Bravari (2)											
23	Montaža temelja 721-001/02	0,5 days	Mon 26.12.22	80,00 €	4 hrs	Mon 26.12.22	↓ Bravari (2)											
24	Montaža temelja 721-001/03	0,5 days	Mon 26.12.22	80,00 €	4 hrs	Mon 26.12.22	↓ Bravari (2)											
25	Montaža temelja 756-001/01	0,5 days	Tue 27.12.22	80,00 €	4 hrs	Tue 27.12.22	↓ Bravari (2)											
26	Montaža temelja 756-001/02	0,5 days	Tue 27.12.22	80,00 €	4 hrs	Tue 27.12.22	↓ Bravari (2)											
27	Montaža temelja 756-002/01	0,5 days	Wed 28.12.22	80,00 €	4 hrs	Wed 28.12.22	↓ Bravari (2)											
28	Montaža temelja 756-002/02	0,5 days	Wed 28.12.22	80,00 €	4 hrs	Wed 28.12.22	↓ Bravari (2)											
29	Montaža temelja 756-003	0,5 days	Thu 29.12.22	80,00 €	4 hrs	Thu 29.12.22	↓ Bravari (2)											
30	Montaža temelja 761-002	0,5 days	Thu 29.12.22	80,00 €	4 hrs	Thu 29.12.22	↓ Bravari (2)											
31	Montaža temelja 803-001	0,5 days	Fri 30.12.22	80,00 €	4 hrs	Fri 30.12.22	↓ Bravari (2)											

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
32	Montaža temelja 803-002	0,5 days	Fri 30.12.22	80,00 €	4 hrs	Fri 30.12.22										
33	Montaža temelja 803-003	0,5 days	Mon 2.1.23	80,00 €	4 hrs	Mon 2.1.23										
34	Montaža temelja 803-004	0,5 days	Mon 2.1.23	80,00 €	4 hrs	Mon 2.1.23										
35	Montaža temelja 813-001/01	0,5 days	Tue 3.1.23	80,00 €	4 hrs	Tue 3.1.23										
36	Montaža temelja 813-001/02	0,5 days	Tue 3.1.23	80,00 €	4 hrs	Tue 3.1.23										
37	Montaža strojeva I uređaja	13,6 days	Mon 26.12.22	2.611,20 €	108,8 hrs	Thu 12.1.23										
38	Montaža 382-002/01	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Mon 26.12.22										
39	Montaža 382-002/02	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Mon 26.12.22										
40	Montaža 601-001	0,4 days	Mon 26.12.22	76,80 €	3,2 hrs	Tue 27.12.22										
41	Montaža 601-019	0,4 days	Tue 27.12.22	76,80 €	3,2 hrs	Tue 27.12.22										
42	Montaža 631-014	0,4 days	Tue 27.12.22	76,80 €	3,2 hrs	Tue 27.12.22										
43	Montaža 631-015	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Wed 28.12.22										
44	Montaža 631-016	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Wed 28.12.22										
45	Montaža 631-022	0,4 days	Wed 28.12.22	76,80 €	3,2 hrs	Thu 29.12.22										
46	Montaža 701-001/01	0,4 days	Thu 29.12.22	76,80 €	3,2 hrs	Thu 29.12.22										
47	Montaža 701-001/02	0,4 days	Thu 29.12.22	76,80 €	3,2 hrs	Thu 29.12.22										
48	Montaža 701-002	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Fri 30.12.22										
49	Montaža 702-002	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Fri 30.12.22										
50	Montaža 702-003	0,4 days	Fri 30.12.22	76,80 €	3,2 hrs	Mon 2.1.23										
51	Montaža 711-001	0,4 days	Mon 2.1.23	76,80 €	3,2 hrs	Mon 2.1.23										
52	Montaža 712-002/01	0,4 days	Mon 2.1.23	76,80 €	3,2 hrs	Mon 2.1.23										
53	Montaža 712-002/02	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Tue 3.1.23										
54	Montaža 713-001/01	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Tue 3.1.23										
55	Montaža 713-001/02	0,4 days	Tue 3.1.23	76,80 €	3,2 hrs	Wed 4.1.23										
56	Montaža 713-009	0,4 days	Wed 4.1.23	76,80 €	3,2 hrs	Wed 4.1.23										
57	Montaža 721-001/01	0,4 days	Wed 4.1.23	76,80 €	3,2 hrs	Wed 4.1.23										
58	Montaža 721-001/02	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Thu 5.1.23										
59	Montaža 721-001/03	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Thu 5.1.23										
60	Montaža 756-001/01	0,4 days	Thu 5.1.23	76,80 €	3,2 hrs	Fri 6.1.23										
61	Montaža 756-001/02	0,4 days	Fri 6.1.23	76,80 €	3,2 hrs	Fri 6.1.23										
62	Montaža 756-002/01	0,4 days	Fri 6.1.23	76,80 €	3,2 hrs	Fri 6.1.23										


Montaža strojeva I uređaja



Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			


ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023		
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
63	Montaža 756-002/02	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Mon 9.1.23									
64	Montaža 756-003	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Mon 9.1.23									
65	Montaža 761-002	0,4 days	Mon 9.1.23	76,80 €	3,2 hrs	Tue 10.1.23									
66	Montaža 803-001	0,4 days	Tue 10.1.23	76,80 €	3,2 hrs	Tue 10.1.23									
67	Montaža 803-002	0,4 days	Tue 10.1.23	76,80 €	3,2 hrs	Tue 10.1.23									
68	Montaža 803-003	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Wed 11.1.23									
69	Montaža 803-004	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Wed 11.1.23									
70	Montaža 813-001/01	0,4 days	Wed 11.1.23	76,80 €	3,2 hrs	Thu 12.1.23									
71	Montaža 813-001/02	0,4 days	Thu 12.1.23	76,80 €	3,2 hrs	Thu 12.1.23									
72	Cjevarski radovi	56,67 days	Tue 3.1.23	44.880,00 €	680 hrs	Thu 23.3.23									
73	Montaža prolaza	10 days	Tue 3.1.23	7.920,00 €	120 hrs	Tue 17.1.23									
74	Montaža nosača	16,67 days	Tue 17.1.23	13.200,00 €	200 hrs	Thu 9.2.23									
75	Montaža cijevi	30 days	Thu 9.2.23	23.760,00 €	360 hrs	Thu 23.3.23									
76	Bravarski radovi	32 days	Thu 9.2.23	5.120,00 €	256 hrs	Mon 27.3.23									
77	Montaža podnica	13 days	Thu 9.2.23	2.080,00 €	104 hrs	Tue 28.2.23									
78	Montaža ljestvi	12 days	Tue 28.2.23	1.920,00 €	96 hrs	Thu 16.3.23									
79	Montaža skala	7 days	Thu 16.3.23	1.120,00 €	56 hrs	Mon 27.3.23									
80	Električarski radovi	57,14 days	Thu 23.3.23	67.200,00 €	800 hrs	Mon 12.6.23									
81	Montaža kablskih prolaza	5,71 days	Thu 23.3.23	6.720,00 €	80 hrs	Thu 30.3.23									
82	Montaža kablskih staza	17,14 days	Thu 30.3.23	20.160,00 €	240 hrs	Tue 25.4.23									
83	Provlačenje kabela	34,29 days	Tue 25.4.23	40.320,00 €	480 hrs	Mon 12.6.23									
84	Limarski radovi	28,67 days	Thu 20.4.23	9.120,00 €	304 hrs	Tue 30.5.23									
85	Montaža ventilacijskih prolaza	6,67 days	Thu 20.4.23	2.400,00 €	80 hrs	Fri 28.4.23									
86	Montaža ventilacijskih kanala	14 days	Thu 4.5.23	5.040,00 €	168 hrs	Wed 24.5.23									
87	Montaža zaštita strojeva I uređaja	4,67 days	Wed 24.5.23	1.680,00 €	56 hrs	Tue 30.5.23									
88	Izolaterski radovi	15 days	Wed 24.5.23	2.400,00 €	120 hrs	Wed 14.6.23									
89	Montaža izolacije	15 days	Wed 24.5.23	2.400,00 €	120 hrs	Wed 14.6.23									
90	Ispitivanje	91,14 days	Tue 28.2.23	30.288,00 €	760 hrs	Wed 5.7.23									
91	Ispitivanje rada strojeva I uređaja	3 days	Tue 14.3.23	288,00 €	24 hrs	Fri 17.3.23									
92	Ispitivanje cjevovoda	24,81 days	Thu 9.3.23	11.616,00 €	264 hrs	Thu 13.4.23									
93	Pregled strukture cjevovoda	10,53 days	Thu 9.3.23	4.928,00 €	112 hrs	Thu 23.3.23									

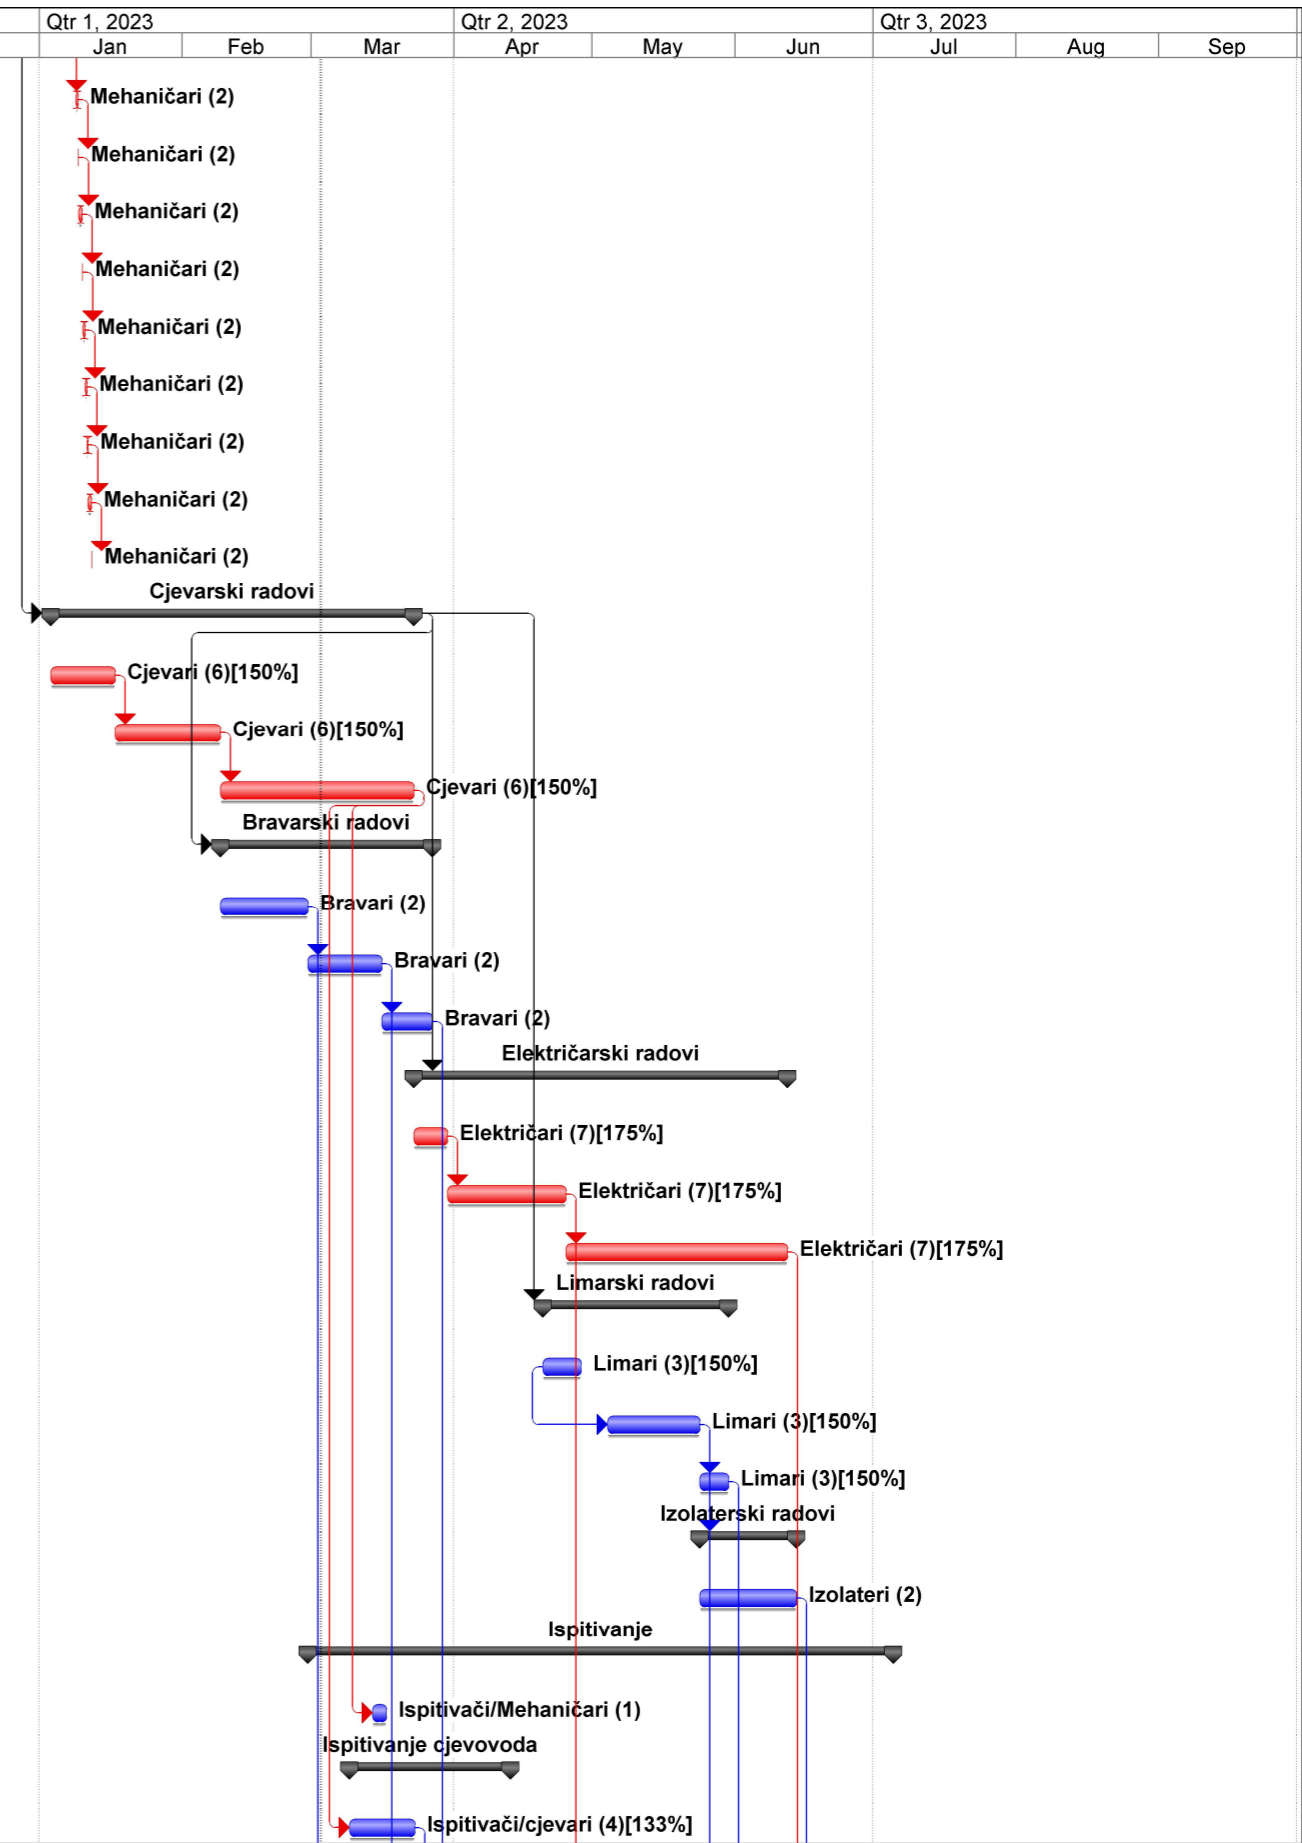

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Cost	Work	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
94	Tlačenje cjevovoda	9,02 days	Thu 23.3.23	4.224,00 €	96 hrs	Wed 5.4.23										
95	Pregled funkcionalnosti cjevovoda	5,26 days	Wed 5.4.23	2.464,00 €	56 hrs	Thu 13.4.23										
96	Pregled bravarskih radova	20 days	Tue 28.2.23	1.280,00 €	64 hrs	Tue 28.3.23										
97	Pregled strukture podnica	2 days	Tue 28.2.23	640,00 €	32 hrs	Thu 2.3.23										
98	Pregled strukture ljestvi	1 day	Thu 16.3.23	320,00 €	16 hrs	Fri 17.3.23										
99	Pregled strukture skala	1 day	Mon 27.3.23	320,00 €	16 hrs	Tue 28.3.23										
100	Ispitivanje električarskih radova	51,29 days	Tue 25.4.23	15.744,00 €	328 hrs	Wed 5.7.23										
101	Pregled strukture kablskih staza	3,5 days	Tue 25.4.23	2.688,00 €	56 hrs	Fri 28.4.23										
102	Pregled montaže kabela	5 days	Mon 12.6.23	3.840,00 €	80 hrs	Mon 19.6.23										
103	Ispitivanje ožičenja kabela	7 days	Mon 19.6.23	5.376,00 €	112 hrs	Wed 28.6.23										
104	Test ispitivanja pod naponom	5 days	Wed 28.6.23	3.840,00 €	80 hrs	Wed 5.7.23										
105	Ispitivanje limarskih radova	5,17 days	Wed 24.5.23	1.120,00 €	56 hrs	Wed 31.5.23										
106	Pregled strukture ventilacije	1 day	Wed 24.5.23	320,00 €	16 hrs	Thu 25.5.23										
107	Pregled funkcionalnosti ventilacije	2 days	Thu 25.5.23	640,00 €	32 hrs	Mon 29.5.23										
108	Pregled strukture zaštite strojeva	0,5 days	Tue 30.5.23	160,00 €	8 hrs	Wed 31.5.23										
109	Ispitivanje izolaterskih radova	3 days	Wed 14.6.23	240,00 €	24 hrs	Mon 19.6.23										
110	Pregled montaže izolacije	3 days	Wed 14.6.23	240,00 €	24 hrs	Mon 19.6.23										

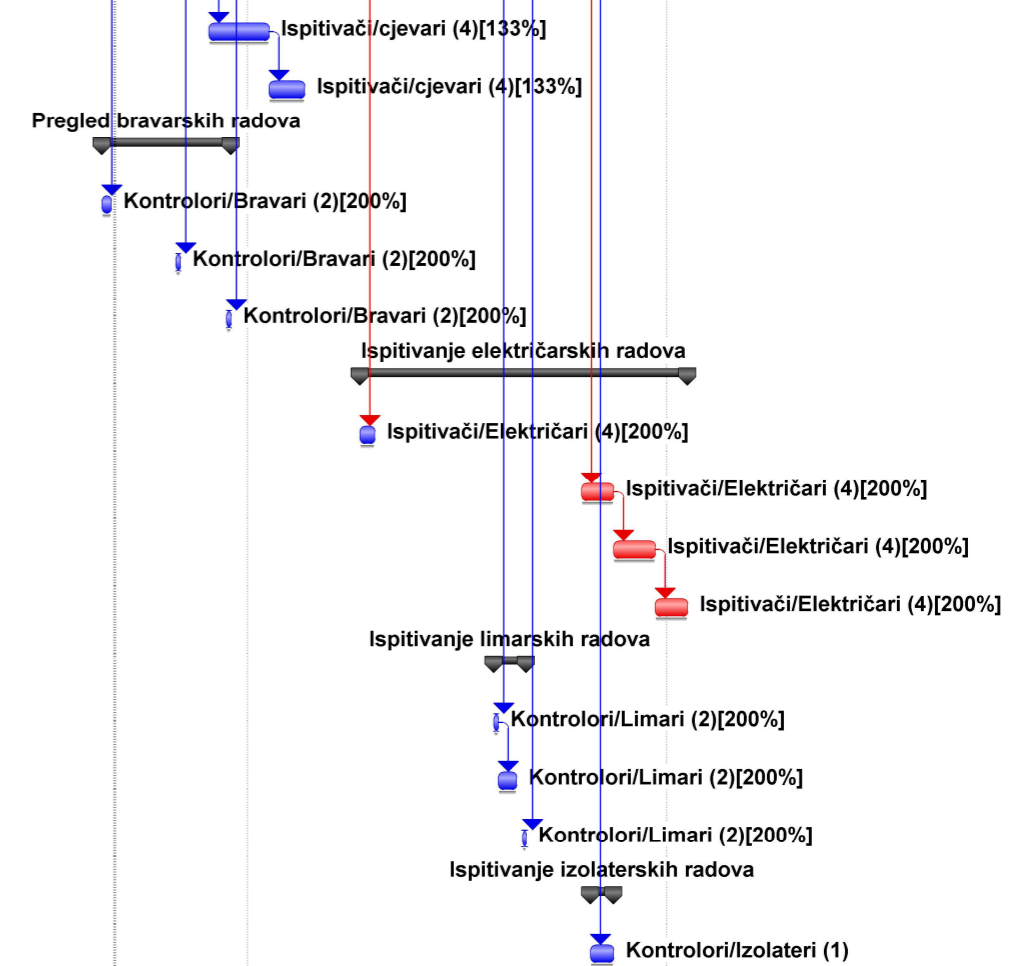

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

Page 4
