

Prilog 4

Ćosić, Matej

Supplement / Prilog

Publication year / Godina izdavanja: **2023**

Permanent link / Trajna poveznica: <https://urn.nsk.hr/urn:nbn:hr:190:693992>

Rights / Prava: [In copyright](#) / [Zaštićeno autorskim pravom.](#)

Download date / Datum preuzimanja: **2025-01-04**



Repository / Repozitorij:

[Repository of the University of Rijeka, Faculty of Engineering](#)



| ID | Task Name | Duration | Start | Cost | Work | Finish | Qtr 1, 2023 | | Qtr 2, 2023 | | Qtr 3, 2023 | |
|----|---|-------------------|---------------------|---------------------|--------------------|---------------------|-------------|-----|-------------|-----|-------------|-----|
| | | | | | | | Nov | Dec | Jan | Feb | Mar | Apr |
| 1 | OPREMANJE KROVA DVODNA STROJARNICE | 142,8 days | Mon 12.12.22 | 105.563,20 € | 3.164,8 hrs | Wed 28.6.23 | | | | | | |
| 2 | Montaža temelja Brigada 1 | 8,5 days | Mon 12.12.22 | 1.360,00 € | 68 hrs | Thu 22.12.22 | | | | | | |
| 3 | Montaža temelja 382-002/01 | 0,5 days | Mon 12.12.22 | 80,00 € | 4 hrs | Mon 12.12.22 | | | | | | |
| 4 | Montaža temelja 382-002/02 | 0,5 days | Mon 12.12.22 | 80,00 € | 4 hrs | Mon 12.12.22 | | | | | | |
| 5 | Montaža temelja 601-001 | 0,5 days | Tue 13.12.22 | 80,00 € | 4 hrs | Tue 13.12.22 | | | | | | |
| 6 | Montaža temelja 601-019 | 0,5 days | Tue 13.12.22 | 80,00 € | 4 hrs | Tue 13.12.22 | | | | | | |
| 7 | Montaža temelja 631-014 | 0,5 days | Wed 14.12.22 | 80,00 € | 4 hrs | Wed 14.12.22 | | | | | | |
| 8 | Montaža temelja 631-015 | 0,5 days | Wed 14.12.22 | 80,00 € | 4 hrs | Wed 14.12.22 | | | | | | |
| 9 | Montaža temelja 631-016 | 0,5 days | Thu 15.12.22 | 80,00 € | 4 hrs | Thu 15.12.22 | | | | | | |
| 10 | Montaža temelja 631-022 | 0,5 days | Thu 15.12.22 | 80,00 € | 4 hrs | Thu 15.12.22 | | | | | | |
| 11 | Montaža temelja 701-001/01 | 0,5 days | Fri 16.12.22 | 80,00 € | 4 hrs | Fri 16.12.22 | | | | | | |
| 12 | Montaža temelja 701-001/02 | 0,5 days | Fri 16.12.22 | 80,00 € | 4 hrs | Fri 16.12.22 | | | | | | |
| 13 | Montaža temelja 701-002 | 0,5 days | Mon 19.12.22 | 80,00 € | 4 hrs | Mon 19.12.22 | | | | | | |
| 14 | Montaža temelja 702-002 | 0,5 days | Mon 19.12.22 | 80,00 € | 4 hrs | Mon 19.12.22 | | | | | | |
| 15 | Montaža temelja 702-003 | 0,5 days | Tue 20.12.22 | 80,00 € | 4 hrs | Tue 20.12.22 | | | | | | |
| 16 | Montaža temelja 711-001 | 0,5 days | Tue 20.12.22 | 80,00 € | 4 hrs | Tue 20.12.22 | | | | | | |
| 17 | Montaža temelja 712-002/01 | 0,5 days | Wed 21.12.22 | 80,00 € | 4 hrs | Wed 21.12.22 | | | | | | |
| 18 | Montaža temelja 712-002/02 | 0,5 days | Wed 21.12.22 | 80,00 € | 4 hrs | Wed 21.12.22 | | | | | | |
| 19 | Montaža temelja 713-001/01 | 0,5 days | Thu 22.12.22 | 80,00 € | 4 hrs | Thu 22.12.22 | | | | | | |
| 20 | Montaža temelja Brigada 2 | 8,5 days | Mon 12.12.22 | 1.360,00 € | 68 hrs | Thu 22.12.22 | | | | | | |
| 21 | Montaža temelja 713-001/02 | 0,5 days | Mon 12.12.22 | 80,00 € | 4 hrs | Mon 12.12.22 | | | | | | |
| 22 | Montaža temelja 713-009 | 0,5 days | Mon 12.12.22 | 80,00 € | 4 hrs | Mon 12.12.22 | | | | | | |
| 23 | Montaža temelja 721-001/01 | 0,5 days | Tue 13.12.22 | 80,00 € | 4 hrs | Tue 13.12.22 | | | | | | |
| 24 | Montaža temelja 721-001/02 | 0,5 days | Tue 13.12.22 | 80,00 € | 4 hrs | Tue 13.12.22 | | | | | | |
| 25 | Montaža temelja 721-001/03 | 0,5 days | Wed 14.12.22 | 80,00 € | 4 hrs | Wed 14.12.22 | | | | | | |
| 26 | Montaža temelja 756-001/01 | 0,5 days | Wed 14.12.22 | 80,00 € | 4 hrs | Wed 14.12.22 | | | | | | |
| 27 | Montaža temelja 756-001/02 | 0,5 days | Thu 15.12.22 | 80,00 € | 4 hrs | Thu 15.12.22 | | | | | | |
| 28 | Montaža temelja 756-002/01 | 0,5 days | Thu 15.12.22 | 80,00 € | 4 hrs | Thu 15.12.22 | | | | | | |
| 29 | Montaža temelja 756-002/02 | 0,5 days | Fri 16.12.22 | 80,00 € | 4 hrs | Fri 16.12.22 | | | | | | |
| 30 | Montaža temelja 756-003 | 0,5 days | Fri 16.12.22 | 80,00 € | 4 hrs | Fri 16.12.22 | | | | | | |
| 31 | Montaža temelja 761-002 | 0,5 days | Mon 19.12.22 | 80,00 € | 4 hrs | Mon 19.12.22 | | | | | | |

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

| | | | | | | | | | |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task | | Milestone | | Rolled Up Critical Task | | Split | | Group By Summary | |
| Critical Task | | Summary | | Rolled Up Milestone | | External Tasks | | Deadline | |
| Progress | | Rolled Up Task | | Rolled Up Progress | | Project Summary | | | |

| ID | Task Name | Duration | Start | Cost | Work | Finish | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|----|---|-----------------|---------------------|-------------------|-----------------|---------------------|-------------|---|-----|-------------|-----|-----|-------------|-----|
| | | | | | | | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun |
| 32 | Montaža temelja 803-001 | 0,5 days | Mon 19.12.22 | 80,00 € | 4 hrs | Mon 19.12.22 | | Bravari (2) B2 | | | | | | |
| 33 | Montaža temelja 803-002 | 0,5 days | Tue 20.12.22 | 80,00 € | 4 hrs | Tue 20.12.22 | | Bravari (2) B2 | | | | | | |
| 34 | Montaža temelja 803-003 | 0,5 days | Tue 20.12.22 | 80,00 € | 4 hrs | Tue 20.12.22 | | Bravari (2) B2 | | | | | | |
| 35 | Montaža temelja 803-004 | 0,5 days | Wed 21.12.22 | 80,00 € | 4 hrs | Wed 21.12.22 | | Bravari (2) B2 | | | | | | |
| 36 | Montaža temelja 813-001/01 | 0,5 days | Wed 21.12.22 | 80,00 € | 4 hrs | Wed 21.12.22 | | Bravari (2) B2 | | | | | | |
| 37 | Montaža temelja 813-001/02 | 0,5 days | Thu 22.12.22 | 80,00 € | 4 hrs | Thu 22.12.22 | | Bravari (2) B2 | | | | | | |
| 38 | Montaža strojeva I uređaja Brigada 1 | 6,8 days | Tue 13.12.22 | 1.305,60 € | 54,4 hrs | Thu 22.12.22 | | Montaža strojeva I uređaja Brigada 1 | | | | | | |
| 39 | Montaža 382-002/01 | 0,4 days | Tue 13.12.22 | 76,80 € | 3,2 hrs | Tue 13.12.22 | | Mehaničari (2) M1 | | | | | | |
| 40 | Montaža 382-002/02 | 0,4 days | Tue 13.12.22 | 76,80 € | 3,2 hrs | Wed 14.12.22 | | Mehaničari (2) M1 | | | | | | |
| 41 | Montaža 601-001 | 0,4 days | Wed 14.12.22 | 76,80 € | 3,2 hrs | Wed 14.12.22 | | Mehaničari (2) M1 | | | | | | |
| 42 | Montaža 601-019 | 0,4 days | Wed 14.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M1 | | | | | | |
| 43 | Montaža 631-014 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M1 | | | | | | |
| 44 | Montaža 631-015 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M1 | | | | | | |
| 45 | Montaža 631-016 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Fri 16.12.22 | | Mehaničari (2) M1 | | | | | | |
| 46 | Montaža 631-022 | 0,4 days | Fri 16.12.22 | 76,80 € | 3,2 hrs | Fri 16.12.22 | | Mehaničari (2) M1 | | | | | | |
| 47 | Montaža 701-001/01 | 0,4 days | Fri 16.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M1 | | | | | | |
| 48 | Montaža 701-001/02 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M1 | | | | | | |
| 49 | Montaža 701-002 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M1 | | | | | | |
| 50 | Montaža 702-002 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Tue 20.12.22 | | Mehaničari (2) M1 | | | | | | |
| 51 | Montaža 702-003 | 0,4 days | Tue 20.12.22 | 76,80 € | 3,2 hrs | Tue 20.12.22 | | Mehaničari (2) M1 | | | | | | |
| 52 | Montaža 711-001 | 0,4 days | Tue 20.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M1 | | | | | | |
| 53 | Montaža 712-002/01 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M1 | | | | | | |
| 54 | Montaža 712-002/02 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M1 | | | | | | |
| 55 | Montaža 713-001/01 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Thu 22.12.22 | | Mehaničari (2) M1 | | | | | | |
| 56 | Montaža strojeva I uređaja Brigada 2 | 6,8 days | Tue 13.12.22 | 1.305,60 € | 54,4 hrs | Thu 22.12.22 | | Montaža strojeva I uređaja Brigada 2 | | | | | | |
| 57 | Montaža 713-001/02 | 0,4 days | Tue 13.12.22 | 76,80 € | 3,2 hrs | Tue 13.12.22 | | Mehaničari (2) M2 | | | | | | |
| 58 | Montaža 713-009 | 0,4 days | Tue 13.12.22 | 76,80 € | 3,2 hrs | Wed 14.12.22 | | Mehaničari (2) M2 | | | | | | |
| 59 | Montaža 721-001/01 | 0,4 days | Wed 14.12.22 | 76,80 € | 3,2 hrs | Wed 14.12.22 | | Mehaničari (2) M2 | | | | | | |
| 60 | Montaža 721-001/02 | 0,4 days | Wed 14.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M2 | | | | | | |
| 61 | Montaža 721-001/03 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M2 | | | | | | |
| 62 | Montaža 756-001/01 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Thu 15.12.22 | | Mehaničari (2) M2 | | | | | | |

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23


| | | | | | | | | | |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task | | Milestone | | Rolled Up Critical Task | | Split | | Group By Summary | |
| Critical Task | | Summary | | Rolled Up Milestone | | External Tasks | | Deadline | |
| Progress | | Rolled Up Task | | Rolled Up Progress | | Project Summary | | | |

| ID | Task Name | Duration | Start | Cost | Work | Finish | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|----|--|------------------|---------------------|--------------------|----------------|--------------------|-------------|-----------------------------|-----|-------------|-----|-----|-------------|-----|
| | | | | | | | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun |
| 63 | Montaža 756-001/02 | 0,4 days | Thu 15.12.22 | 76,80 € | 3,2 hrs | Fri 16.12.22 | | Mehaničari (2) M2 | | | | | | |
| 64 | Montaža 756-002/01 | 0,4 days | Fri 16.12.22 | 76,80 € | 3,2 hrs | Fri 16.12.22 | | Mehaničari (2) M2 | | | | | | |
| 65 | Montaža 756-002/02 | 0,4 days | Fri 16.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M2 | | | | | | |
| 66 | Montaža 756-003 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M2 | | | | | | |
| 67 | Montaža 761-002 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Mon 19.12.22 | | Mehaničari (2) M2 | | | | | | |
| 68 | Montaža 803-001 | 0,4 days | Mon 19.12.22 | 76,80 € | 3,2 hrs | Tue 20.12.22 | | Mehaničari (2) M2 | | | | | | |
| 69 | Montaža 803-002 | 0,4 days | Tue 20.12.22 | 76,80 € | 3,2 hrs | Tue 20.12.22 | | Mehaničari (2) M2 | | | | | | |
| 70 | Montaža 803-003 | 0,4 days | Tue 20.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M2 | | | | | | |
| 71 | Montaža 803-004 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M2 | | | | | | |
| 72 | Montaža 813-001/01 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Wed 21.12.22 | | Mehaničari (2) M2 | | | | | | |
| 73 | Montaža 813-001/02 | 0,4 days | Wed 21.12.22 | 76,80 € | 3,2 hrs | Thu 22.12.22 | | Mehaničari (2) M2 | | | | | | |
| 74 | Cjevarski radovi | 47,5 days | Tue 13.12.22 | 29.920,00 € | 680 hrs | Thu 16.2.23 | | Cjevarski radovi | | | | | | |
| 75 | Montaža prolaza | 15 days | Tue 13.12.22 | 5.280,00 € | 120 hrs | Tue 3.1.23 | | Cjevvari (4) C1 | | | | | | |
| 76 | Montaža nosača | 25 days | Tue 13.12.22 | 8.800,00 € | 200 hrs | Tue 17.1.23 | | Cjevvari (4) C2 | | | | | | |
| 77 | Montaža cijevi brigada 1 | 22,5 days | Tue 3.1.23 | 7.920,00 € | 180 hrs | Thu 2.2.23 | | Cjevvari (4) C1 | | | | | | |
| 78 | Montaža cijevi brigada 2 | 22,5 days | Tue 17.1.23 | 7.920,00 € | 180 hrs | Thu 16.2.23 | | Cjevvari (4) C2 | | | | | | |
| 79 | Bravarski radovi | 16,5 days | Thu 5.1.23 | 5.120,00 € | 256 hrs | Mon 30.1.23 | | Bravarski radovi | | | | | | |
| 80 | Montaža podnica | 13 days | Thu 5.1.23 | 2.080,00 € | 104 hrs | Tue 24.1.23 | | Bravari (2) B1 | | | | | | |
| 81 | Montaža ljestvi | 12 days | Thu 5.1.23 | 1.920,00 € | 96 hrs | Mon 23.1.23 | | Bravari (2) B2 | | | | | | |
| 82 | Montaža skala brigada 1 | 3,5 days | Tue 24.1.23 | 560,00 € | 28 hrs | Mon 30.1.23 | | Bravari (2) B1 | | | | | | |
| 83 | Montaža skala brigada 2 | 3,5 days | Mon 23.1.23 | 560,00 € | 28 hrs | Fri 27.1.23 | | Bravari (2) B2 | | | | | | |
| 84 | Električarski radovi | 60 days | Thu 16.2.23 | 38.400,00 € | 800 hrs | Thu 11.5.23 | | Električarski radovi | | | | | | |
| 85 | Montaža kablskih prolaza - brigada 1 | 10 days | Thu 16.2.23 | 3.840,00 € | 80 hrs | Thu 2.3.23 | | Električari (4) E1 | | | | | | |
| 86 | Montaža kablskih staza - brigada 2 | 30 days | Thu 16.2.23 | 11.520,00 € | 240 hrs | Thu 30.3.23 | | Električari (4) E2 | | | | | | |
| 87 | Provlačenje kabela brigada 1 | 30 days | Thu 2.3.23 | 11.520,00 € | 240 hrs | Thu 13.4.23 | | Električari (4) E1 | | | | | | |
| 88 | Provlačenje kabela brigada 2 | 30 days | Thu 30.3.23 | 11.520,00 € | 240 hrs | Thu 11.5.23 | | Električari (4) E2 | | | | | | |
| 89 | Limarski radovi | 21 days | Thu 16.3.23 | 6.080,00 € | 304 hrs | Fri 14.4.23 | | Limarski radovi | | | | | | |
| 90 | Montaža ventilacijskih prolaza - brigada 1 | 10 days | Thu 16.3.23 | 1.600,00 € | 80 hrs | Thu 30.3.23 | | Limari (2) L1 | | | | | | |
| 91 | Montaža ventilacijskih kanala - brigada 2 | 21 days | Thu 16.3.23 | 3.360,00 € | 168 hrs | Fri 14.4.23 | | Limari (2) L2 | | | | | | |
| 92 | Montaža zaštita strojeva I uređaja - brigada 1 | 3,5 days | Thu 30.3.23 | 560,00 € | 28 hrs | Wed 5.4.23 | | Limari (2) L1 | | | | | | |
| 93 | Montaža zaštita strojeva I uređaja - brigada 1 | 3,5 days | Wed 5.4.23 | 560,00 € | 28 hrs | Mon 10.4.23 | | Limari (2) L1 | | | | | | |

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

| | | | | | | | | | |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task | | Milestone | | Rolled Up Critical Task | | Split | | Group By Summary | |
| Critical Task | | Summary | | Rolled Up Milestone | | External Tasks | | Deadline | |
| Progress | | Rolled Up Task | | Rolled Up Progress | | Project Summary | | | |

| ID | Task Name | Duration | Start | Cost | Work | Finish | Nov | | Dec | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|-----|---|------------------|--------------------|--------------------|----------------|--------------------|-----|--|-----|--|-------------|-----|-----|-------------|-----|-----|-------------|--|
| | | | | | | | | | | | Jan | Feb | Mar | Apr | May | Jun | Jul | |
| 94 | Izolaterski radovi | 7,5 days | Fri 14.4.23 | 2.400,00 € | 120 hrs | Wed 26.4.23 | | | | | | | | | | | | |
| 95 | Montaža izolacije - brigada 1 | 7,5 days | Fri 14.4.23 | 1.200,00 € | 60 hrs | Wed 26.4.23 | | | | | | | | | | | | |
| 96 | Montaža izolacije - brigada 2 | 7,5 days | Fri 14.4.23 | 1.200,00 € | 60 hrs | Wed 26.4.23 | | | | | | | | | | | | |
| 97 | Ispitivanje | 111 days | Tue 24.1.23 | 18.312,00 € | 760 hrs | Wed 28.6.23 | | | | | | | | | | | | |
| 98 | Ispitivanje rada strojeva I uređaja | 1,5 days | Tue 7.2.23 | 144,00 € | 12 hrs | Thu 9.2.23 | | | | | | | | | | | | |
| 99 | Ispitivanje rada strojeva I uređaja | 1,5 days | Tue 7.2.23 | 144,00 € | 12 hrs | Thu 9.2.23 | | | | | | | | | | | | |
| 100 | Ispitivanje cjevovoda | 24,5 days | Thu 2.2.23 | 8.712,00 € | 264 hrs | Thu 9.3.23 | | | | | | | | | | | | |
| 101 | Pregled strukture cjevovoda | 14 days | Thu 2.2.23 | 3.696,00 € | 112 hrs | Wed 22.2.23 | | | | | | | | | | | | |
| 102 | Tlačenje cjevovoda | 12 days | Wed 15.2.23 | 3.168,00 € | 96 hrs | Fri 3.3.23 | | | | | | | | | | | | |
| 103 | Pregled funkcionalnosti cjevovoda - brigada 1 | 3,5 days | Fri 3.3.23 | 924,00 € | 28 hrs | Thu 9.3.23 | | | | | | | | | | | | |
| 104 | Pregled funkcionalnosti cjevovoda - brigada 2 | 3,5 days | Fri 3.3.23 | 924,00 € | 28 hrs | Thu 9.3.23 | | | | | | | | | | | | |
| 105 | Pregled bravarskih radova | 4,5 days | Tue 24.1.23 | 640,00 € | 64 hrs | Tue 31.1.23 | | | | | | | | | | | | |
| 106 | Pregled strukture podnica - brigada 1 | 2 days | Tue 24.1.23 | 160,00 € | 16 hrs | Thu 26.1.23 | | | | | | | | | | | | |
| 107 | Pregled strukture podnica - brigada 2 | 2 days | Tue 24.1.23 | 160,00 € | 16 hrs | Thu 26.1.23 | | | | | | | | | | | | |
| 108 | Pregled strukture ljestvi | 2 days | Thu 26.1.23 | 160,00 € | 16 hrs | Fri 27.1.23 | | | | | | | | | | | | |
| 109 | Pregled strukture skala | 2 days | Fri 27.1.23 | 160,00 € | 16 hrs | Tue 31.1.23 | | | | | | | | | | | | |
| 110 | Ispitivanje električarskih radova | 64 days | Thu 30.3.23 | 7.872,00 € | 328 hrs | Wed 28.6.23 | | | | | | | | | | | | |
| 111 | Pregled strukture kablskih staza | 7 days | Thu 30.3.23 | 1.344,00 € | 56 hrs | Mon 10.4.23 | | | | | | | | | | | | |
| 112 | Pregled montaže kabela | 10 days | Thu 11.5.23 | 1.920,00 € | 80 hrs | Thu 25.5.23 | | | | | | | | | | | | |
| 113 | Ispitivanje ožičenja kabela | 14 days | Thu 25.5.23 | 2.688,00 € | 112 hrs | Wed 14.6.23 | | | | | | | | | | | | |
| 114 | Test ispitivanja pod naponom | 10 days | Wed 14.6.23 | 1.920,00 € | 80 hrs | Wed 28.6.23 | | | | | | | | | | | | |
| 115 | Ispitivanje limarskih radova | 14,2 days | Fri 14.4.23 | 560,00 € | 56 hrs | Thu 4.5.23 | | | | | | | | | | | | |
| 116 | Pregled strukture ventilacije | 2 days | Fri 14.4.23 | 160,00 € | 16 hrs | Tue 18.4.23 | | | | | | | | | | | | |
| 117 | Pregled funkcionalnosti ventilacije brigada 1 | 2 days | Tue 18.4.23 | 160,00 € | 16 hrs | Thu 20.4.23 | | | | | | | | | | | | |
| 118 | Pregled funkcionalnosti ventilacije brigada 2 | 2 days | Tue 18.4.23 | 160,00 € | 16 hrs | Thu 20.4.23 | | | | | | | | | | | | |
| 119 | Pregled strukture zaštite strojeva | 1 day | Thu 4.5.23 | 80,00 € | 8 hrs | Thu 4.5.23 | | | | | | | | | | | | |
| 120 | Ispitivanje izolaterskih radova | 1,5 days | Wed 26.4.23 | 240,00 € | 24 hrs | Thu 27.4.23 | | | | | | | | | | | | |
| 121 | Pregled montaže izolacije brigada 1 | 1,5 days | Wed 26.4.23 | 120,00 € | 12 hrs | Thu 27.4.23 | | | | | | | | | | | | |
| 122 | Pregled montaže izolacije brigada 2 | 1,5 days | Wed 26.4.23 | 120,00 € | 12 hrs | Thu 27.4.23 | | | | | | | | | | | | |

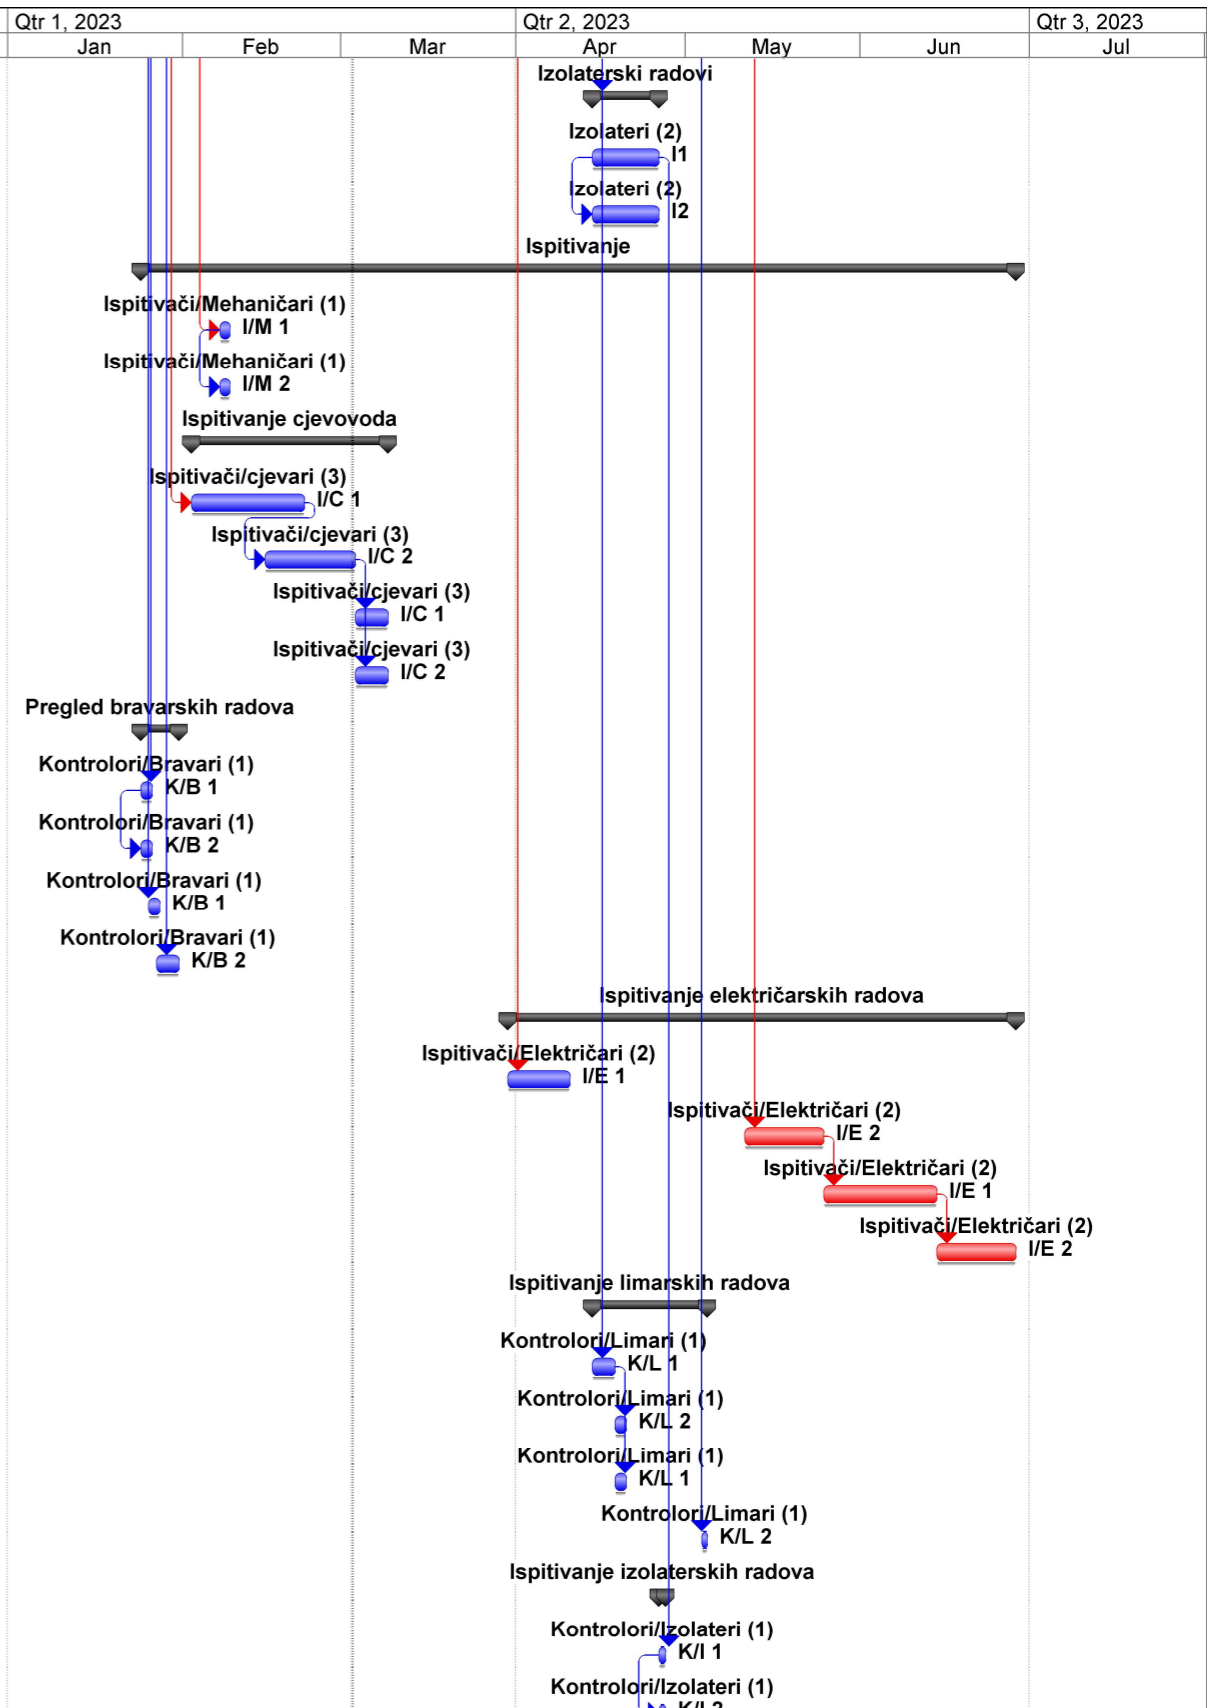

Project: Popis aktivnosti za opremanje
Date: Fri 3.3.23

| | | | | | | | | | |
|---------------|--|----------------|--|-------------------------|--|-----------------|--|------------------|--|
| Task | | Milestone | | Rolled Up Critical Task | | Split | | Group By Summary | |
| Critical Task | | Summary | | Rolled Up Milestone | | External Tasks | | Deadline | |
| Progress | | Rolled Up Task | | Rolled Up Progress | | Project Summary | | | |
