

# Prilog - prvi slučaj

---

**Butorac, Lovro**

**Supplement / Prilog**

*Publication year / Godina izdavanja:* **2023**

*Permanent link / Trajna poveznica:* <https://urn.nsk.hr/urn:nbn:hr:190:680990>

*Rights / Prava:* [In copyright](#)/[Zaštićeno autorskim pravom.](#)

*Download date / Datum preuzimanja:* **2024-11-23**



*Repository / Repozitorij:*

[Repository of the University of Rijeka, Faculty of Engineering](#)




ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Half 2, 2023							Half 1, 2024				
									M	J	J	A	S	O	N	D	J	F		
1	<b>OPREMANJE 2. PLATFORME STROJARNICE</b>	<b>134,5 days</b>	<b>Thu 6.7.23</b>	<b>Wed 10.1.24</b>		<b>\$148.448,00</b>	<b>4.588 hrs</b>		<b>OPREMANJE 2. PLATFORME STROJARNICE</b>											
2	<b>Montaža temelja</b>	<b>27,75 days</b>	<b>Thu 6.7.23</b>	<b>Mon 14.8.23</b>		<b>\$8.880,00</b>	<b>444 hrs</b>		<b>Montaža temelja</b>											
3	Montaža temelja 445-003	0,75 days	Thu 6.7.23	Thu 6.7.23		\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 445-003 F B											
4	Montaža temelja 445-004	0,75 days	Thu 6.7.23	Fri 7.7.23	3	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 445-004 F B											
5	Montaža temelja 452-001	0,75 days	Fri 7.7.23	Mon 10.7.23	4	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 452-001 F B											
6	Montaža temelja 452-005	0,75 days	Mon 10.7.23	Mon 10.7.23	5	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 452-005 F B											
7	Montaža temelja 581-001	0,75 days	Tue 11.7.23	Tue 11.7.23	6	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 581-001 F B											
8	Montaža temelja 581-002	0,75 days	Tue 11.7.23	Wed 12.7.23	7	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 581-002 F B											
9	Montaža temelja 581-003	0,75 days	Wed 12.7.23	Thu 13.7.23	8	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 581-003 F B											
10	Montaža temelja 582-001	0,75 days	Thu 13.7.23	Thu 13.7.23	9	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 582-001 F B											
11	Montaža temelja 582-003/01	0,75 days	Fri 14.7.23	Fri 14.7.23	10	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 582-003/01 F B											
12	Montaža temelja 582-003/02	0,75 days	Fri 14.7.23	Mon 17.7.23	11	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 582-003/02 F B											
13	Montaža temelja 644-008/01	0,75 days	Mon 17.7.23	Tue 18.7.23	12	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 644-008/01 F B											
14	Montaža temelja 644-008/02	0,75 days	Tue 18.7.23	Tue 18.7.23	13	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 644-008/02 F B											
15	Montaža temelja 651-001	0,75 days	Wed 19.7.23	Wed 19.7.23	14	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 651-001 F B											
16	Montaža temelja 651-002	0,75 days	Wed 19.7.23	Thu 20.7.23	15	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 651-002 F B											
17	Montaža temelja 651-003	0,75 days	Thu 20.7.23	Fri 21.7.23	16	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 651-003 F B											
18	Montaža temelja 702-001	0,75 days	Fri 21.7.23	Fri 21.7.23	17	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 702-001 F B											
19	Montaža temelja 702-004	0,75 days	Mon 24.7.23	Mon 24.7.23	18	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 702-004 F B											
20	Montaža temelja 702-005	0,75 days	Mon 24.7.23	Tue 25.7.23	19	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 702-005 F B											
21	Montaža temelja 703-001	0,75 days	Tue 25.7.23	Wed 26.7.23	20	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 703-001 F B											
22	Montaža temelja 703-002	0,75 days	Wed 26.7.23	Wed 26.7.23	21	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 703-002 F B											
23	Montaža temelja 712-001	0,75 days	Thu 27.7.23	Thu 27.7.23	22	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 712-001 F B											
24	Montaža temelja 713-007	0,75 days	Thu 27.7.23	Fri 28.7.23	23	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 713-007 F B											
25	Montaža temelja 714-001	0,75 days	Fri 28.7.23	Mon 31.7.23	24	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 714-001 F B											
26	Montaža temelja 756-001/02	0,75 days	Mon 31.7.23	Mon 31.7.23	25	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 756-001/02 F B											
27	Montaža temelja 722-011	0,75 days	Tue 1.8.23	Tue 1.8.23	26	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 722-011 F B											
28	Montaža temelja 731-001/01	0,75 days	Tue 1.8.23	Wed 2.8.23	27	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 731-001/01 F B											
29	Montaža temelja 731-001/02	0,75 days	Wed 2.8.23	Thu 3.8.23	28	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 731-001/02 F B											
30	Montaža temelja 731-002	0,75 days	Thu 3.8.23	Thu 3.8.23	29	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 731-002 F B											
31	Montaža temelja 731-003/01	0,75 days	Fri 4.8.23	Fri 4.8.23	30	\$240,00	12 hrs	Bravari (2)[200%]	Montaža temelja 731-003/01 F B											

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23


Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Half 2, 2023							Half 1, 2024			
									M	J	J	A	S	O	N	D	J	F	
32	Montaža temelja 731-003/01	0,75 days	Fri 4.8.23	Mon 7.8.23	31	\$240,00	12 hrs	Bravari (2)[200%]											
33	Montaža temelja 733-001	0,75 days	Mon 7.8.23	Tue 8.8.23	32	\$240,00	12 hrs	Bravari (2)[200%]											
34	Montaža temelja 733-012	0,75 days	Tue 8.8.23	Tue 8.8.23	33	\$240,00	12 hrs	Bravari (2)[200%]											
35	Montaža temelja 734-001	0,75 days	Wed 9.8.23	Wed 9.8.23	34	\$240,00	12 hrs	Bravari (2)[200%]											
36	Montaža temelja 743-002	0,75 days	Wed 9.8.23	Thu 10.8.23	35	\$240,00	12 hrs	Bravari (2)[200%]											
37	Montaža temelja 743-003	0,75 days	Thu 10.8.23	Fri 11.8.23	36	\$240,00	12 hrs	Bravari (2)[200%]											
38	Montaža temelja 751-001	0,75 days	Fri 11.8.23	Fri 11.8.23	37	\$240,00	12 hrs	Bravari (2)[200%]											
39	Montaža temelja 756-004	0,75 days	Mon 14.8.23	Mon 14.8.23	38	\$240,00	12 hrs	Bravari (2)[200%]											
40	<b>Montaža strojeva I uređaja</b>	<b>18,5 days</b>	<b>Thu 3.8.23</b>	<b>Wed 30.8.23</b>	<b>2FS-7 days</b>	<b>\$7.104,00</b>	<b>296 hrs</b>												
41	Montaža 445-003	0,5 days	Thu 3.8.23	Fri 4.8.23		\$192,00	8 hrs	Mehaničari (2)[200%]											
42	Montaža 445-004	0,5 days	Fri 4.8.23	Fri 4.8.23	41	\$192,00	8 hrs	Mehaničari (2)[200%]											
43	Montaža 452-001	0,5 days	Fri 4.8.23	Mon 7.8.23	42	\$192,00	8 hrs	Mehaničari (2)[200%]											
44	Montaža 452-005	0,5 days	Mon 7.8.23	Mon 7.8.23	43	\$192,00	8 hrs	Mehaničari (2)[200%]											
45	Montaža 581-001	0,5 days	Mon 7.8.23	Tue 8.8.23	44	\$192,00	8 hrs	Mehaničari (2)[200%]											
46	Montaža 581-002	0,5 days	Tue 8.8.23	Tue 8.8.23	45	\$192,00	8 hrs	Mehaničari (2)[200%]											
47	Montaža 581-003	0,5 days	Tue 8.8.23	Wed 9.8.23	46	\$192,00	8 hrs	Mehaničari (2)[200%]											
48	Montaža 582-001	0,5 days	Wed 9.8.23	Wed 9.8.23	47	\$192,00	8 hrs	Mehaničari (2)[200%]											
49	Montaža 582-003/01	0,5 days	Wed 9.8.23	Thu 10.8.23	48	\$192,00	8 hrs	Mehaničari (2)[200%]											
50	Montaža 582-003/02	0,5 days	Thu 10.8.23	Thu 10.8.23	49	\$192,00	8 hrs	Mehaničari (2)[200%]											
51	Montaža 644-008/01	0,5 days	Thu 10.8.23	Fri 11.8.23	50	\$192,00	8 hrs	Mehaničari (2)[200%]											
52	Montaža 644-008/02	0,5 days	Fri 11.8.23	Fri 11.8.23	51	\$192,00	8 hrs	Mehaničari (2)[200%]											
53	Montaža 651-001	0,5 days	Fri 11.8.23	Mon 14.8.23	52	\$192,00	8 hrs	Mehaničari (2)[200%]											
54	Montaža 651-002	0,5 days	Mon 14.8.23	Mon 14.8.23	53	\$192,00	8 hrs	Mehaničari (2)[200%]											
55	Montaža 651-003	0,5 days	Mon 14.8.23	Tue 15.8.23	54	\$192,00	8 hrs	Mehaničari (2)[200%]											
56	Montaža 702-001	0,5 days	Tue 15.8.23	Tue 15.8.23	55	\$192,00	8 hrs	Mehaničari (2)[200%]											
57	Montaža 702-004	0,5 days	Tue 15.8.23	Wed 16.8.23	56	\$192,00	8 hrs	Mehaničari (2)[200%]											
58	Montaža 702-005	0,5 days	Wed 16.8.23	Wed 16.8.23	57	\$192,00	8 hrs	Mehaničari (2)[200%]											
59	Montaža 703-001	0,5 days	Wed 16.8.23	Thu 17.8.23	58	\$192,00	8 hrs	Mehaničari (2)[200%]											
60	Montaža 703-002	0,5 days	Thu 17.8.23	Thu 17.8.23	59	\$192,00	8 hrs	Mehaničari (2)[200%]											
61	Montaža 712-001	0,5 days	Thu 17.8.23	Fri 18.8.23	60	\$192,00	8 hrs	Mehaničari (2)[200%]											
62	Montaža 713-007	0,5 days	Fri 18.8.23	Fri 18.8.23	61	\$192,00	8 hrs	Mehaničari (2)[200%]											

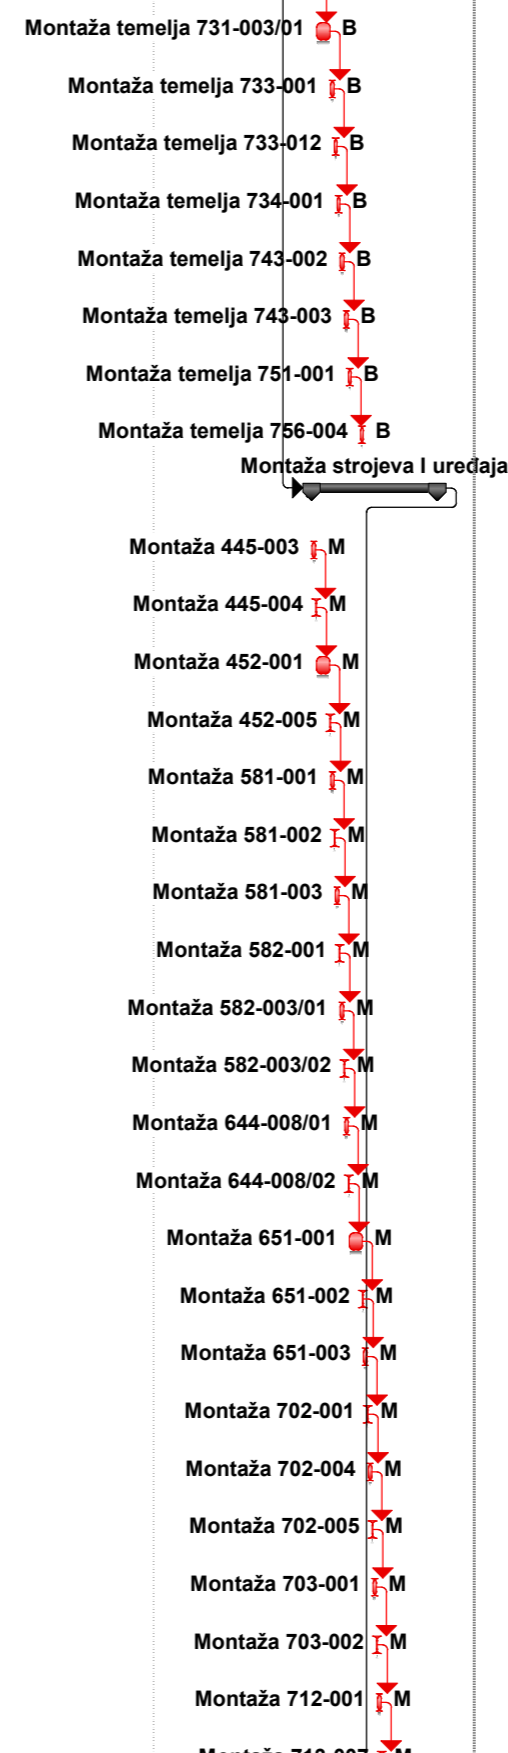

Project: OPREMANJE 2 PLATFORME Date: Thu 7.9.23	Critical		Split		Slack		Project Summary		External Tasks	
	Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
	Task		Milestone		Summary		Rolled Up Critical		Deadline	


ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Half 2, 2023							Half 1, 2024			
									M	J	J	A	S	O	N	D	J	F	
63	Montaža 714-001	0,5 days	Fri 18.8.23	Mon 21.8.23	62	\$192,00	8 hrs	Mehaničari (2)[200%]											
64	Montaža 756-001/02	0,5 days	Mon 21.8.23	Mon 21.8.23	63	\$192,00	8 hrs	Mehaničari (2)[200%]											
65	Montaža 722-011	0,5 days	Mon 21.8.23	Tue 22.8.23	64	\$192,00	8 hrs	Mehaničari (2)[200%]											
66	Montaža 731-001/01	0,5 days	Tue 22.8.23	Tue 22.8.23	65	\$192,00	8 hrs	Mehaničari (2)[200%]											
67	Montaža 731-001/02	0,5 days	Tue 22.8.23	Wed 23.8.23	66	\$192,00	8 hrs	Mehaničari (2)[200%]											
68	Montaža 731-002	0,5 days	Wed 23.8.23	Wed 23.8.23	67	\$192,00	8 hrs	Mehaničari (2)[200%]											
69	Montaža 731-003/01	0,5 days	Wed 23.8.23	Thu 24.8.23	68	\$192,00	8 hrs	Mehaničari (2)[200%]											
70	Montaža 731-003/01	0,5 days	Thu 24.8.23	Thu 24.8.23	69	\$192,00	8 hrs	Mehaničari (2)[200%]											
71	Montaža 733-001	0,5 days	Thu 24.8.23	Fri 25.8.23	70	\$192,00	8 hrs	Mehaničari (2)[200%]											
72	Montaža 733-012	0,5 days	Fri 25.8.23	Fri 25.8.23	71	\$192,00	8 hrs	Mehaničari (2)[200%]											
73	Montaža 734-001	0,5 days	Fri 25.8.23	Mon 28.8.23	72	\$192,00	8 hrs	Mehaničari (2)[200%]											
74	Montaža 743-002	0,5 days	Mon 28.8.23	Mon 28.8.23	73	\$192,00	8 hrs	Mehaničari (2)[200%]											
75	Montaža 743-003	0,5 days	Mon 28.8.23	Tue 29.8.23	74	\$192,00	8 hrs	Mehaničari (2)[200%]											
76	Montaža 751-001	0,5 days	Tue 29.8.23	Tue 29.8.23	75	\$192,00	8 hrs	Mehaničari (2)[200%]											
77	Montaža 756-004	0,5 days	Tue 29.8.23	Wed 30.8.23	76	\$192,00	8 hrs	Mehaničari (2)[200%]											
78	<b>Cjevarski radovi</b>	<b>27,75 days</b>	<b>Mon 21.8.23</b>	<b>Wed 27.9.23</b>	<b>40FS-7 days</b>	<b>\$39.072,00</b>	<b>888 hrs</b>												
79	Montaža prolaza	5,25 days	Mon 21.8.23	Mon 28.8.23		\$7.392,00	168 hrs	Cjevvari (4)[400%]											
80	Montaža nosača	7,5 days	Mon 28.8.23	Wed 6.9.23	79	\$10.560,00	240 hrs	Cjevvari (4)[400%]											
81	Montaža cijevi	15 days	Thu 7.9.23	Wed 27.9.23	80	\$21.120,00	480 hrs	Cjevvari (4)[400%]											
82	<b>Bravarski radovi</b>	<b>26,5 days</b>	<b>Thu 24.8.23</b>	<b>Fri 29.9.23</b>	<b>78FS-25 days</b>	<b>\$8.480,00</b>	<b>424 hrs</b>												
83	Montaža podnica	10,5 days	Thu 24.8.23	Thu 7.9.23		\$3.360,00	168 hrs	Bravari (2)[200%]											
84	Montaža ljestvi	9 days	Thu 7.9.23	Wed 20.9.23	83	\$2.880,00	144 hrs	Bravari (2)[200%]											
85	Montaža skala	7 days	Wed 20.9.23	Fri 29.9.23	84	\$2.240,00	112 hrs	Bravari (2)[200%]											
86	<b>Električarski radovi</b>	<b>35,25 days</b>	<b>Thu 7.9.23</b>	<b>Thu 26.10.23</b>	<b>80</b>	<b>\$54.144,00</b>	<b>1.128 hrs</b>												
87	Montaža kablskih prolaza	5,25 days	Thu 7.9.23	Thu 14.9.23		\$8.064,00	168 hrs	Električari (4)[400%]											
88	Montaža kablskih staza	11,25 days	Thu 14.9.23	Fri 29.9.23	87	\$17.280,00	360 hrs	Električari (4)[400%]											
89	Provlačenje kabela	18,75 days	Fri 29.9.23	Thu 26.10.23	88	\$28.800,00	600 hrs	Električari (4)[400%]											
90	<b>Limarski radovi</b>	<b>53,5 days</b>	<b>Thu 26.10.23</b>	<b>Tue 9.1.24</b>	<b>78FS+20 days</b>	<b>\$8.160,00</b>	<b>408 hrs</b>												
91	Montaža ventilacijskih prolaza	7 days	Thu 26.10.23	Fri 3.11.23		\$2.240,00	112 hrs	Limari (2)[200%]											
92	Montaža ventilacijskih kanala	15 days	Wed 15.11.23	Tue 5.12.23	91SS+14 days	\$4.800,00	240 hrs	Limari (2)[200%]											
93	Montaža zaštite strojeva I uređaja	3,5 days	Thu 4.1.24	Tue 9.1.24	92FS+21 days	\$1.120,00	56 hrs	Limari (2)[200%]											

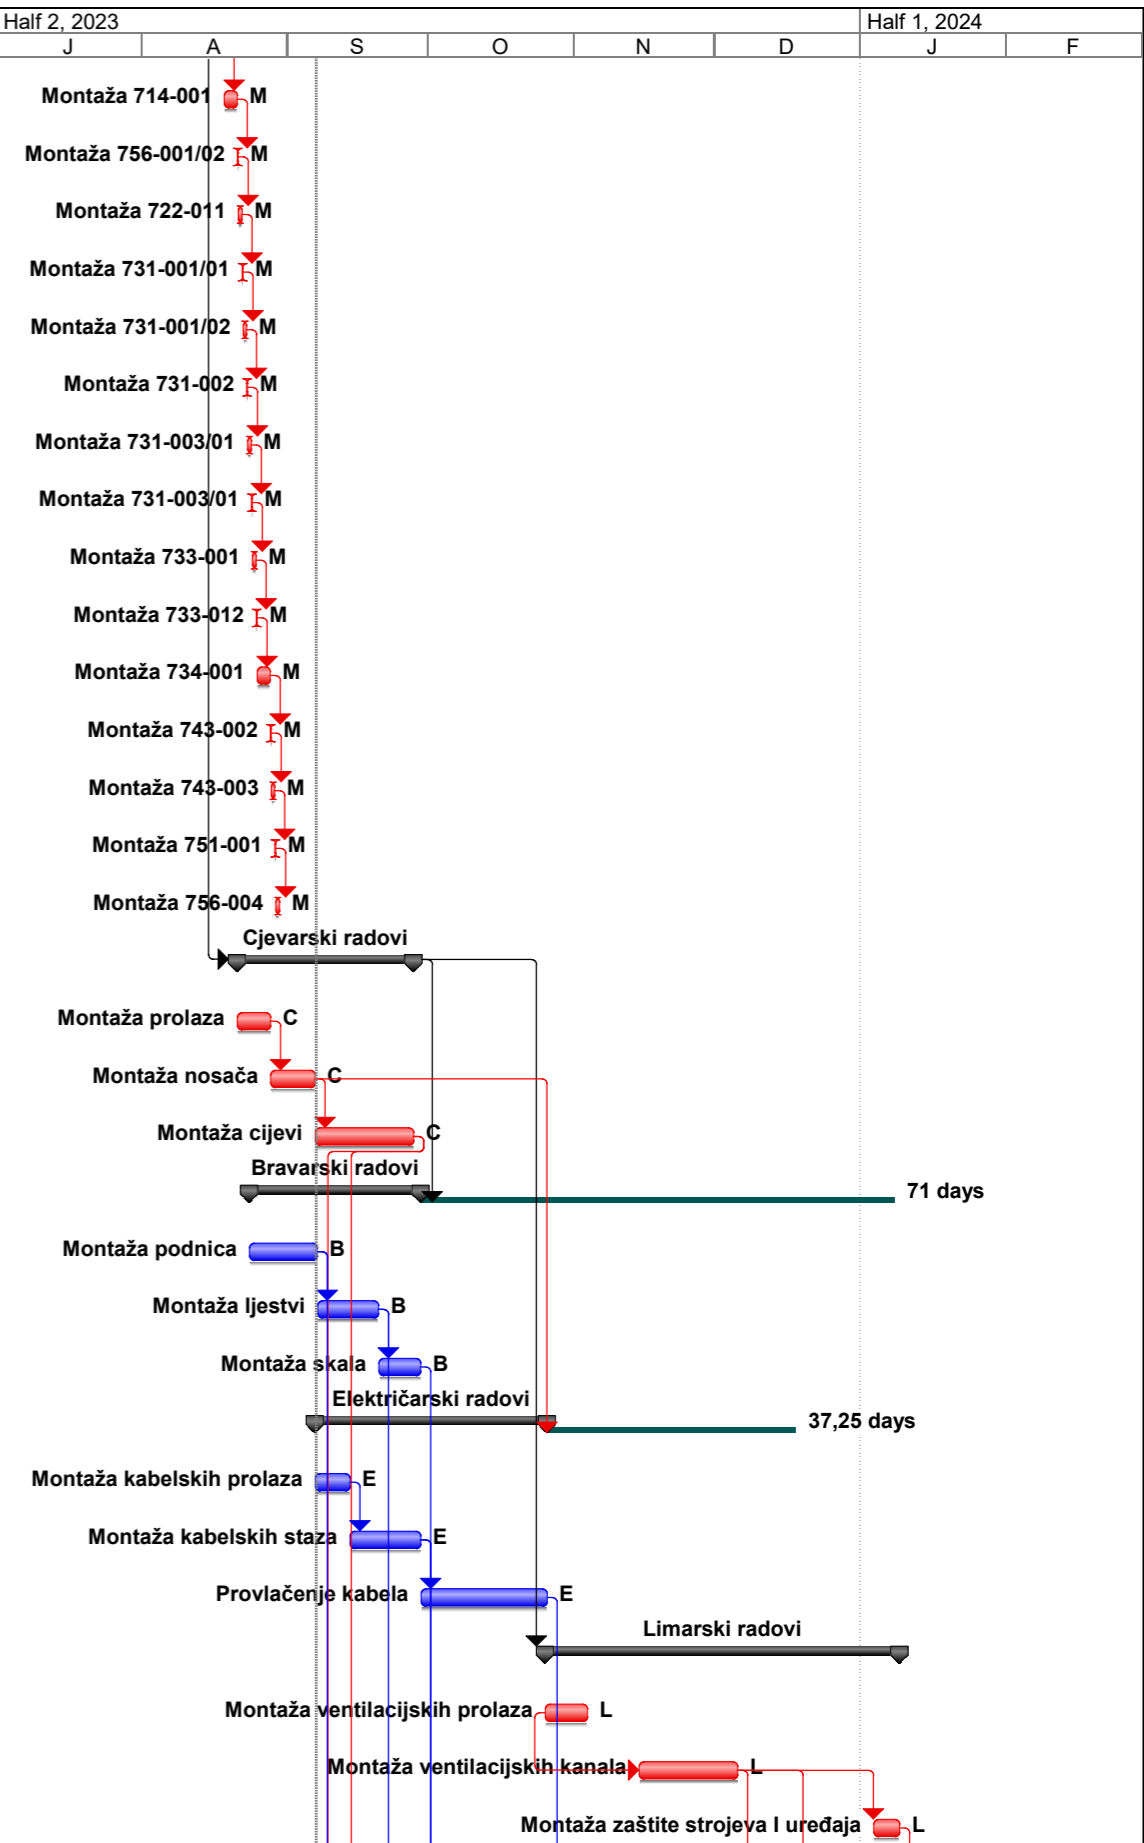

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Cost	Work	Resources	Half 2, 2023							Half 1, 2024				
									M	J	J	A	S	O	N	D	J	F		
94	<b>Izolaterski radovi</b>	<b>10 days</b>	<b>Wed 6.12.23</b>	<b>Tue 19.12.23</b>	<b>92</b>	<b>\$7.200,00</b>	<b>240 hrs</b>													
95	Montaža izolacije	10 days	Wed 6.12.23	Tue 19.12.23		\$7.200,00	240 hrs	Izolateri (3)[300%]												
96	<b>Ispitivanje</b>	<b>89 days</b>	<b>Thu 7.9.23</b>	<b>Wed 10.1.24</b>		<b>\$15.408,00</b>	<b>760 hrs</b>													
97	Ispitivanje rada strojeva I uređaja	3 days	Tue 19.9.23	Thu 21.9.23	81FS-7 days	\$288,00	24 hrs	Ispitivači/Mehaničari (1)												
98	<b>Ispitivanje cjevovoda</b>	<b>16,5 days</b>	<b>Thu 14.9.23</b>	<b>Fri 6.10.23</b>		<b>\$5.808,00</b>	<b>264 hrs</b>													
99	Pregled strukture cjevovoda	7 days	Thu 14.9.23	Fri 22.9.23	81FS-10 days	\$2.464,00	112 hrs	Ispitivači/cjevvari (2)[200%]												
100	Tlačenje cjevovoda	6 days	Mon 25.9.23	Mon 2.10.23	99	\$2.112,00	96 hrs	Ispitivači/cjevvari (2)[200%]												
101	Pregled funkcionalnosti	3,5 days	Tue 3.10.23	Fri 6.10.23	100	\$1.232,00	56 hrs	Ispitivači/cjevvari (2)[200%]												
102	<b>Pregled bravarskih radova</b>	<b>18 days</b>	<b>Thu 7.9.23</b>	<b>Tue 3.10.23</b>		<b>\$640,00</b>	<b>64 hrs</b>													
103	Pregled strukture podnica	4 days	Thu 7.9.23	Wed 13.9.23	83	\$320,00	32 hrs	Kontrolori/Bravari (1)												
104	Pregled strukture ljestvi	2 days	Wed 20.9.23	Fri 22.9.23	84	\$160,00	16 hrs	Kontrolori/Bravari (1)												
105	Pregled strukture skala	2 days	Fri 29.9.23	Tue 3.10.23	85	\$160,00	16 hrs	Kontrolori/Bravari (1)												
106	<b>Ispitivanje električarskih radova</b>	<b>35,75 days</b>	<b>Fri 29.9.23</b>	<b>Mon 20.11.23</b>		<b>\$7.872,00</b>	<b>328 hrs</b>													
107	Pregled strukture kablskih staza	3,5 days	Fri 29.9.23	Wed 4.10.23	88	\$1.344,00	56 hrs	Ispitivači/Električari (2)[200%]												
108	Pregled montaže kabela	5 days	Thu 26.10.23	Thu 2.11.23	89	\$1.920,00	80 hrs	Ispitivači/Električari (2)[200%]												
109	Ispitivanje ožičenja kabela	7 days	Thu 2.11.23	Mon 13.11.23	108	\$2.688,00	112 hrs	Ispitivači/Električari (2)[200%]												
110	Test ispitivanja pod naponom	5 days	Mon 13.11.23	Mon 20.11.23	109	\$1.920,00	80 hrs	Ispitivači/Električari (2)[200%]												
111	<b>Ispitivanje limarskih radova</b>	<b>25,5 days</b>	<b>Wed 6.12.23</b>	<b>Wed 10.1.24</b>		<b>\$560,00</b>	<b>56 hrs</b>													
112	Pregled strukture ventilacije	2 days	Wed 6.12.23	Thu 7.12.23	92	\$160,00	16 hrs	Kontrolori/Limari (1)												
113	Pregled funkcionalnosti	4 days	Fri 8.12.23	Wed 13.12.23	112	\$320,00	32 hrs	Kontrolori/Limari (1)												
114	Pregled strukture zaštite strojeva	1 day	Tue 9.1.24	Wed 10.1.24	93	\$80,00	8 hrs	Kontrolori/Limari (1)												
115	<b>Ispitivanje izolaterskih radova</b>	<b>3 days</b>	<b>Wed 20.12.23</b>	<b>Fri 22.12.23</b>		<b>\$240,00</b>	<b>24 hrs</b>													
116	Pregled montaže izolacije	3 days	Wed 20.12.23	Fri 22.12.23	95	\$240,00	24 hrs	Kontrolori/Izolateri (1)												

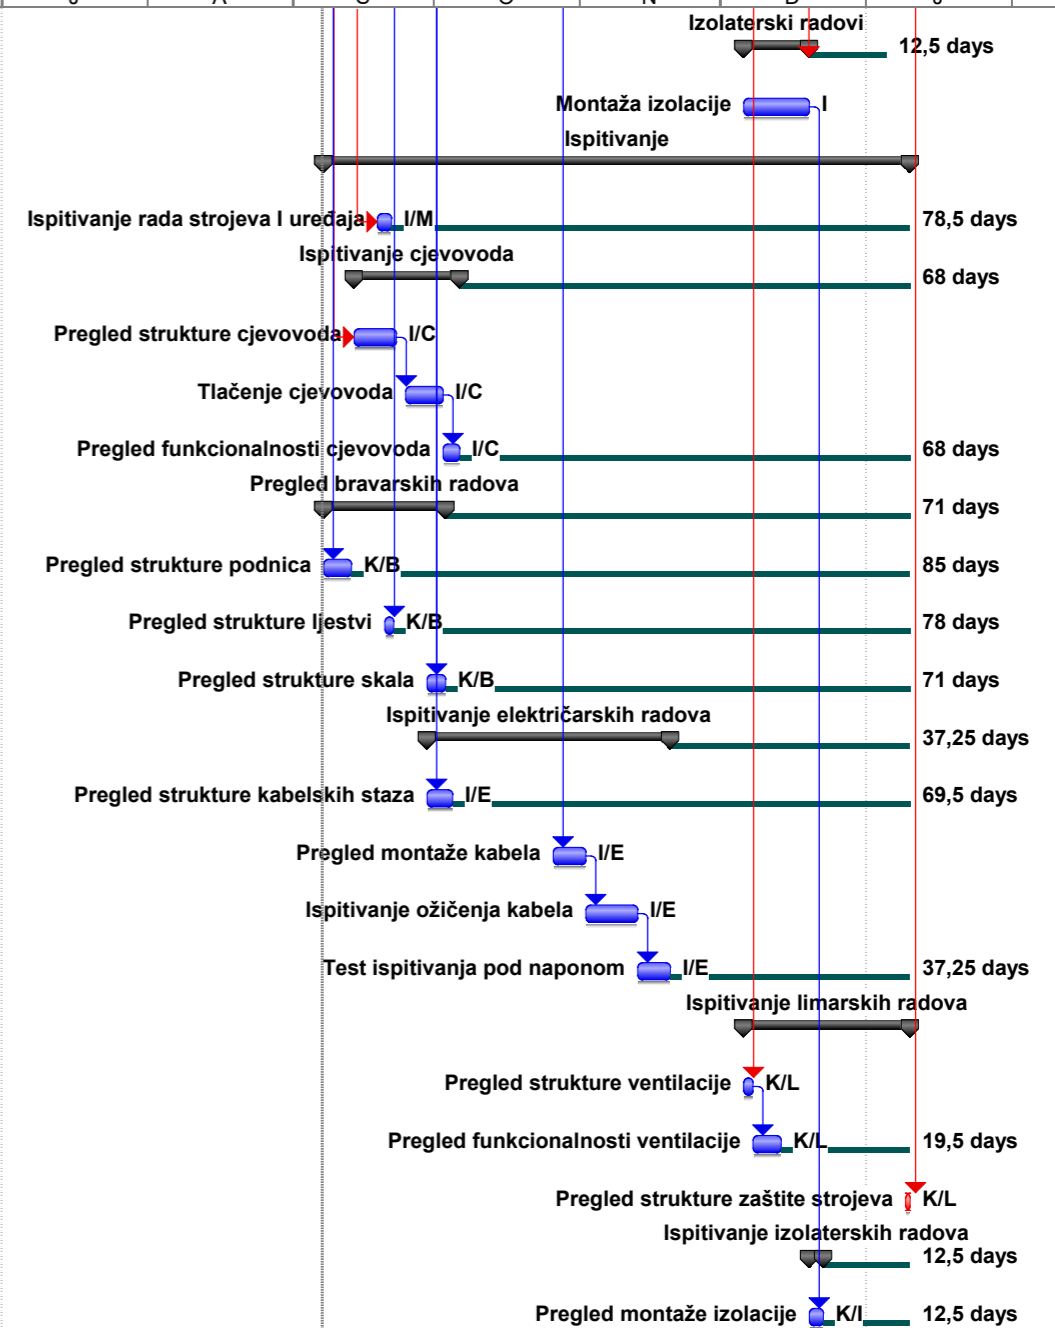

Project: OPREMANJE 2 PLATFORME  
Date: Thu 7.9.23

Critical		Split		Slack		Project Summary		External Tasks	
Critical Split		Progress		Slippage		Rolled Up Critical		External Milestone	
Task		Milestone		Summary		Rolled Up Critical		Deadline	
